



2016 District 1 Highway Construction Program

For additional information contact:

Beth Petrowske

MnDOT District 1 Public Affairs

Office: 218-725-2708

Email: beth.petrowske@state.mn.us

Last updated November 18, 2016

Map #	Carryover projects General project information	Letting and tentative construction dates	Project engineer / supervisor	Work description / traffic impacts
1	SP 0901-67 Hwy 23 (Carlton County) 17 miles NE of the south Carlton County line Contractor: Northland Constructors Original bid — \$3,159,914	COMPLETED Let: 11/21/14 Construction: June 1, 2015 – Nov 11, 2016	Andrew Deming	Construct a new bridge and approaches (0.587 miles reconstruction) Temporary-lane closures, flaggers
2	SP 6910-89 Hwy 23 (St. Louis County) In Duluth from I-35 to 84 th Ave W Contractor: Northland Constructors of Duluth LLC Original bid — \$10,385,411 Remaining work \$2.5 million	COMPLETED Let: 4/24/15 Construction: May 2016 – June 18, 2016	Jim Sorenson	In 2015, I-35 to 84th Ave W, (1.7 miles) will be reconstructed Included in the project; a new bridge at Kingsbury Creek, traffic signals, ADA and pedestrian crossing upgrades, new curb and gutter, sidewalks and drainage improvements Single lane traffic in each direction, temporary lane closures, flaggers
3	SP 6916-104 Hwy 53 (St. Louis County) In Duluth from Haines Road to Midway Road Contractor: Hardrives Inc. Original bid — \$4,184,091	COMPLETED Let: 7/24/15 Construction: May to June 17, 2016	Jim Sorenson	ADA improvements, signal revisions Temporary lane closures, flaggers

4	SP 6918–69129A Hwy 53 (St. Louis County) Between Eveleth and Virginia Contractor: Kiewit Original bid — \$17.1 million	Let: 5/8/15-Wk Work Pkg 1 Construction: Fall 2015 to Fall 2017	Pat Huston	Early steel package, procurement of bridge beams No traffic delays
5	SP 6918–86 Hwy 53 (St. Louis County) Between Eveleth and Virginia Contractor: Kiewit Original bid — \$138,891,655	Let:10/21/15 Work Pkgs 2+3 Construction: Fall 2015 to Fall 2017	Pat Huston	New Hwy 53 alignment, bridge, approaches and interchange at Hwy 135 (3.2 miles pavement)
6	SP 0916–29 Hwy 210 (Carlton County) CR 151 (Jay Cooke Rd) to Hwy 23 in Jay Cooke State Park Contractor: Veit Original bid — \$21,300,000	Let: 3/18/15 Construction: Late-May 2015 – late-Oct 2017	Aaron Gunderson	Resurface, drainage improvements, slope flattening The damaged section of Hwy 210 has been closed since 2012 and will remain closed until the project is finished.

Number of carryover projects: 6

Value: \$195,021,071

Map #	New Projects General project information	Letting and tentative construction dates	Project engineer / supervisor	Work description / traffic impacts
7	SP 6904–52 Hwy 169 (St. Louis County) From just W of the Six Mile Lake Rd to just E of Bradach Rd in the Eagles Nest Lake area Contractor: Wagner Construction Original bid — \$218,885	COMPLETE Let: 12/18/15 Construction: Feb to April 1, 2016	Rob Ronning	Tree clearing
8	SP 6904-46 Hwy 169 (St. Louis County) From just W of Six Mile Lake Rd to just E of Bradach Rd, Eagles Nest Lake area Contractor: Hoffman Const Co. Original bid — \$16,376,833	Let: 11/18/16 Construction: Winter 2017 – summer 2018	Rob Ronning	Reconstruct 5.8 miles of Hwy 1, straighten alignment and flatten hills (two lane highway) Lane closures and flagging

9	SP 6907-48 Hwy 2 Saginaw Weigh Station (St. Louis County) Contractor: Original bid — \$117,170	COMPLETE Let: 2/12/16 Construction: July 5 – late-July	Brett Weybright	Install variable message sign, public address system, scoreboards, over-height detectors Temporary, intermittent, lane closures
10	SP 6910-96 Hwy 23 (St. Louis County) In Duluth from Becks Rd to I-35 Contractor: Northland Constructors of Duluth LLC Original bid — \$12,284,695	Let: 4/22/16 Construction: June 1 – Late-Nov., 2016 Work will resume in spring and be completed about June 17	Jim Sorenson	In 2016/2017, 84th Ave W to Becks Rd, (3.29 miles) will be reconstructed. Total 3.6 miles. Also included in the projects; a new bridge will be built at Knowlton Creek, traffic signals, ADA and pedestrian crossing upgrades, new curb and gutter, sidewalks and drainage improvements Single lane traffic in each direction, temporary lane closures, <i>flaggers</i>
11	SP 6910-98 Hwy 23 (St. Louis County) At the St Louis River (WI border) Contractor: Original bid — \$3,052,470	Let: 12/18/15 Construction: May 2 – Oct. 28, 2016 Work will resume in spring 2017 and will be finished in late-May	Jim Sorenson	Resurface bridge deck, replace expansion joints (0.1 miles) Single-lane traffic controlled by signals or flaggers
12	SP 5809-15 Hwy 23 (Pine County) One mile E of I-35 over the Kettle River Contractor: Lunda Construction Co Original bid — \$560,850	COMPLETE Let: 4/22/16 Construction: July 11 – Aug 19, 2016	Andrew Deming	Bridge resurfacing (0.159 miles of resurfacing) Detour
13	SP 0906-48 Hwy 33 (Carlton County) NB and SB from the N end of the St. Louis River / Railroad St to just N of Stark Rd in Cloquet Contractor: Hardrives Inc Original bid — \$1,377,981	COMPLETE Let: 4/22/16 Construction: July 11 – Aug 26, 2016	Jim Sorenson	Resurface 2 miles of pavement, signals ADA improvements Lane restrictions, minor impact

14	SP 5880–191 I-35 (Pine County) From 1 mile S of CR 11 to 1.8 mile N of Hwy 23 (Pine City to Hinckley) Contractor: Knife River Corp. Original bid — \$27,034,314	COMPLETED Let: 1/29/16 Construction: April 11 – Nov.11, 2016	Andrew Deming	Resurface pavement (UBO), replace bridge (2 miles S of Hwy 48 over the St. Croix Valley RR) approach panels and guard rail (11.798 miles of resurfacing, NB and SB) Open to four lanes, Friday, Nov. 4 at 1 p.m. throughout the weekend, then lane closures next week until the project is finished.
15	SP 6982–317 I-35, Hwy 61, Hwy 194 (St. Louis, Lake Counties) NB and SB from Lake Ave to Hwy 61/London Rd, Hwy 61 NB from Homestead Rd to 450 feet N of the Knife River; and on Hwy 194 between E Skyline Pkwy and W 3rd St in Duluth Attached to projects 21 and 24 Contractor: PCI Roads, LLC Original bid — \$3,029,324	COMPLETED Let: 3/18/16 Construction: May 9 – Sept. 5, 2016	Brett Weybright	2.4 miles of concrete pavement repairs, drainage repairs and bituminous overlay Lane restrictions on I-35 and periods of ramp closures. Ramp closures will require detours
16	SP 3109–40M Hwy 46 (Itasca County) 3 miles S of CR 13 at the Popple River Contractor: Gladen Construction Original bid — \$757,197	COMPLETED Let: 3/18/16 Construction: July – Aug 2016	Darren Laesch D2 project, D1 funding	Resurface 0.1 mile of pavement, new box culvert 30-mile detour http://www.dot.state.mn.us/d2/
17	SP 6918–81 Hwy 53 (St. Louis County) From Hwy 37 to just S of Vermilion Dr in Eveleth and Virginia Contractor: Ulland Brothers Inc. Original bid — \$1,377,801	COMPLETED Let: 11/20/2015 Construction: May 9 – July 15, 2016	Rob Ronning	Resurface 2.2 miles of pavement, drainage repairs, ADA improvements, lighting, signals, RICWS 2.2 miles resurfaced both NB and SB (4 lane highway) total = 4.4 miles Temporary lane closures, flaggers
18	SP 6917-141 Hwy 53 (St. Louis County) SB Hwy 53, from just S of the White Face River to Augusta Lake Rd Contractor: KGM Contractors Inc Original bid — \$2,176,621	COMPLETED Let: 12/18/15 Construction: May 9 – June 23, 2016	Rob Ronning	Resurface 8.1 miles pavement (southbound only) (2 lanes SB) Lane closures and traffic reduced to a single lane

19	SP 6916-105 Hwy 53 (St. Louis County) Hwy 53 at CR 91 (Haines Rd) in Duluth Contractor: Chippewa Concrete Services Inc. Original bid — \$624,008	COMPLETED Let: 3/18/16 Construction: Aug 8 – Nov. 4, 2016	Brett Weybright	Traffic signal revisions, ADA improvements Traffic restricted to single lane
20	SP 6917-142 Hwy 53 (St. Louis County) 0.35 miles S of CR 93 to Hwy 37 Contractor: Northland Constructors of Duluth LLC Original bid — \$3,650,513	COMPLETED Let: 7/22/16 Construction: Sept 7 – late-Oct, 2016	Rob Ronning	Resurfacing project, 12.42 miles Lane closures
21	SP 1603-48 Hwy 61 (Cook County) 4 miles NE of the Gunflint Trail Contractor: Northland Constructors of Duluth LLC Original bid — \$2,495,379	COMPLETED Let: 1/29/16 Construction: May 31 – Mid-Nov, 2016	Brett Weybright	Replace bridge over the Devil Track River, approach work, paving (0.1 mile with bridge) Lane restrictions controlled by a temporary signal system
22	SP 6926-52 Hwy 61 (St. Louis County) NB lanes from the Homestead Rd to the S end of the Knife River Bridge Contractor: PCI Roads, LLC \$150,000 Sub of 6982-317	COMPLETED Let: 3/18/16 Construction: Mid-June – Sept 5, 2016	Brett Weybright	2.9 miles concrete pavement and drainage repairs Lane restrictions
23	SP 3806-70 Hwy 61 (Lake County) South of Beaver Bay Contractor: Northland Constructors of Duluth LLC Original bid — \$3,456,410	Let: 10/28/16 Construction: Summer 2017 NO WORK IN 2016	Derek Fredrickson	Rehabilitate Beaver River Bridge and approaches (0.2 miles) Lane restrictions
24	SP 3116-142 Hwy 169 (Itasca County) From 0.66 miles SW of CR 15 to just E of Scenic CR 7 Contractor: KGM Contractors Inc Original bid — \$5,887,833	Let: 6/3/16 Construction: September 12 2016 – Fall 2017	Jeff Tillman	Two to four-lane expansion, new box culvert 1.6 miles both NB and SB (4 lane highway) = 3.2 miles Most work will be off-road, some flagging

25	SP 6933-92 Hwy 194 (St. Louis County) N Mesaba Ave to I-35 in Duluth Contractor: PCI Roads, LLC \$150,000 Sub of 6982-317	COMPLETED Let: 3/18/16 Construction: May 9 – July 15, 2016	Brett Weybright	Drainage repairs (0.9 miles, drainage repairs only with no roadway surfacing) Lane restrictions
26	SP 6933-94 Hwy 194 (St. Louis County) From 8th St to 9th St in Duluth Contractor: Tony J. Lastovich dba/Tony's Construction Original bid – \$72,464	COMPLETED Let: 3/18/16 Construction: Summer 2016	Jim Sorenson	Retaining wall and building removal (wall tipping, buying and demolishing nearby building) No traffic impacts expected, sidewalk closures can be anticipated
27	SP 3614-20 Hwy 217 (Koochiching County) From Front St in Littlefork to Hwy 53 Contractor: Mark Sand & Gravel Original bid – \$4,805,864	COMPLETED Let: 1/29/16 Construction: June – Oct 17, 2016	Jeff Tillman	Resurface 16.6 miles of pavement, improve lighting, repair bridge at the Rat Root River Long detour until Sept 2
28	SP 6980-59 I-535 (St. Louis County) Blatnik Bridge to I-35 in Duluth Contractor: PCI Roads. LLC Original bid – \$1,938,637	COMPLETED Let: 6/24/16 Construction: Aug 22-Oct 7 2016	Jim Sorenson	1 mile concrete pavement and structural, drainage repairs Three lanes on the Blatnik Bridge will close, one direction of traffic will detour to the Hwy 2 Bong Bridge, periods of ramp closures
29	SP 8821-253 Hwy 61, 135, 37, 73, 169, 53 (St. Louis, Lake, Cook Counties) Grand Marais to Grand Portage Contractor: Northland Constructors of Duluth LLC Original bid – \$4,142,300	COMPLETED Let: 7/24/15 Construction: May 9 – mid-Oct., 2016	Brett Weybright	Maintain, improve drainage systems, (Exact locations won't be determined until spring) Lane closures controlled by signals or flaggers
30	SP 8821-268 Districtwide in Aitkin, Cook, Itasca, St. Louis Counties Contractor: Parsons Electric LLC Original bid – \$170,825	Let: 3/18/16 Construction: Sept 19 – Sept 30, 2016 Work will resume March 2017 and be finished by March 31	Robert Ronning	Rural lighting Shoulder closures and possibly some short-term lane closures/flagging

31	SP 8821-267 Districtwide in Pine, Kanabec Counties Contractor: Safety Signs, LLC Original bid — \$199,910	Let: 3/18/16 Construction: Oct 3, 2016 – Fall 2016	Andrew Deming	Signing project on Hwys 48,70 and 123 Intermittent lane closures
32	SP 8821-273 Districtwide Contractor: Century Fence Inc. Original bid — \$657,248	COMPLETED Let: 1/29/16 Construction: June 6 – June 26, 2016	Andrew Deming	Sinusoidal centerline rumble strips Intermittent lane closures

Number of new projects: 26


Value of new 2016 highway projects: \$96,465,532

Total value of highway projects in Northeastern Minnesota: \$291,486,603

Please note: The “estimated cost” and “original bid” amounts do not include the cost of right of way acquisition or preliminary engineering work.

2016 Highway Construction

District 1 – Duluth

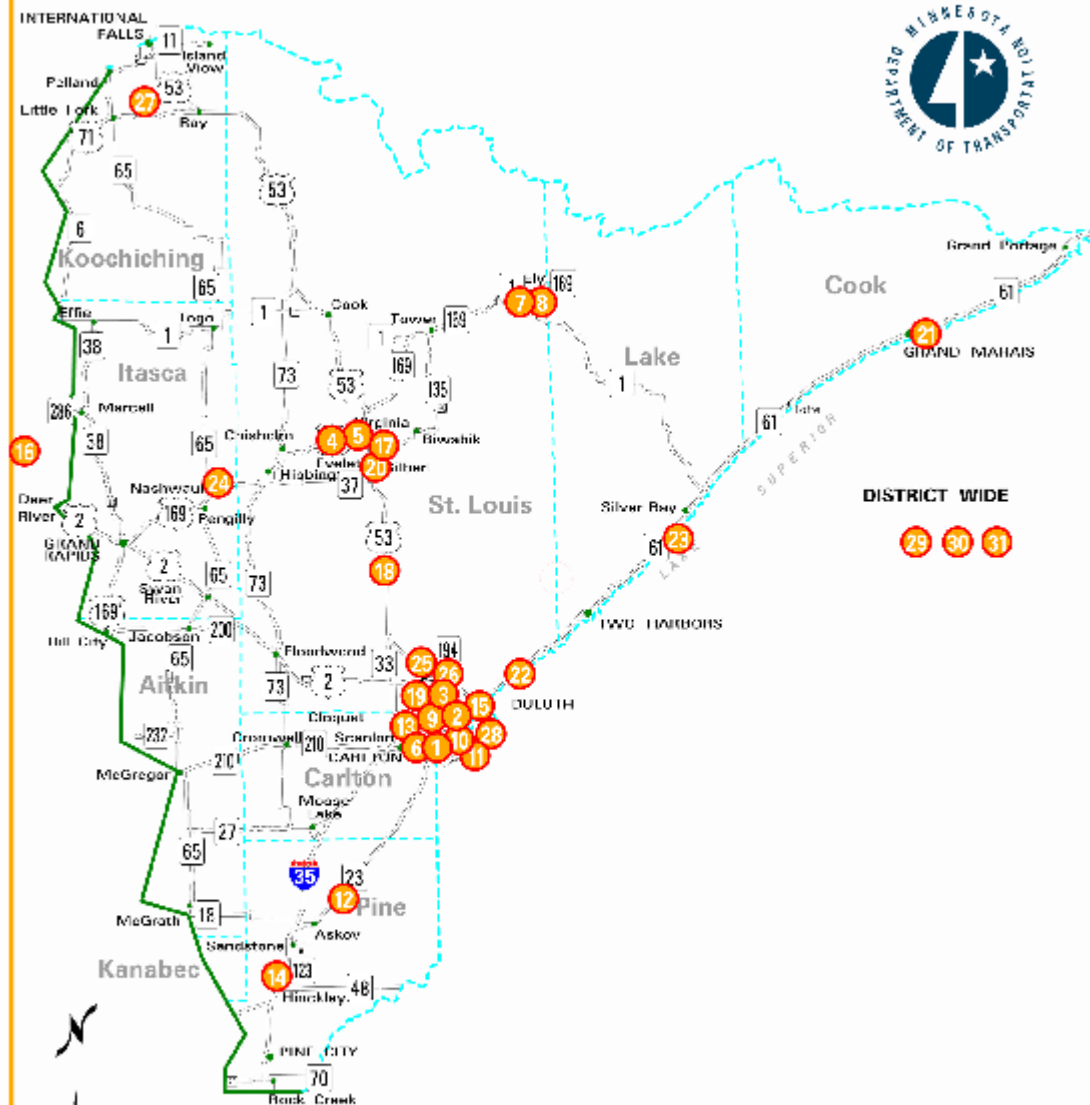

20 0 20 40 Miles
