


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2734
TRUNK HIGHWAY 100
COUNTY Hennepin
DISTRICT 5A

LIMITS: S.Jct.T.H.169 in Edina - N.Jct.T.H.169 in St. Louis Park



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
1926	100-5-31-3	Grading	60'		
1927	100-5-31-3	Grading Br. 4612 & 4598	60' 40'		
1928	100-5-31-3	Concrete	40'		
1938	2735-02	Grading Gravel	60' 60'	12"	
1938	A.F.E. 24	Mixed Bitum.	60'	2"	
M	1946	A.F.E. 4	Bit. Surf. Repair	60'	
C	1949	2734-02	Traffic Signals		
C	1950	2734-03	Traffic Signals		
C	1952	2734-04	Aphaltic Conc.	40'	3"
M	1952	A.F.E. 4	Spot Bit. Patching	37'	
M	1954	A.F.E. 627	Bit. Seal Coat	40'	
C	1964	By Maint. Div.	Deceleration Lanes		
C	1965	C	Spot Bit. Shoulders Plant Mix Bit.	Var. 40'	
C	1970	2734-15	Br. 27106 Br. 27105		

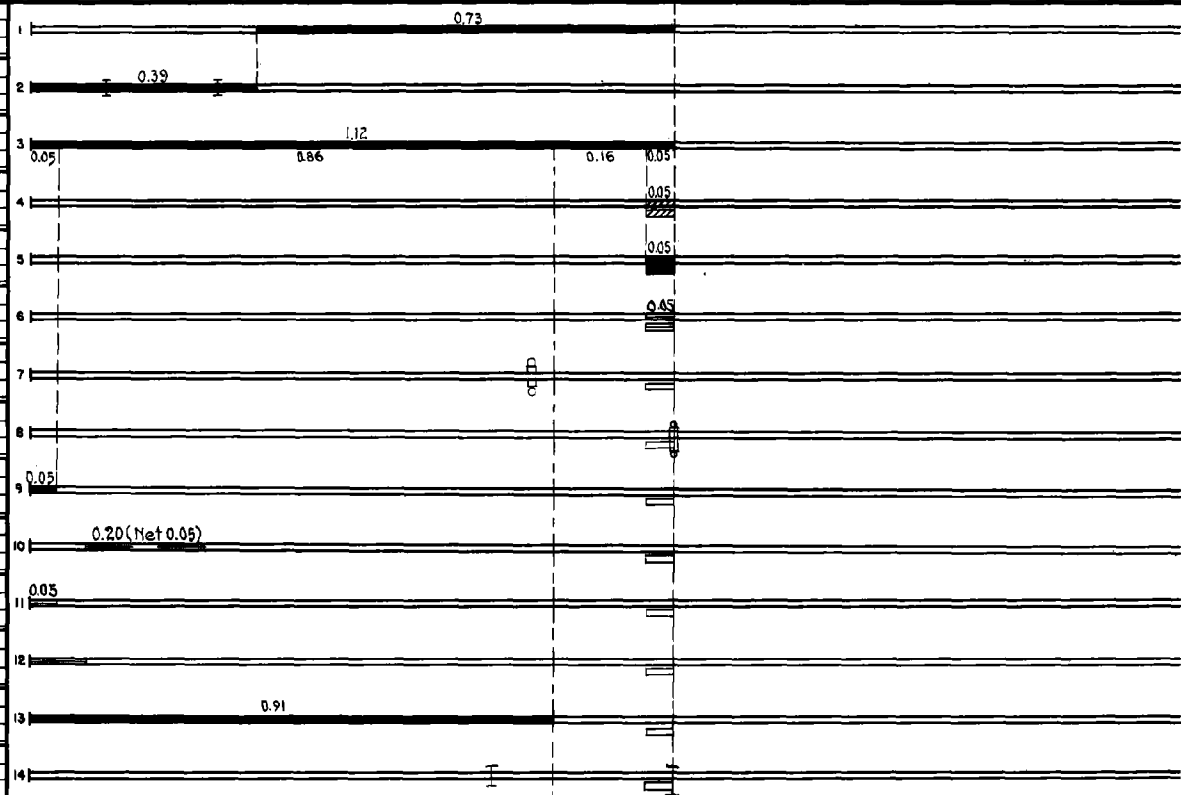

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1927	1972	1.12	0.00	0.00	1.09	0.03	0.00	0.00	1.09	0.03
1973		1.24			1.21	0.03			1.21	0.03

REMARKS: Layout is to scale as of 1927
(1) Contract not final but work substantially complete.

11-95

