


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2805  
TRUNK HIGHWAY 61  
COUNTY Houston  
DISTRICT 6A

LIMITS: N. Co. Line - Y. End of Bridge (Miss. River)



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
		Earth	24'		No Record of Constr.
1921	61-3-14	Grading	24'		
1922	61-3-30	Gravel	24'	2 1/2"	1100 C.Y./Mi.
1925	61-3-38-1	Grading Concrete	V.M. 18'22"	7"	
1927	61-3-38-2	Grading Concrete	32' 18'	9 7/8"	
1932	61-3-38-1A	Grading Concrete	20'	8-8-8"	
C	2805-06	Br. 5475	222'		Not used until 1941. 252' B.S.-O.H. On new line.
C	2805-11	Grading Cully Ext. Stab. Sand Base Bit. Surf. Treat.	42' 42' 22'	2" 3/4"	W 84 D.
C	2805-11	Grading	238'		Divided Highway.
1941	2805-05	Stab. Sand Base	238'	2"	
	2805-02	Bit. Surf. Treat.	222'	3/4"	
C	2805-03	Grading	V.M.		Divided Highway.
1941	2805-04	Stab. Sand Base Bit. Surf. Treat.	222' 222'	2" 3/4"	
C	2805-04	Widening	V.M.		New Roadway.
1941	2805-04	Grad. Stab. Gr. Base Bit. Surf. Treat.	22' 22'	2" 3/4"	Divided Highway. (1)
C	2805-04	Grading	V.M.		Divided Highway.
1941	2805-04	Stab. Sand Base Bit. Surf. Treat.	222' 222'	2" 3/4"	
M	1942 A.F.E.4	Bit. Retreat			Tar 135 1/2 Gal./Mi. Agg 160 C.Y./Mi. Maint. Dept.
C	1942 2805-29	Misc. Const.			Drainage Struct's

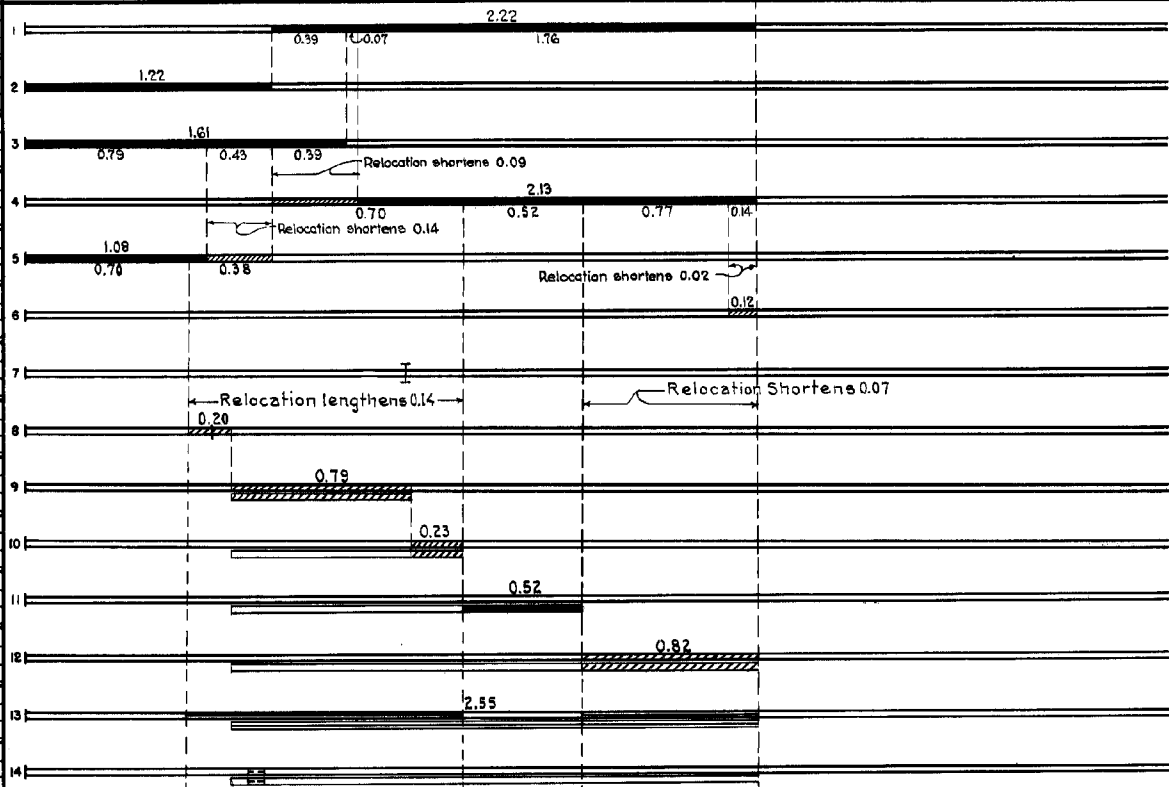

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED			INCORPORATED			RURAL				URBAN			
			ROWY. MI.	BR. MI.		ROWY. MI.	BR. MI.		ROWY. MI.	BR. MI.		ROWY. MI.	BR. MI.			
1921	1924	3.44	1.09	0.00		2.35	0.00		3.44	0.00	0.00	0.00				
1925	1926	3.35	1.09	0.00		2.26	0.00		3.35	0.00	0.00	0.00				
1927	1931	3.21	1.09	0.00		2.12	0.00		3.21	0.00	0.00	0.00				
1932	1940	3.19	1.07	0.00		2.12	0.00		3.19	0.00	0.00	0.00				
1941	1950	3.26	1.14	0.00		2.07	0.05		3.21	0.05	0.00	0.00				
1951	1963	3.26	1.14	0.00		2.07	0.05		1.14	0.00	2.07	0.05				
1964		3.25	1.14	0.00		2.06	0.05		1.14	0.00	2.06	0.05				

REMARKS: Layout is to scale as of 1932. Plan revised for 1941 relocation.


(1) Old concrete left in place and new roadway with bit. surf. built parallel to old roadway with raised island between.

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2805  
TRUNK HIGHWAY 61  
COUNTY Houston  
DISTRICT 6A

LIMITS: N.Co. Line - W. End of Bridge (Miss. River)



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>	MILES
		TYPE	WIDTH	THICK-NESS		
1943	A.F.E. 4	Bit. Surf. Repair	30'4"		RT-586, 15466 Gal./Mi. Agg. 770 C.Y./Mi. Maint. Dept.	2.55
1944	A.F.E. 5	Bit. Seal Coat	22'		RC3, 5789 Gal./Mi. Agg. 203 C.Y./Mi. Main. Div.	2.55
1945	A.F.E. 30	Install Manhole & Culvert			In La Crescent Maint. Div.	
1946	A.F.E. 17	Bit. Resurfacing Mixed Bit.	22'4"	1" Added	MC3, 71879 Gal. Agg. 2634 C.Y.	2.56
1947	A.F.E. 44	Spot Repair & Bit. Surfacing Mixed Bit.	22'	1"	MC-3, 1343 Agg. 428 C.Y. On old Conc. base	0.52
1948	A.F.E. 29	Bit. Resurfacing Mixed Bit.	22'4"	1" added	MC3, 42303 Gal. Agg. 3511 Tons	2.56
1970	A.F.E. 4 A.F.E. 38	Spot Treat. Bit. Surface Repair Replace Culvert			MC-3, 1910 Gal. Agg. 100 C.Y.	2.56 (Net 0.20)
1951	A.F.E. 4	Spot Treat. Bit. Surf. Repair			MC3, 2513 Gal. Agg. 40 C.Y.	2.56 (Net 0.34)
1952	2805-35	Concrete	44'	9'7"	2 Row's @ 22'	2.19
1953	2805-39 2805-41 2805-40	Roadside Develop. Traffic Signals Rip Rep			A.F.E. 866 Install & Catch basins	
1953	A.F.E. 605	Light Bit Seal			RC5-2, 1055 Gal. Agg. 45 C.Y.	0.37
1954	A.F.E. 822	Guard Rail			17482 ft.	
1956	A.F.E. 821 A.F.E. 605	Spot Bit. Surf. Re- pair on Service Drive Light Bit Seal (0.37 Mi)	20'		MC245C3, 3576 Gal. Agg. 208 Tons @ 24 C.Y.	0.37 (Repair)
1959	A.F.E. 866	Erosion Control				

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet No 1  
(1) Bit Surface placed over old concrete on North Bound Rdway and 0.20 mi. of spot repairs on other areas.

