


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2904
TRUNK HIGHWAY 71
COUNTY Hubbard
DISTRICT 2A

LIMITS: S. Co. Line - Jct. T.H. 34 in Park Rapids



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o DIST
		TYPE	WIDTH	THICKNESS	
		Earth	24'		No Record of Constr. 16 E.S.
1925	Br. 6230 71-4-29-3C	WI 108 D Grading Clay	24'	2.7"	
1926	71-4-29-3C	Gravel	24'	3 1/2"	1600 C.Y./Mile.
1930	71-4-30	Grading Br. 8336	32'		WI 1010 D.
1931	(1) 71-4-29-3C	Oil Tr. Gravel	30'	1"	Maint. Dept.
1931	(1) 71-4-30	Tar Tr. Gravel	30'	1"	16000 Gal./Mile. Maint. Dept.
1932	(1) 71-4-30	Tar Tr. Gravel	28 1/2'	1 1/2"	6936 Gal./Mile. Maint. Dept.
1934	71-4-29-3C	Bit.	20'	1 1/2"	16357 Gal./Mile.
M	1942 A.F.E. 4	Bit. Retreat	28'		RT-5 7137 Gal./Mi. Grav. 361 C.Y. Maint. Dept.
C	1947 A.F.E. 17	Bit. Resurfacing Mixed Bit.	24'	1 1/4" added	MC-3 87683 Gal. Agg. 6090 C.Y.
M	1950 A.F.E. 4	Bit. Fog Seal	24'		RCS-1, 10958 Gal. Agg. 294 C.Y.
C	1951 2904-02	Traffic Signals			951
C	(B) 1953 2904-04	Grading Bit. Stab. Base Plant Mix Bit.	5468'	6"	6" Select Mat'l. 4-53
M	1954 A.F.E. 604	Light Bit Seal	24'		RCS-1, 14516 Gal. Agg. 570 C.Y.

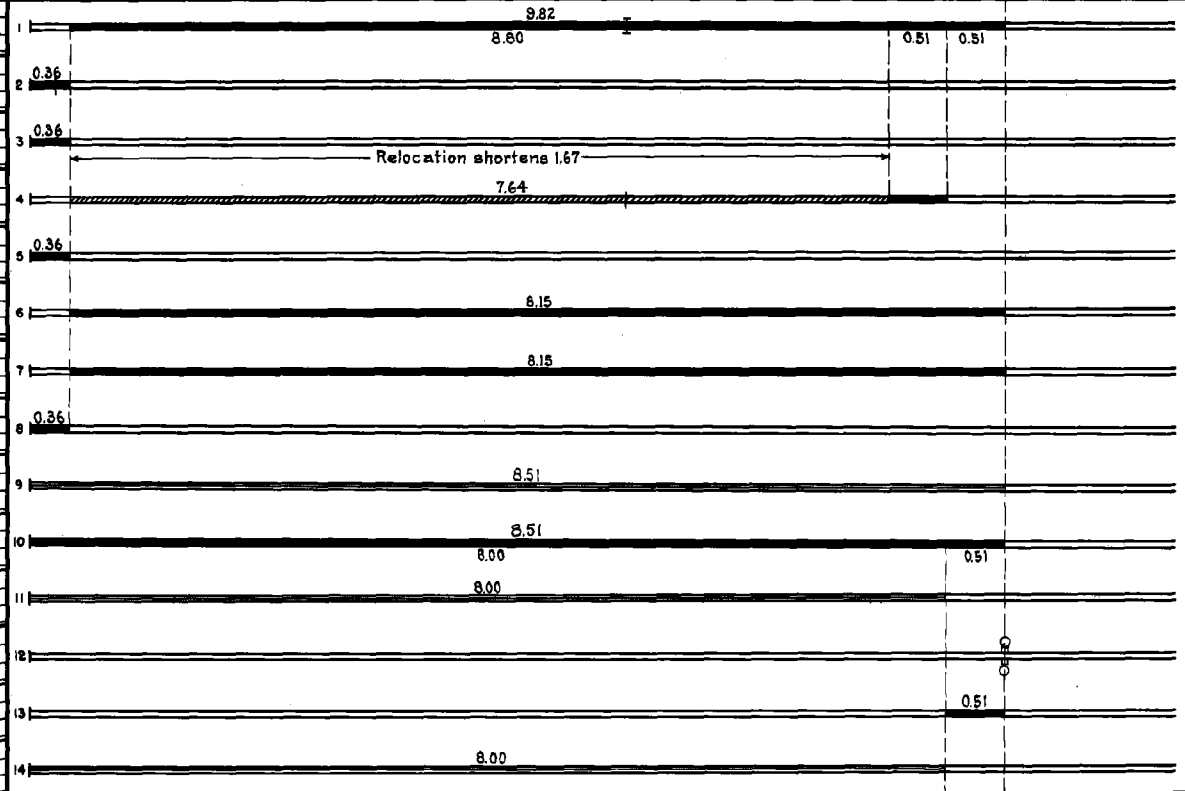

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1925	1929	10.18	9.16	0.00	1.02	0.00	9.16	0.00	1.02	0.00
1930	1959	8.51	7.49	0.00	1.02	0.00	7.49	0.00	1.02	0.00
1950		8.52	7.49	0.00	1.03	0.00	7.49	0.00	1.03	0.00

REMARKS: Layout is to scale as of 1930
 (1) This work not done under these project numbers but lies within the limits of these projects
 (2) Accumulated thickness (3) Contract not final but work substantially complete

