


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4809  
TRUNK HIGHWAY 95  
COUNTY Mille Lacs  
DISTRICT 38

LIMITS: W. Co. Line - S. Jct. T.H. 169 in Princeton



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°						
		TYPE	WIDTH	THICKNESS							
		Gravel	22'	1 1/2"	No Record of Constr. Added in 1934. Hood Span.	1	9.80				
		Br. X-267	15'								0.39
1934		Br. 3804	23'		18' Timber Span. Maint. Dept.	2					
1939	A.F.E. 51	Grading	30'		Maint. Dept.	3				5.70	
C	1940 A.F.E. 55	Grading	30'		Maint. Dept.	4				3.22	
C	1940 A.F.E. 55	Mixed Bitum.	26'	1 1/4"	Maint. Dept.	5				6.09	
M	1942 A.F.E. 5	Bit. Seal Coat	24'		RT-10, 22,64 Gal./Mi. Grav. 88 C.Y./Mi. Maint. Dept.	6				6.09	
M	1943 A.F.E. 4	Spot Treat. Bit. Surf. Repair	26'		MC-2&RG-4, 453 G./Mi. Grav. 19 C.Y./Mi. Maint. Dept.	7				6.09	
M	1944 A.F.E. 4	Spot Treat. Bit. Surf. Repair	26'		MC-3, 1421 Gal./Mi. Grav. 82 C.Y./Mi. Maint. Div.	8				6.08	
M	1945 A.F.E. 4	Spot Treat. Bit. Surf. Repair	26'		RT-6, 719 Gal./Mi. Grav. 34 C.Y./Mi. Maint. Div.	9				6.09	
M	1946 A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		RT-6, 9286 Gal. Agg. 468 C.Y.	10				6.09 (Net 1.16)	
M	1947 A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		SC-3, 1532 Gal. Agg. 85 C.Y.	11				6.09 (Net 0.23)	
C	1947 A.F.E. 34	Gravel Base Mixed Bit. (Mixed Prime)	27' 26'	7' 2"	SC-3, 48267 Gal. Agg. 27502 Tons.	12	0.80	3.22	1.44	0.98	
M	1948 A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		MC-3&SG-3, 25402 Gal. Agg. 1628 C.Y.	13				6.09 (Net 3.18)	
M	1949 A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		EC-3, 11692 Gal. Agg. 754 C.Y.	14				9.31 (Net 1.49)	

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1939	9.80	8.66	0.01	1.3	0.00	8.66	0.01	1.13	0.00
1940	1945	9.31	8.17	0.01	1.3	0.00	8.17	0.01	1.13	0.00
1956	1970	9.24	8.11	0.00	1.13	0.00	8.11	0.00	1.13	0.00
1971		9.16	8.03	0.00	1.13	0.00	8.03	0.00	1.13	0.00

REMARKS: Layout is to scale as of 1934


10-75

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4809  
TRUNK HIGHWAY 95  
COUNTY Wille Lacs  
DISTRICT 3B

LIMITS: West Co. Line to S. Jct. T.H. 169 in Princeton



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION				CODE N <sup>o</sup>
		TYPE	WIDTH	THICK-NESS	REMARKS	
M 1950	A.F.E. 4	Spot Treat. Bit. Surface Repair	24'		MC-1 RT-4, 9172 Gal. Agg. 598 C.Y.	
M 1951	A.F.E. 30 A.F.E. 4	Spot Base Repair Spot Treat. Bit. Surf. Repair	24'		SC-4, 2906 Gal. Agg. 169 C.Y.	
M 1952	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		SC-4, 15857 Gal. Agg. 1004 C.Y.	
M 1954	A.F.E. 604 A.F.E. 605	Spot Treat. Bit. Surf. Repair Fog & Light Seal	24'		Bit. 24075 Gal. Agg. 593 tons & 528 C.Y.	
C 1954 (1)	4809-05	Bit. Stab. Base (0.57 Mi) Plant Mix Bit.	24'	6" 2"		
M 1955	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		SC-4, 6424 Gal. Agg. 575 Tons	
M 1956	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		SC-4, 2970 Gal. Agg. 291 tons	
C 1956 (1)	4809-07	Grading Bit. Stab. Base Mixed Bit.	38' 38' 24'	5" 1"	Const. C10RDXB, 8914). on 12" sand-gr. sub-base	
M 1958	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		SC-4 & MC-2, 5325 Gal. Agg. 483 Tons	
M 1959	A.F.E. 605	Bit. Seal Coat	25'		RC-2, 15131 Gal. Agg. 244 C.Y.	
M 1960		Spot Treat. Bit. Surf. Repair	24'		SC-4, 4180 Gal. Agg. 455 Tons	
M 1964	C	Light Bit Seal	25'		RS-2K, 16732 Gal. Agg. 655 C.Y.	
C 1971	4809-10	Grading & Gr. Base Pl. Mix Bit. Base Pl. Mix Bit. Surf.	16 1/2" 1 1/2" 24'		Extend Br. 8914 43' Rt. 2 Lt.	
R 1980	4809-15 (0.82 - 1.04)	Grading Bit. Surfacing Curb & Outlet	24'	1 1/2"	Portions only on 14" T.H. 95	

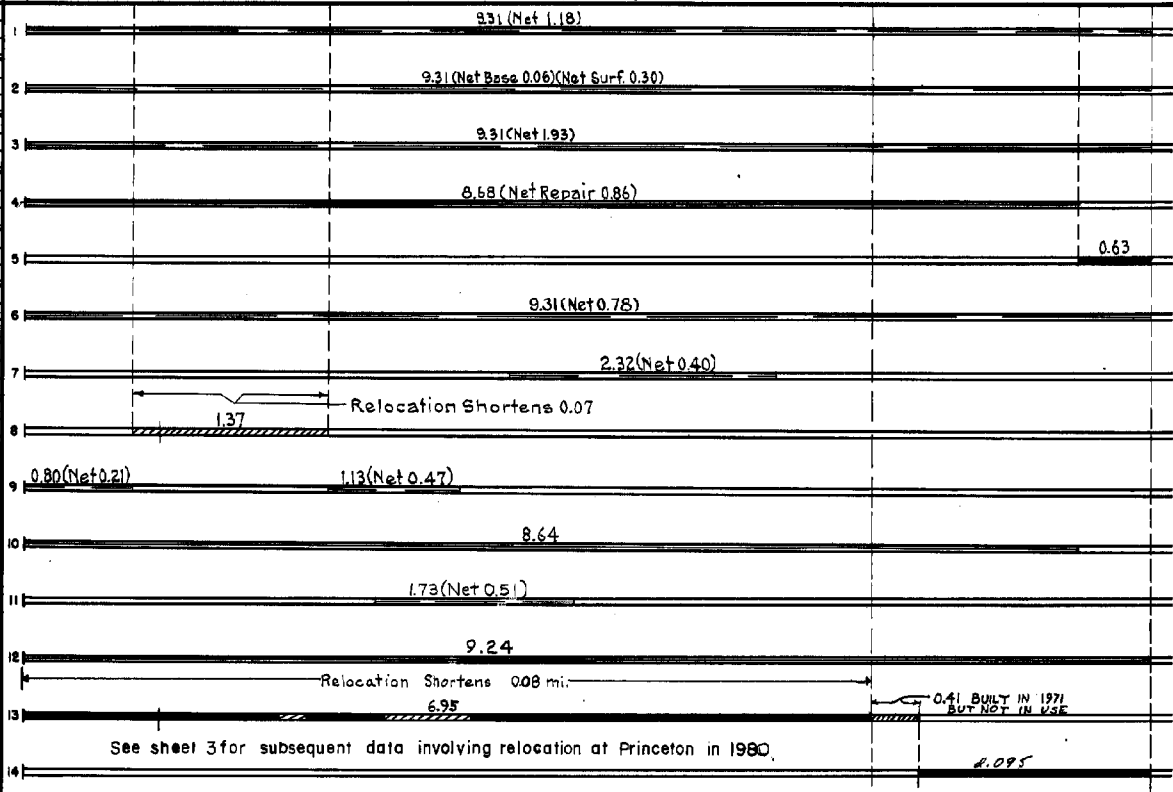

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet N<sup>o</sup> 1  
(1) Contract not final but work substantially complete

10-75

