


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 5102
TRUNK HIGHWAY 30
COUNTY MURRAY
DISTRICT 88

LIMITS: W. Jct. T.H. 91 in Lake Wilson - S. Jct. T.H. 59 in Slayton



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Grading	24'		No Record of Const.
		Gravel			No Record of Const.
1919	47-47-5	Br. 3194	20'		35' C.D.G.
1921	47-47-4 47-47-01	Grading	24'		
1921	47-47-1	Gravel	24'	1 3/4"	Co. Job 2004 800 C.Y./MI.
1922	47-47-4	Gravel	24'	2"	Maint. Dept.
1922	47-47-6	Concrete			
1922	47-17-5 47-17-7	Gravel Concrete	24'	3"	1600 C.Y./MI.
1932	47-47-21-2	Grading	40'		
		Br. 5167	27'		35' B.S.
1932	47-47-21-2	Gravel	32'	1"	600 C.Y./MI.
1932	47-47-21-2 B	Concrete	20'	9-9	
1935	47-47-21-2	Oil Tr. Gravel	24'	1"	13605 Gal./Mile Maint. Dept.
1936	47-47-21-2A	Concrete	20'	9-9	
1937	47-47-21-2C	Concrete	20'	9-9	

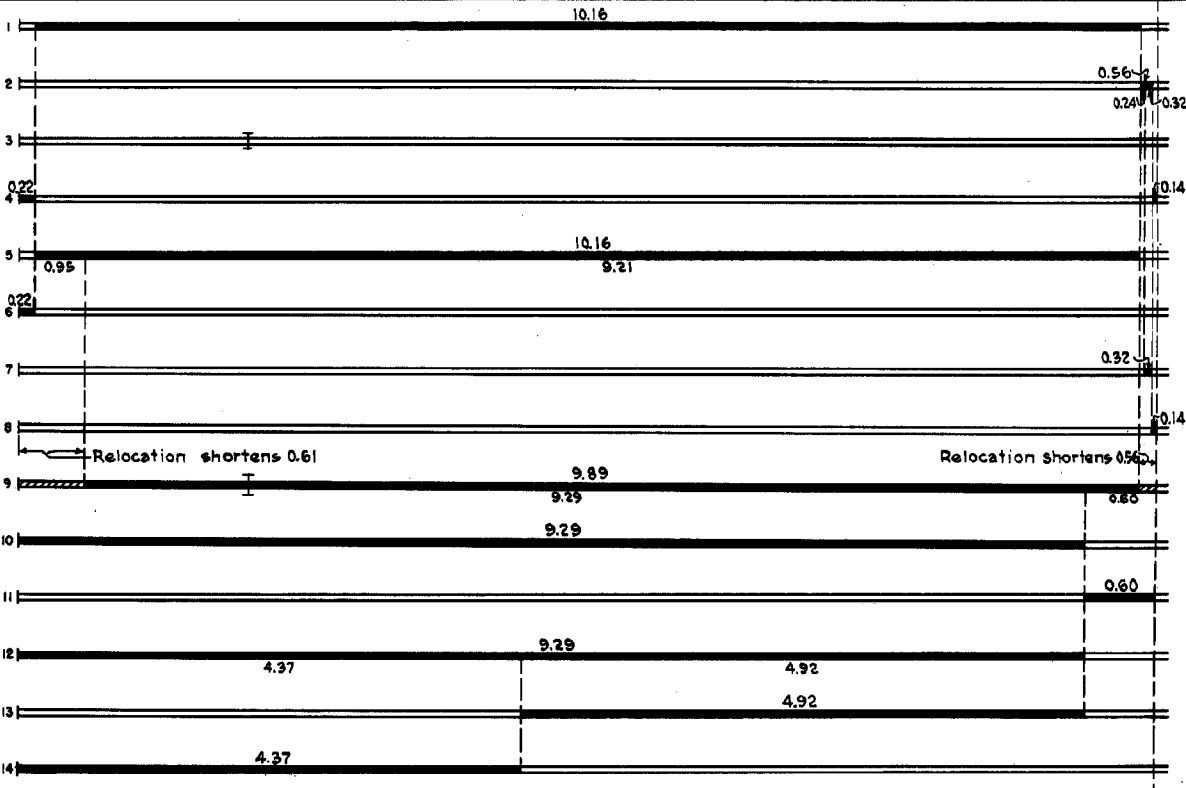

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1922	1931	11.68	8.78	0.01	2.29	0.00	10.01	0.01	1.06	0.00
1922	1955	9.89	8.97	0.01	0.91	0.00	9.38	0.01	0.50	0.00
1956		10.03	8.97	0.01	1.05	0.00	8.38	0.01	0.64	0.00

REMARKS: Layout is to scale as of 1937.
(1) This work not done under this project number but lies within the limits of this project.

