


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8002
TRUNK HIGHWAY 79
COUNTY Wadena
DISTRICT 4A

LIMITS: In Wadena
W. Co. Line (W. Corp. Limits) - Jct. T.H. 71
Ref. Pt. 125+00.681 - 126+00.557



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Earth			No Record of Constr.
1922	29-29-4	Concrete			
1928		Gravel			No Record of Constr. Status Map shows Gravel in 1928.
		Concrete			No Record of Constr. City St. taken over in 1933.
1933	29-29-24-2B	Grading Gravel	32' 30'	1 1/2"	800 C.Y./Mile
1935	29-29-24-2B	Tar Tr. Gravel	24'		Maint. Dept.
M	1940 A.F.E. 18	Bit. Seal Coat			Tar 3924 Gal./Mi. Sand 114 C.Y./Mi. Maint. Dept.
M	1944 A.F.E. 5	Bit. Seal Coat	24'		RC3, 3585 Gal./Mi. Agg. 130 C.Y./Mi. Maint. Div.
C	1947 A.F.E. 20	Bit. Resurfacing Mixed Bit.	24'	1" Added	MC3, 6124 Gal. Agg. 560 Ton.
M	1950 A.F.E. 4	Bit. Fog Seal	24'		RCS-1, 1948 Gal. Agg. 35 C.Y.
M	1953 A.F.E. 605	Light Bit. Seal	27'		MG3, 1000 Gal. Agg. 48 C.Y.
C	1954 8002-02	Plant Mix Bit.	24'	2" added	
M	1964 C	Light Bit. Seal	25'		RS-2K, 2155 Gal. Agg. 63 C.Y.
C	1974 -5	Grading, Agg. Base, Pl. Mix Bit. 3 1/2"	32' 50'	1 1/2" 3"	

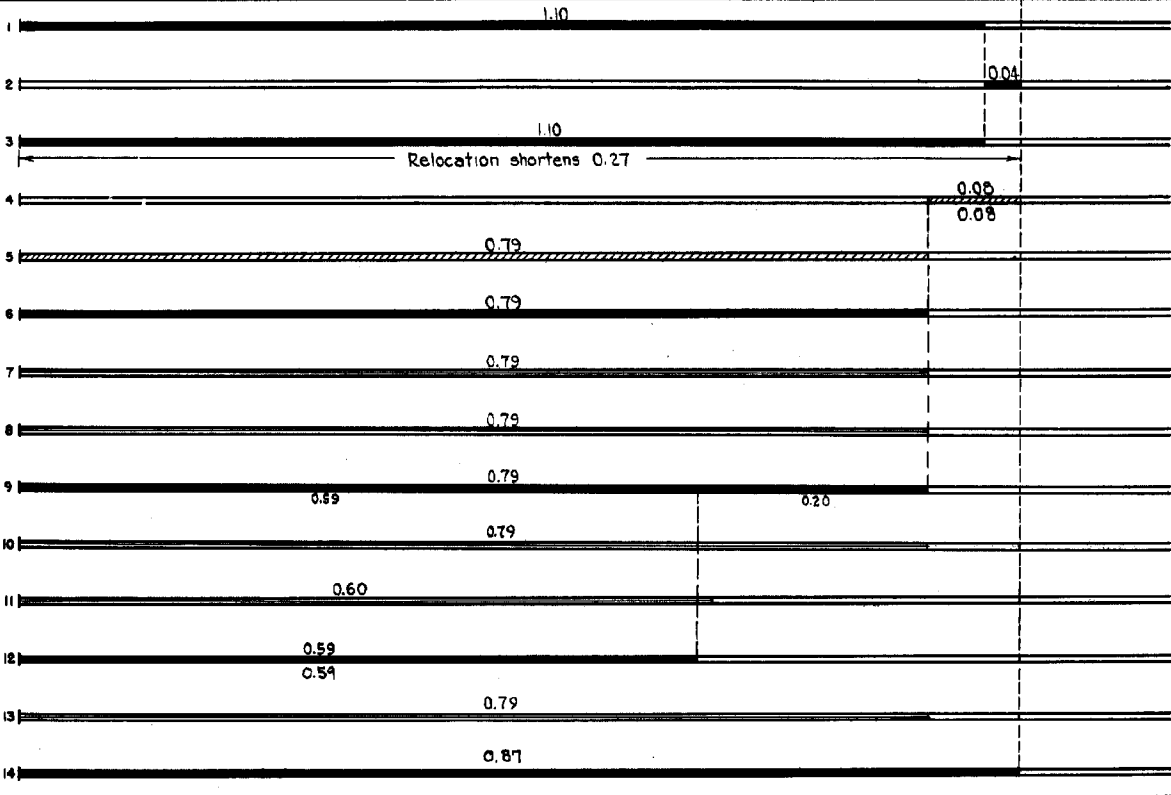

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1922	1932	1.14	0.00	0.00	1.14	0.00	0.00	0.00	1.14	0.00
1933		0.87	0.00	0.00	0.87	0.00	0.00	0.00	0.87	0.00

REMARKS: Layout is to scale as of 1933.
(1) This work not done under this project number but lies within the limits of this project.

