


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8209
TRUNK HIGHWAY 95
COUNTY Washington
DISTRICT 9A

LIMITS: Jct. T.H. 12 in Lakeland - S. Jct. T.H. 212 (S. Lim Stillwater)



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
					No Record of Constr.
		Oil Tr. Gravel	20'	1 1/2"	Added in 1934
		Tar Tr. Gravel (1)	18 1/2'	1 1/2"	Added in 1934
		Br. 6265 & X-464	21 1/2'		
1935	95-95-24	Grading	30'		
	(2)				
1935	95-95-24	Tar Tr. Gravel	28'	2"	10103 Gal./Mi. Maint. Dept.
M	1941 A.F.E. 24	Bit. Retread	26'		RT-6 3152 Gal./Mi. Gravel, 101 CY./Mi. Maint. Dept.
M	1942 A.F.E. 5	Bit. Seal Coat	24'		RT-10 2558 Gal./Mi. Sand, 111 CY./Mi. Maint. Dept.
M	1946 A.F.E. 4	Spot Treat. Bit. Surf. Repair	Var.		RT-6, 9281 Gal. Agg. 528 CY.
M	1947 A.F.E. 5	Bit. Seal Coat			RT-10, 12959 Gal. Agg. 595 Gal.
C	1941 A.F.E. 23	Mixed Bit. (1' Retread)	23'		RT-6, 7839 Gal./Mi. Gravel, 501 CY./Mi. Maint. Dept.
M	1942 A.F.E. 5	Bit. Seal Coat	22'		RT-10, 2818 Gal./Mi. Sand, 97 CY./Mi. Maint. Dept.
M	1947 A.F.E. 5	Bit. Seal Coat			
C	1949 8209-04 8209-06	Grading Stab. Gravel Seeding & Sodding	68'	1"	1200 CY./Mi.
C	1949 A.F.E. 30	Bit. Surfacing Mixed Bit.	48'	1"	56-38 RT-6, 6777 Gal. Agg. 275 CY.
M	1970 A.F.E. 4	Light Bit. Seal			RT-8, 7792 Gal. Agg. 277 CY.

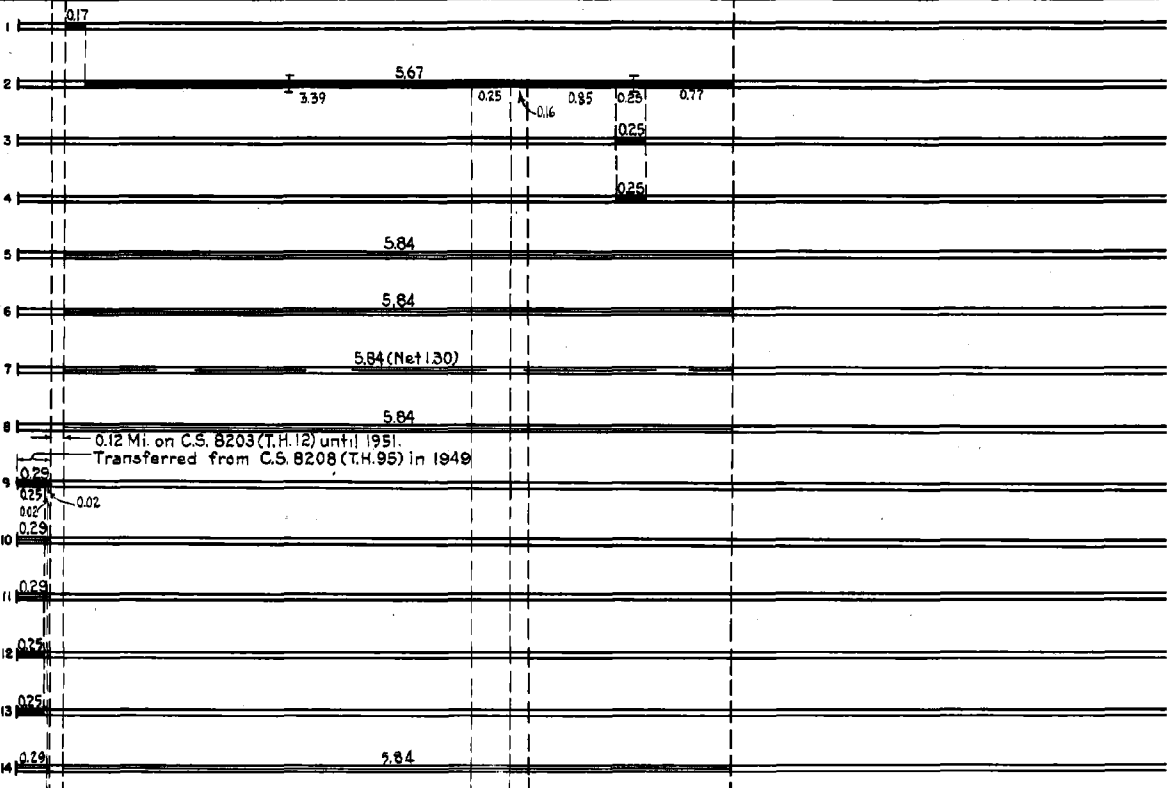

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1934	5.84	3.84	0.03	1.97	0.00	3.84	0.03	1.97	0.00
1935	1948	5.84	3.65	0.00	1.99	0.00	3.65	0.00	1.99	0.00
1949	1950	6.13	4.14	0.00	1.99	0.00	4.14	0.00	1.99	0.00
1951	1951	6.25	3.39	0.00	2.66	0.00	4.26	0.00	1.99	0.00
1952	1958	6.14	3.31	0.00	2.83	0.00	4.18	0.00	1.96	0.00
1959	1959	6.14	2.74	0.00	3.40	0.00	4.18	0.00	1.96	0.00
1960	1965	5.85	2.53	0.05	3.27	0.00	3.98	0.05	1.82	0.00


REMARKS: Layout is to scale as of 1934.
 (1) Br. X-464 replaced by Fill in 1935. Br. 6265, B.S. & W. RT-U.P.; Br. X-464, 174' W. RT-O.H.
 (2) This work not done under this project number but lies within the limits of this project.

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8209
TRUNK HIGHWAY 95
COUNTY Washington
DISTRICT 9A

LIMITS: Jct. T.H. 12 in Lakeland - S. Jct. T.H. 212 (S. Lim. Stillwater)



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
M	1951 A.F.E. 4	Bit. Seal Coat (Spots)			RT-6, 1684 Gal. Agg. 60 C.Y.
					Transferred from T.H. 12 (C.S. 8209) in 1951.
		Tarvin Tr. Gravel	27'	3"	13700 Gal.
C	1952 8209-03 A.F.E. 48	Grading Gravel Base Guard Rail	32 1/2' 30 1/2'	3" 4'-6"	10' Select Mat'l (Sand)
C	1952 A.F.E. 45	Bit. Surfacing Mixed Bit. Bit. Fog Seal	32 1/2'	1"	RT-4&6, 26026 Gal.
M	1952 A.F.E. 4	Spot Treat Bit. Surf. Repair Spot Fog Seal	22' 24'		MC-3 RT-4&6, 8472 Gal. Agg. 820 C.Y. Spot Seal Patching
C	1953 8209-11 (3)	Grading Grav. Base Plant Mix Bit.	41' 52' 24 1/2'	4 1/2" 9" 2'-3"	
M	1955 A.F.E. 604	Spot Treat Bit. Surf. Repair	24'		MC-3, 16290 Gal. Agg. 1590 Tons
M	1956 A.F.E. 604	Spot Treat Bit. Surf. Repair	24'		MC-3, 9169 Gal. Agg. 897 Tons
C	1960 8209-17 8209-16	Grading, Gravel Base Road Mix Bit. (Base) Br. 9391	52 1/2' 41'	1 1/2"	0.41 Mi. Divided Highway 260' B.S.-O.H.
C	1960 8214-13	Grading Gravel & Bit. Base Plant Mix Bit.	36 1/2' 24 1/2'	1 1/2" 3"	0.23 Mi. Divided Highway
C	1961 8209-10	Grading Gravel & Bit. Base Plant Mix Bit. Surf.	24 1/2'	3"	846 Tons Bit. Mat'l.
M	1972 SF	Bit. Surf. Repair			RC-250 100 Gal. Agg. 1077 Ton
C	1973 8209-29	Rt. TURN LANE	13'	9"	At 10 th Av. N.
C	1984 8282-39	Grading, Base Bit. Surfacing Bit. Shoulders	24' 24' 10'	6" 6 1/4"	Divided Rdwy.

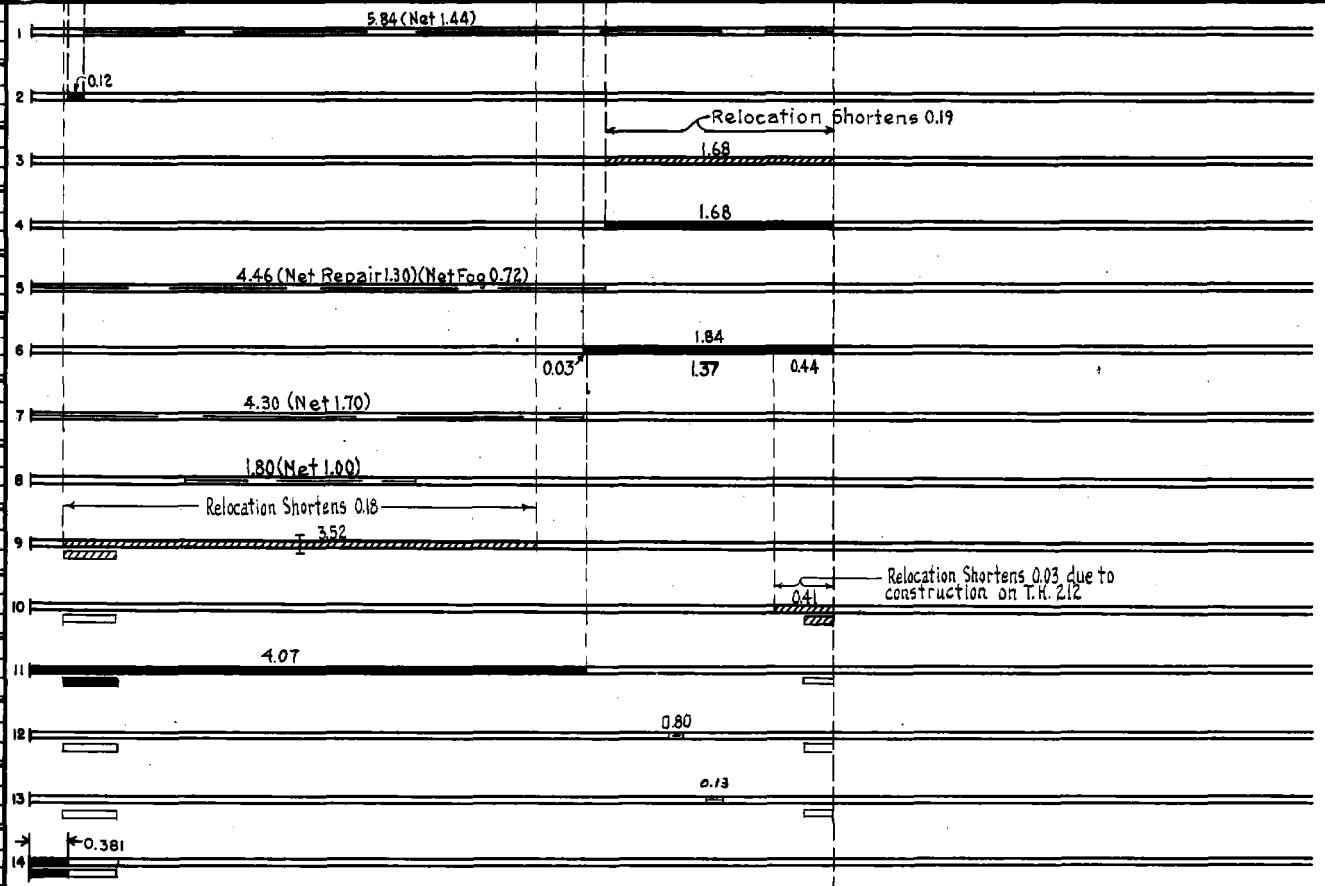

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1966		5.85	1.99	0.09	3.81	0.00	3.98	0.09	1.82	0.00

REMARKS: See Sheet No. 1
(3) Contract not final but work substantially complete (4) See C.S. 8203

