




PREPARED BY  
BUREAU OF POLICY & PLANNING  
IN COOPERATION WITH  
U.S. DEPARTMENT OF TRANSPORTATION-FEDERAL HIGHWAY ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF TRANSPORTATION  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 7380C  
TRUNK HIGHWAY 94  
COUNTY Stearns  
DISTRICT 3B

LIMITS: E. Lim. of Avon to Jct T.H. 15  
Ref. Pt. 153+00.825 - 166+00.632



YEAR BUILT	PROJECT NO	DESCRIPTION				REMARKS
		TYPE	WIDTH	THICKNESS		
C	1978 7380-73871	Perf. Br			298'-6"	
M	1980 7380-165	Erosion & Drainage Corr.				
M	1982 SF	Snow & Ice Control				Contract No 3952 Oct. 13, 1982 - May 15, 1983
M	1982 7380-182	Safety Barrierment Guardrail, Misc. Grading Culvert Extensions				Contract No. 18417
C	1984 7380-178	Bit. Milling Bit. Surfacing	2-24'	3 1/2"		
C	1985 7380-179	Br. Repair & Overlay	40'-8"	2 1/2"		Br. 73886 & 73882
C	1991 7380-181	Conc. Repair				
C	1995 7380-198	Milling Bit. Overlay	12 1/2'	1 1/2"		Spec. 2347
C	1995 7380-198	Bit. Overlay Edge Drain Bit. Overlay (shldr)	24'-36'	3"		Spec. 2347 Spec. 2331
C	1999 7380-205	Milling Bit. Overlay	24'	2 1/2"		Spec. 2360
M	2001 8823-19	Micro-Surfacing	25'			Spec. 2356 Type 2
M	2004 8823-59	Concrete Planing Microsurfacing	24'			Type 2
R	2009 7380-227	Grinding Concrete Rehab.				E.B. Only
M	2011 8823-244	Microsurfacing				Fog seal shoulders WB EB

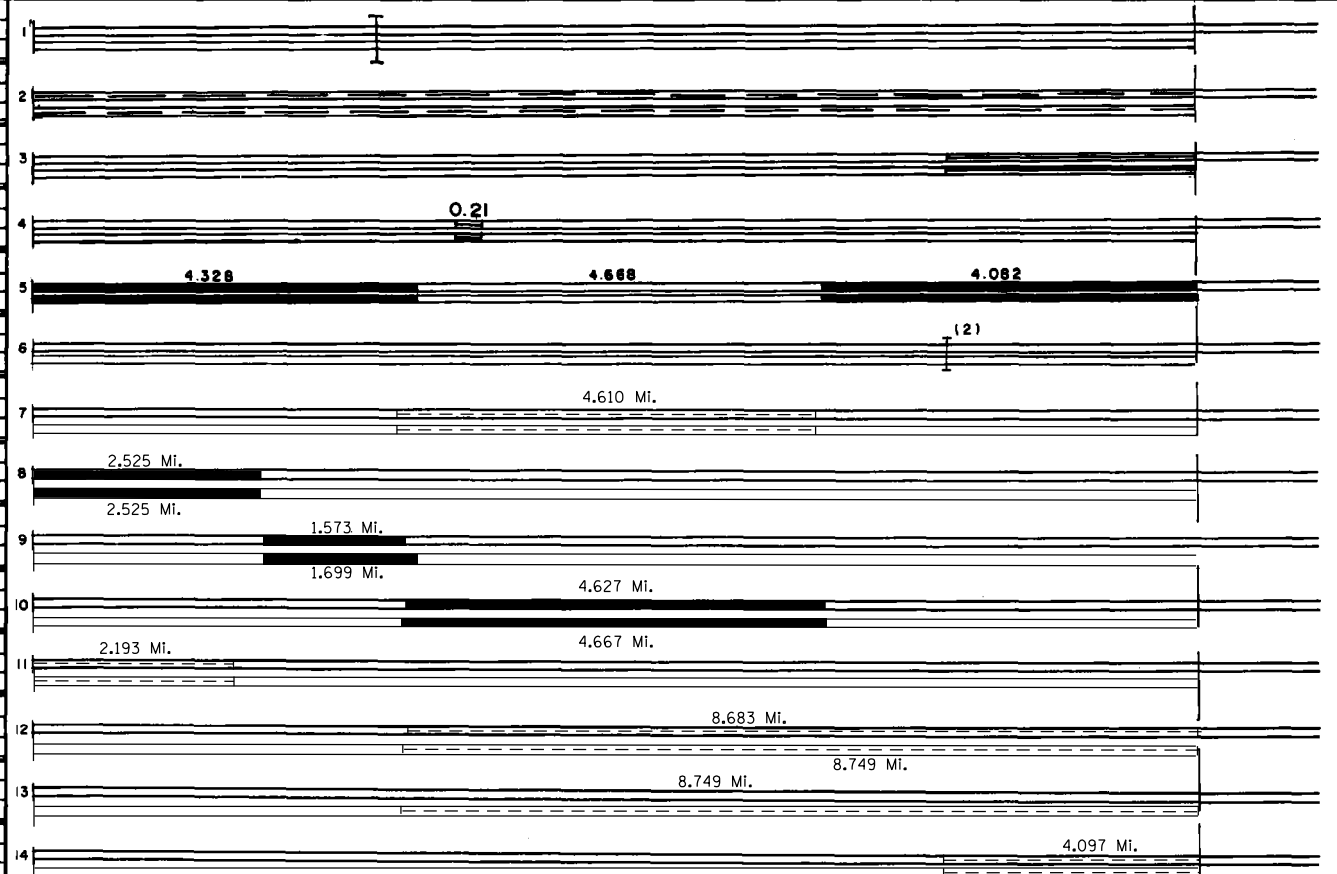

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN		REMARKS:
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	

4.088 Mi.

