


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0309  
TRUNK HIGHWAY 225  
COUNTY Becker  
DISTRICT 4A

LIMITS: Ponsford - Jct.T.H.34 at Osage  
Ref. Pt. 000+00.000 - 008+00.793



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Mixed Bit.	20'-30'		
					No Record of Const. Added in 1949
C	A.F.E. 16	Bit. Resurfacing			MC-3, 83150 Gal.
1950		Mixed Bit.	22'-30'	1 1/2" added	Agg. 6174 Tons
M	A.F.E. 605	Light Bit. Seal	21'-30'		RS2, 17773 Gal. Agg. 615 C.Y.
1954					
M	A.F.E. 604	Spot Treat Bit. Surf. Repair	22'		MC-3, 19218 Gal. Agg. 1320 Tons
1956					
M	A.F.E. 604	Bit. Surf. Repair	24'		MC-3, 9455 Gal. Agg. 539 Tons
1958					
M	A.F.E. 604	Bit. Surf. Repair	24'	1"	MC-3, 19425 Gal. Agg. 1340 Tons
1959					
M	SF	Bit. Surf. Repair	22'		MC-2, Tack 798 Gal. Bit Mix 1264 Tons
1965					
M	SF	RESHAPE CURVES	24'	VAR	Pl. Mix Bit. 1500 Ton TACK 600 GAL
1977					
M	SF	BIT OVERLAY	22'	2"	Pl. Mix Bit. 12791.9 Ton SEAL 5400 GAL
1977					
M	SF	SHOULDERING	2'	4"	AGGREGATE 4200 Ton
1977					
S	0309-02	Bit. Overlay	22'	1 1/2"	Spec. 2350
2002					
S	8824-116	Aggregate Shouldering	2'	2"	Class 1 RT & LT
2014					
2017	0309	CS turnback 8.809 mi. to Becker Co.			Effective date September 1, 2017

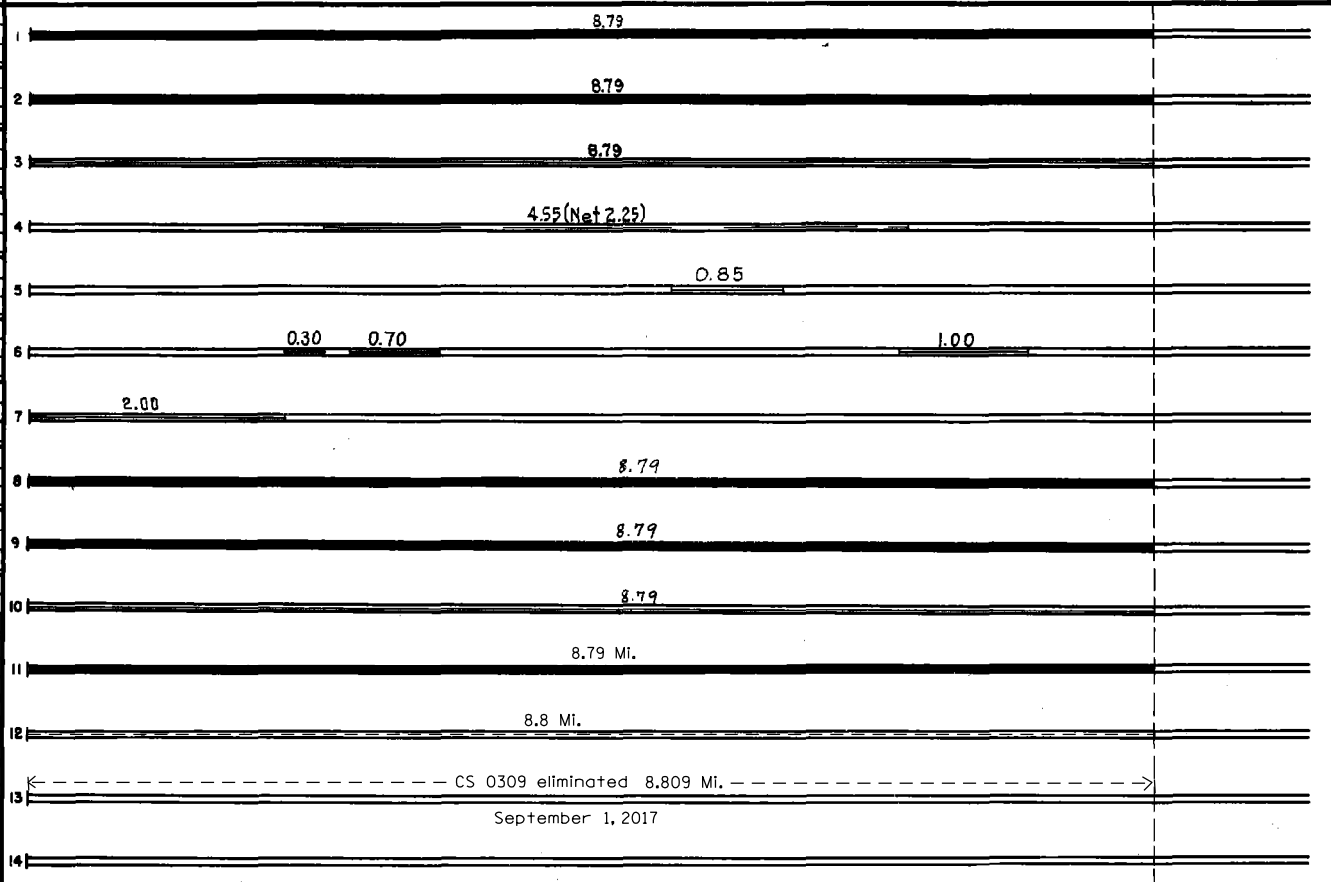

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949		8.79	8.79	0.00	0.00	0.00		8.79	0.00	0.00

REMARKS: Layout is to scale as of 1949
