


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0806
TRUNK HIGHWAY 68
COUNTY Brown
DISTRICT 7B

LIMITS: Jct. T.H.15 - East County Line



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
1930		Gravel	24'	2 1/2"	Co. Job N ^o 2902. 1200 C.Y./Mile. Added in 1934.
1935	83-83-21	Grading Br. N ^o 5431	32' 30'		132' C.D.G. - 0H.
1936	83-83-21	CaCl ₂ Stab Grav. Sand Base	24' 24'	2" 10"	1/3" Sand sub. base. 1/4" Sand at base.
1937	83-83-21 A.F.E. 20-Dist. 14	Oil Tr. Gravel	24'	1 1/2"	15408 Gal./Mile. Maint. Dept.
1937	A.F.E. 10	Seeding			Maint. Dept.
M	A.F.E. 4	Spot Treat. Bit. Surf. Repair			MG 3, 2099 Gal./Mi. Grav. 104 C.Y./Mi. Maint. Div.
C	A.F.E. 16	Bit. Resurfacing Mixed Bit.	24'	7/8" added	MG 2, 9629 Gal./Mi. Grav. 415 C.Y./Mi. Maint. Div.
M	A.F.E. 5	Bit. Seal Coat	26'		RC 4, 17574 Gal. Agg. 4000 C.Y.
M	A.F.E. 604 A.F.E. 605	Bit. Surf. Repair Light Bit. Seal	24' 24'		SC 36 RS 2, 3448 Gal. Agg. 45 Tons & 118 C.Y.
C	0806-05	Sand Grav. Subbase Bit. Stab. base Plant Mix Bit.	34' 34' 24'	6" 4" 1 1/2"	Grad. or Shoulder Grad.
M	1957 A.F.E. 605	Bit. Seal Coat	25'		RS-2, 11410 Gal. Agg. 405 C.Y.
M	1964 C	Light Bit. seal	25'		RS-2K, 5878 Gal. Agg. 200 C.Y.
M	1966 SF	Bit. Surf. Repair	24'	1 1/2"	RC-2 Bit, 170 Gal. Pl. Mix Bit, 1639 Ton
C	1969 0805-22	Grade, Base Pl. Mix. Bit. Surf. Pl. Mix. Bit. Shldr.	24'	3"	

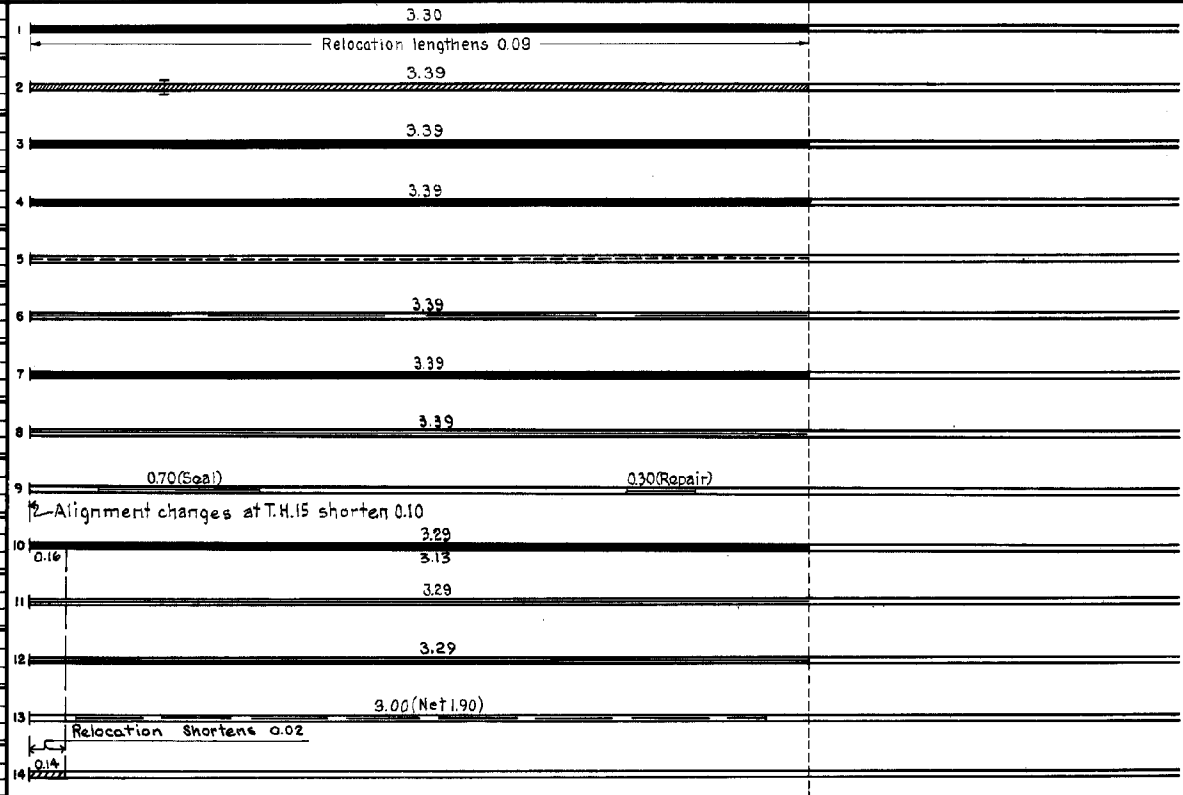

YEARS FROM TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934 1934	3.30	3.30	0.00	0.00	0.00	3.30	0.00	0.00	0.00
1935 1955	3.39	3.36	0.03	0.00	0.00	3.36	0.03	0.00	0.00
1956 1966	3.29	3.26	0.03	0.00	0.00	3.26	0.03	0.00	0.00
1969	3.27	3.24	0.03	0.00	0.00	3.24	0.03	0.00	0.00

REMARKS: Layout is to scale as of 1935

(1) This work not done under this project number but lies within the limits of this project.

