


PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0980A
TRUNK HIGHWAY 35
COUNTY Carlton
MAINTENANCE DISTRICT 1A

LIMITS: S. Co. Line - C.S.A.H.4
Ref. Pt. 213+00.334 - 227+00.314



YEAR BUILT	PROJECT NO	DESCRIPTION			
		TYPE	WIDTH	THICKNESS	REMARKS
C	0980-31	Grading 1.70 mi.			Divided Highway
1966	0980-39	Gravel, Sub-base & Base P.C. Concrete 1.60 mi.		5 1/4" 2@24" 9"	
C	0980-09811	Br. 09811			231' P.P.G. - U.P.
1966					
C	0980-32	Grading Br. 09810 Br. 09835 & 09836			Divided Highway C1212D Both 264' B.S.
1970	0980-32	Br. 09815 & 09816			Both 141' B.S.
C	0980-30	Grading Br. 09832			Divided Highway 220' P.P.G. - U.P.
1970	0980-30	Br. 09817 & 09818 Br. 09819 Br. 09820			Both 107' B.S. 282' B.S. - U.P. 220' P.P.G. - U.P.
C	0980-30	Br. 09821			195' P.P.G. - U.P.
1970	0980-48	Gravel & P.M. Bit Base P.C. & Asph. Concrete	2@24"	9" 13/16"	9.68 Mi. P.C. 2.50 Mi. Asph. P.M. Mix Bit Shoulders
C	0980-44	Grading, Base P.M. Mix. Bit. Surface for Interchange Ramps			
1975	0980-77	CONCRETE PAVEMENT JOINT REPAIR			
C	0980-97	SURFACING OF MISC RAMPS, ACCEL. & DECEL LANE AND SHOULDERS			
1981	0980-100	Traffic Barrier HES 000S(47)			Construction
C	0980-108	Pavement Crack and Joint Repair			
M	1984	SF	1-2'	0-4"	Sp. 2361 410 Tons With C.S. 5880
M	1985	SF	3'	1"	Wedge Paving Left Shldr.
C	1990	0980-114	24'	1"	Mill & Bit. Overlay Spec. 2341 Spec. 2361

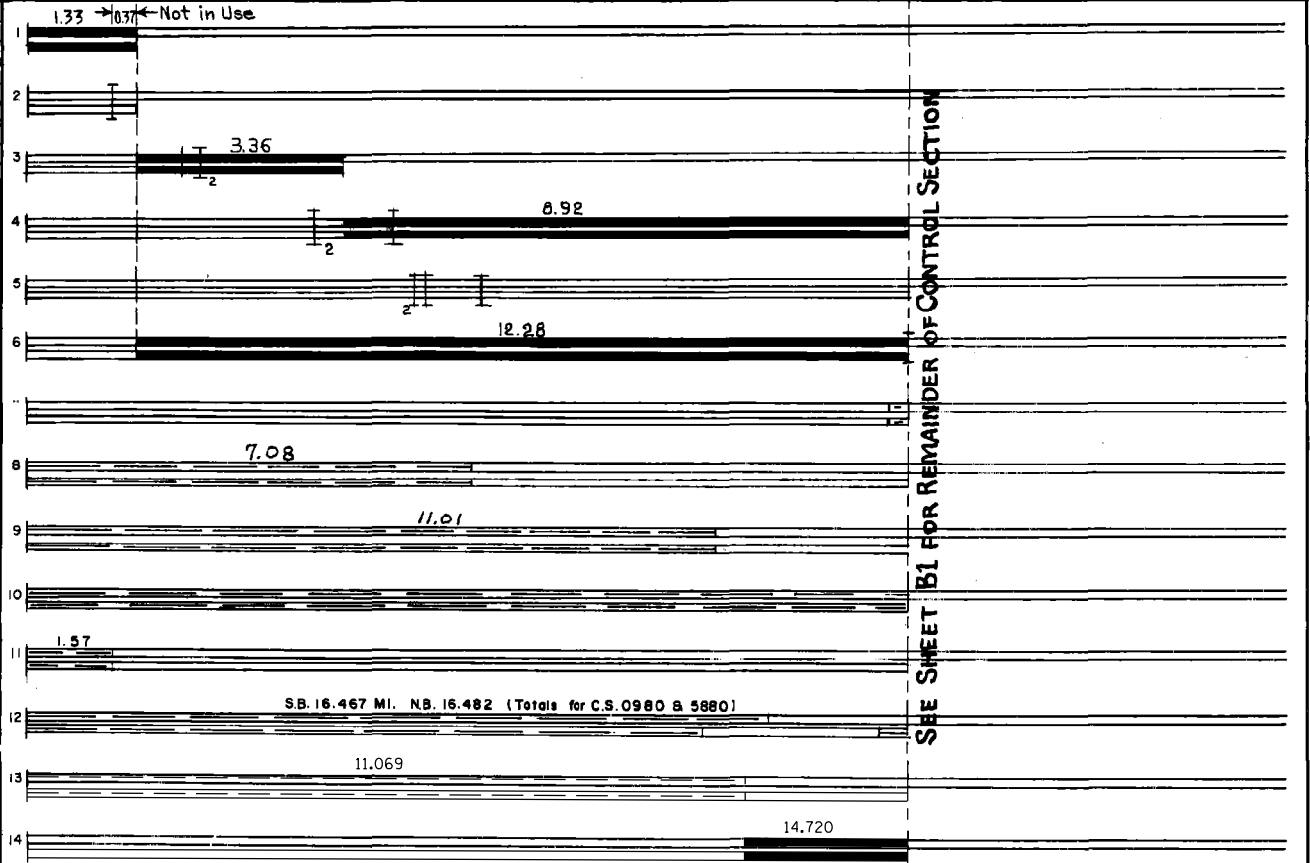

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN		
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	
1966	1969	1.33	1.33	0.00	0.00	0.00	0.00	1.33	0.00	0.00	0.00
1970		13.98	13.32	0.00	0.56	0.10	13.88	0.10	0.00	0.00	

REMARKS: Layout is to scale as of 1966.

