


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1203  
TRUNK HIGHWAY 7  
COUNTY Chippewa  
DISTRICT 8A

LIMITS: Jct. T.H. 23 - E. Co. Line



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
		Oil Tr. Gravel	50'	2"	No Record of Const. Added in 1934.
		Gravel Br. 2778	18'	1"	No Record of Const. Added in 1934 43 C.T.G.
1926		Gravel	18'	2 1/2"	Co. Job N <sup>o</sup> 2616. 1200 C.Y. / Mile. Added in 1934.
M	1941 A.F.E. 60	Regravelling			183 C.Y. / Mile. Maint. Dept.
C	1941 1203-02	Grading Stab. Gravel Culvert	36'		1357 C.Y. / Mile. C84X40.
C	1942 1203-01	Br. 5865	30'		40 C.D.G.
C	1942 A.F.E. 7	Seeding			Seed supplied by R.S.D.(S.P.1203-06) Maint. Dept.
M	1944 A.F.E. 6	Grav. Resurfacing			315 C.Y. / Mi. Maint. Div.
M	1947 A.F.E. 6	Grav. Resurfacing			4032 Tons
M	1949 A.F.E. 6	Grav. Resurfacing			4885 Tons
C&M	1952 A.F.E. 23 A.F.E. 6	Install S.C. Culvert Grav. Resurfacing	34'		48" x 84" 8701 Tons
C	1953 1203-07	Sand-Grav. Subbase Grav. Base Plant Mix Bit.	32' 32' 24'	9-12" 3" 2"	
M&C	1956 A.F.E. 605 A.F.E. 819	Bit Seal Coat Install S.C. Culv.	24'		RC-5 20947 Gal. Agg. 845 C.Y.
C	1962 1203-09	Grading Sub-base & base Gravel Base Plant Mix Bit			Grading Sub-base & base rt & lt of surf. in place. for major portion of proj.

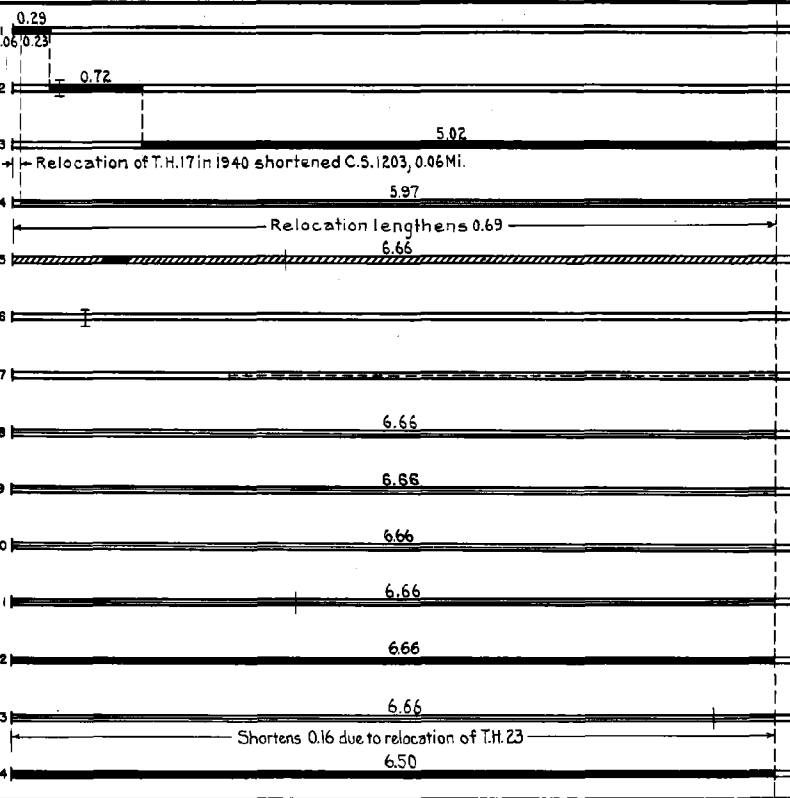

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1938	6.03	4.52	0.00	1.50	0.01	6.02	0.01	0.00	0.00
1940	1940	5.37	4.52	0.00	1.44	0.01	5.96	0.01	0.00	0.00
1941	1943	6.66	4.75	0.00	1.90	0.01	6.65	0.01	0.00	0.00
1944	1950	6.66	5.89	0.00	0.76	0.01	6.65	0.01	0.00	0.00
1951	1961	6.66	5.89	0.00	0.76	0.01	7.89	0.00	0.76	0.01
1962		6.50	5.65	0.00	0.80	0.01	5.69	0.00	0.80	0.01

REMARKS: Layout is to scale as of 1941

