


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1302
TRUNK HIGHWAY 61
COUNTY Chicago
DISTRICT 9A

LIMITS: South Co. Line - Jct. T.H.98 in Wyoming



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
1918		Grading	26'		F.A.P. N ^o 2.
1920		Gravel	24'	3 1/2"	F.A.P. N ^o 2. 1700 C.Y./Mile.
1926	61-1-34B	Grading Concrete	32' 18'	8-78	
1939	A.F.E. 33	Stab. Grav. Should.	12'	1"	Grt. & Lt. Maint. Dept.
C		Grade Widening			
1949	1302-03	Plant Mix Bit. (2)	24'	3 1/2"	
(1)	1302-04	Ext. W86D			A.F.E. 27(3)
M					RC-1, 4671 Gal. Agg. 130 C.Y.
1950	A.F.E. 5	Light Bit. Seal			
M					RC-5, 2,4197 Gal. Agg. 135 C.Y.
1952	A.F.E. 5	Light Bit. Seal	24'		
M		Grav. Lift 0.06 Mi. Mixed Bit. 0.06 Mi. Bit. Seal Coat	24'		AG-1, 6 Tons RT-6, 1205 Gal. Agg. 92 C.Y.
1954	A.F.E. 605	Light Bit. Seal	24'		RC-2, 3405 Gal. Agg. 160 C.Y.
M		Profile Correction			Plant Mix 768 Tons Shoulder Grav. 208 C.Y.
1957	A.F.E. 818	Profile Correction			
M		Bit. Seal Coat	25'		RC-5, 7439 Gal. Agg. 272 C.Y.
1958	A.F.E. 605	Bit. Seal Coat	25'		
C		Plant Mix Bit Gravel Shoulders	24'	2 1/2"	
1965	By Maint. Div.	Plant Mix Bit Gravel Shoulders	24'	2 1/2"	
C		Grade, Base, Pl. Mix Bit. Surf. Boz2 C & G	44'	3 1/2"	
1969	1302-06	Grade, Base, Pl. Mix Bit. Surf. Boz2 C & G	44'	3 1/2"	

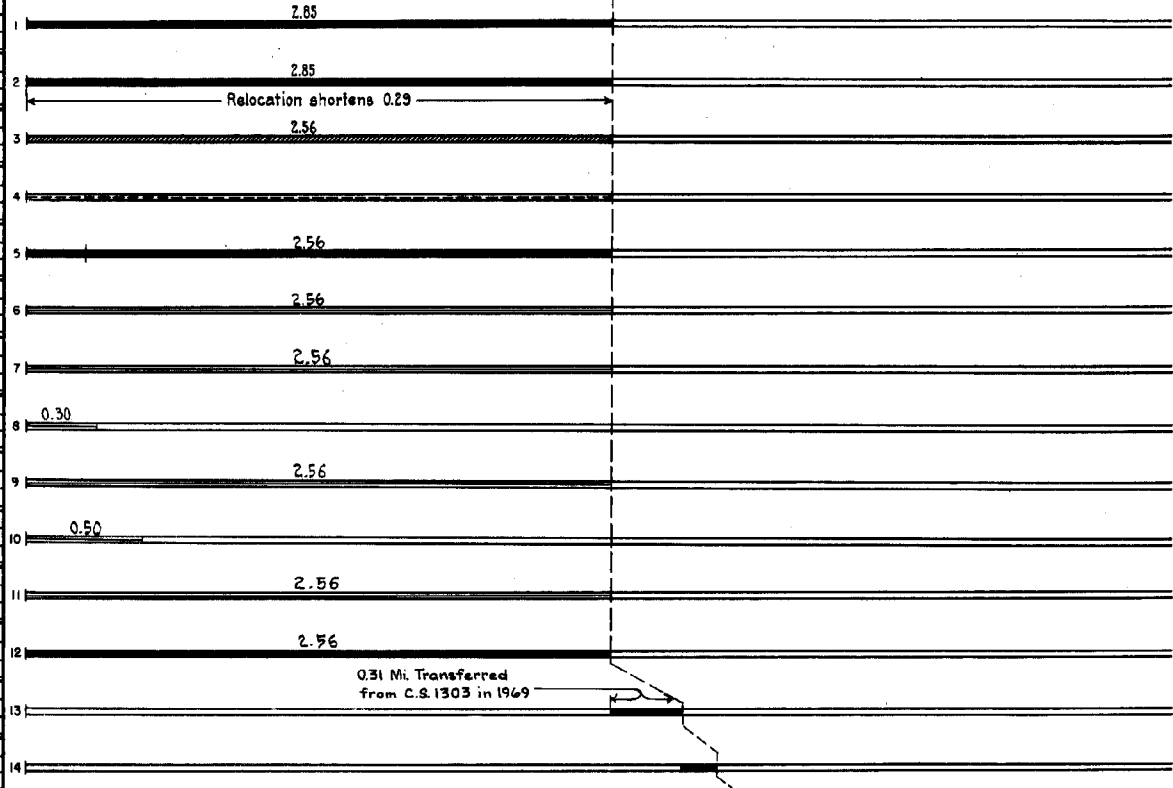

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1923	2.85	2.33	0.00	0.50	0.00	2.85	0.00	0.00	0.00
1926	1967	2.56	2.08	0.00	0.48	0.00	2.56	0.00	0.00	0.00
1968	1968	2.56	1.66	0.00	0.90	0.00	2.56	0.00	0.00	0.00
1969		3.24	1.66	0.00	1.58	0.00	3.24	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1926
 (1) Contract not final but work substantially complete in 1949 on S.P. 1302-04. (2) 19.5% of this 2.56 Mi. is Plant Mix Bit. on Van (11" min) Bit. Stab. Base, the balance is Plant Mix Bit. on old 18" Concrete Base which was widened to 24". (3) A.F.E. 27 covers a temporary 1" x 28" Bit. Mat placed on Bit. Stab. Base.

