


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2105
TRUNK HIGHWAY 52
COUNTY Douglas
DISTRICT 4B

LIMITS: Jct. T.H. 79 in Evansville - W. Jct. T.H. 29 in Alexandria
(See sheet 2 for revised limits)



YEAR BUILT	PROJECT N ^o	DESCRIPTION				CODE N ^o
		TYPE	WIDTH	THICKNESS	REMARKS	
1920	52-3-12	Grading Gravel Br. 1655	24' 24' 22'		Co. Job 1821. 1200 C.Y./Mile. 16' Slab Span.	
1921		Grading (1) Gravel	24' 24'	2"	Maint. Dept. Divided Highway.	
1921	52-3-16	Asph. Concrete Concrete Base	46' 46'	2" 6"	2-23 Roadways with 30' Ctr. Island.	
1925	52-3-41B	Grading Gravel	30' 24'		1800 C.Y./Mile.	
1930	52-3-53-1&2	Grading	40'			
1930	52-3-53-1&2	Gravel	28'	1 1/2"	800 C.Y./Mile. Maint. Dept.	
1930	52-3-53-1	Oil Tr. Gravel			9937 Gal./Mile. Maint. Dept.	
1931	52-3-53-1&2	Grading Gravel	40' 28'		800 C.Y./Mile.	
1932	52-3-41D	Grading Gravel	40' 28'	1 1/2"	800 C.Y./Mile.	
1932	52-3-53-3	Grading Gravel	40' 28'	2 1/2"	1400 C.Y./Mile.	
1932	52-3-53-1&2	Concrete	20'	9-79		
1933	52-3-53-3	Concrete	20'	9-79		
1935	52-3-53-1	Roadside Develop.				
1936	52-3-41D	Roadside Develop.				

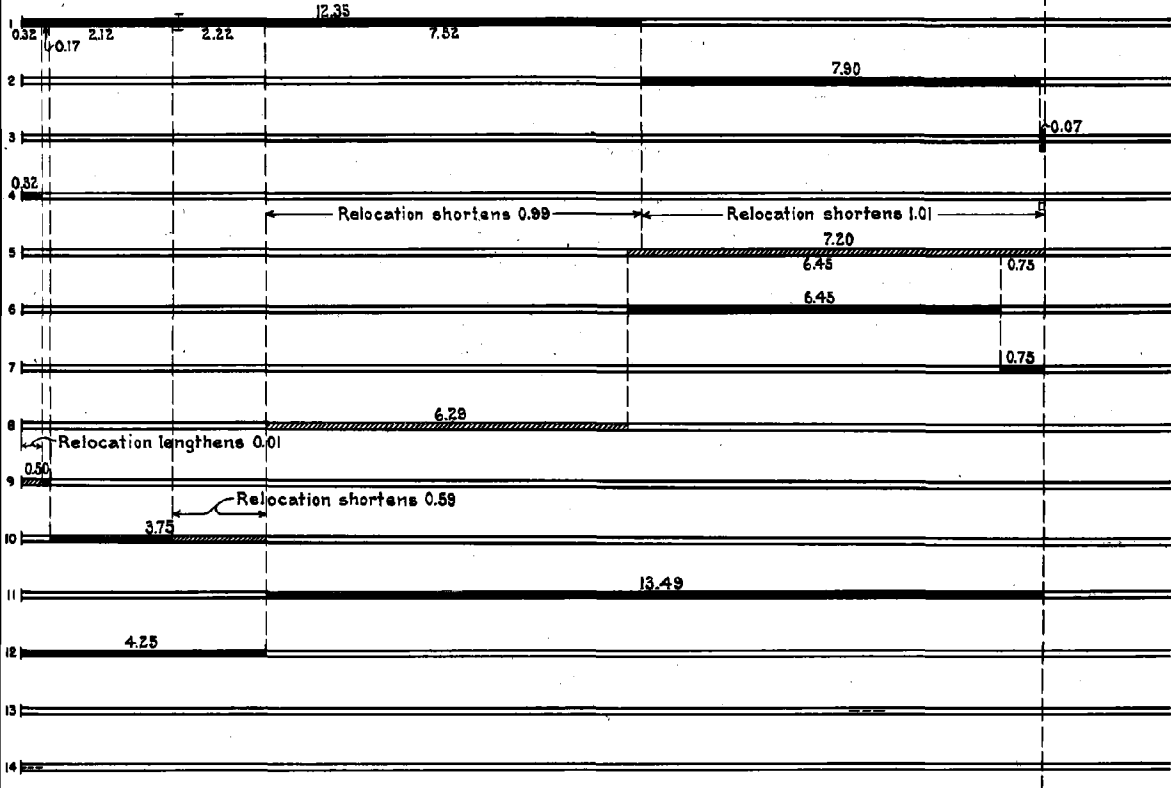

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1929	20.32	17.16	0.00	3.16	0.00	19.35	0.00	0.97	0.00
1930	1930	19.31	16.50	0.00	2.81	0.00	18.56	0.00	0.75	0.00
1931	1931	18.32	15.92	0.00	2.40	0.00	18.57	0.00	0.75	0.00
1932	1937	17.74	15.33	0.00	2.41	0.00	16.95	0.00	0.75	0.00
1938	See Sheet No 2									

REMARKS: Layout is to scale as of 1932

(1) No record of constr. of grading

(2) This work not done under these project numbers but lies within the limits of these projects

