


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2407  
TRUNK HIGHWAY 109  
COUNTY Freeborn  
DISTRICT 6B-7A

LIMITS: W. Co. Line - S. Ramps At T.H. 90



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
		Gravel Br 2969	20'4" 17'	2" 14"	No Record of Constr. Added in 1934.
1936	109-124-22-1	Grading Concrete Gravel Cushion	20'58"	9-7-9 12"	
1936	109-124-22-1	Grading Concrete Gravel Cushion	20'58"	9-7-9 12"	Not in use as Trunk Highway until 1947
1936	109-124-22	Xing Signal			
M	1942 A.F.E.6	Regravelling			487 C.Y./Mile. Maint. Dept.
M	1943 A.F.E.6	Grav. Resurface (Spots)			48 C.Y./Mi. Maint. Dept.
M	1944 A.F.E.6	Grav. Resurfacing			538 C.Y./Mi. Maint. Div.
C	1947 2407-01	Grading Stab Gravel Culvert (1)	36'0"	1 1/2"	1200 C.Y./Mi. C86x74.
C	1948 2407-03 (2)	Shoulder Grading Concrete & Concrete Widening	24'4"	9-7-9 9-7-9	
M	1968 SF	Regravel Shoulders	16'		8' each Side 3/4" Crushed Grav.
C	1972 2481-05	Grading Gravel Base P.C. Concrete	24'	8"	See C.S. 2481 for Br 24810
C	1975 2481-23	GRAVEL BASE P.C. CONC. P.L. MIX BIT. SHLDRS	24'	9"	SHORTENS C.S. 0.45 MI.
M	1977 SF	P.L. MIX BIT. OVERLAY	22'	1 3/4"	1200 TON S
M	1980 2407	Gravel Shoulders	10'	3"	1648 TON

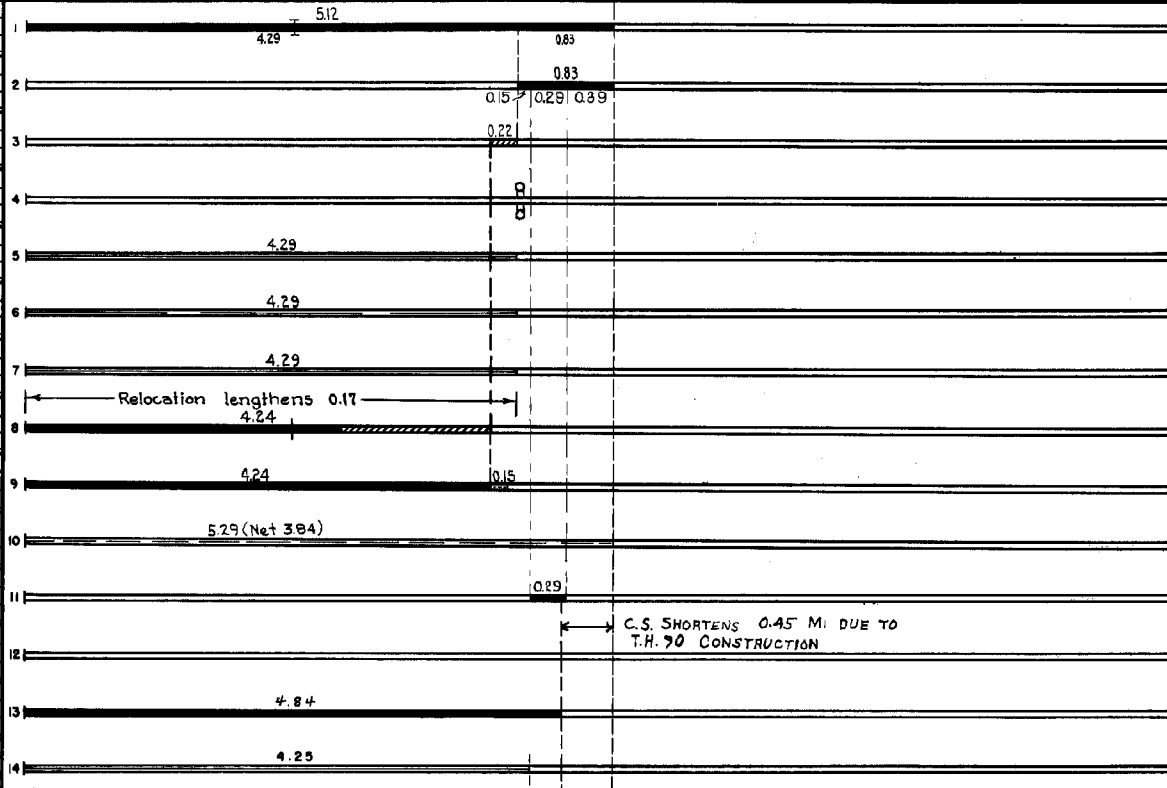

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1946	5.12	4.16	0.01	0.96	0.00	5.11	0.01	0.00
1947	1974	5.29	4.09	0.00	1.20	0.00	5.29	0.00	0.00
1975		4.84	3.78	0.06	1.00	---	3.78	0.06	---

REMARKS: Layout is to scale as of 1934.  
(1) Culvert C86x74' replaces Br 2969 which was removed.  
(2) Contract not final but work substantially complete in 1948.

12-75

