


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2910  
TRUNK HIGHWAY 200  
COUNTY Hubbard  
DISTRICT 2A

LIMITS: W. Co. Line - WJct. T.H. 71  
Ref. Pt. 087+00.050 - 091+00.359



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup> DIST
		TYPE	WIDTH	THICKNESS	
		Gravel	22'	2"	No Record of Constr. Added in 1934.
1934		Oil Tr. Gravel	25'	1 1/2"	1000 Gal./Mile. Maint. Dept.
M 1941	A.F.E. 15	Bit. Seal Coat	22'		RT-10, 3217 Gal./Mi. Sand 79 C.Y./Mi. Maint. Dept.
C 1950	2910-01	Grading Sand-Gravel Lift Gravel Surf.	34' 34' 26'	12" 2 1/4"	1200 C.Y./Mi. 350
C 1951	2910-05	Bit. Stab. upper 1" of Base in Place Mixed Bit.	27' 26'		Sealed under A.F.E. 4 RCS-1, 2516 Gal. Agg. 53 C.Y. 751
M 1955	A.F.E. 605	Light Bit. Seal	26'		RCS-2, 7097 Gal. Agg. 250 C.Y.
C 1956	2910-06	Plant Mix Bit.	24'	2" added	756
M 1964	c	Light Bit. Seal	25'		Bit. Mat'l, 6452 Gal. Agg. 252 C.Y.
C 1979	2900-03	THREE CABLE GUARD RAIL AT MP 87.4, 88, 88.4, 88.7			3488 L.N. Ft. 179
C 1986	2910-08	Grading, Base Bit. Surface Bit. Shoulders	30' 24' 8'	7 1/2" 4 1/2" 1 1/2"	CL 6A 3" 2331, 1 1/2" 2341 2331
S 2006	S05179 2910-09	Milling Bit Overlay Culvert Rplacmt	24' 24'	1 1/2" 3"	Spec. 2360
2013	8822-152	Bit. Seal Coat	26'		F2

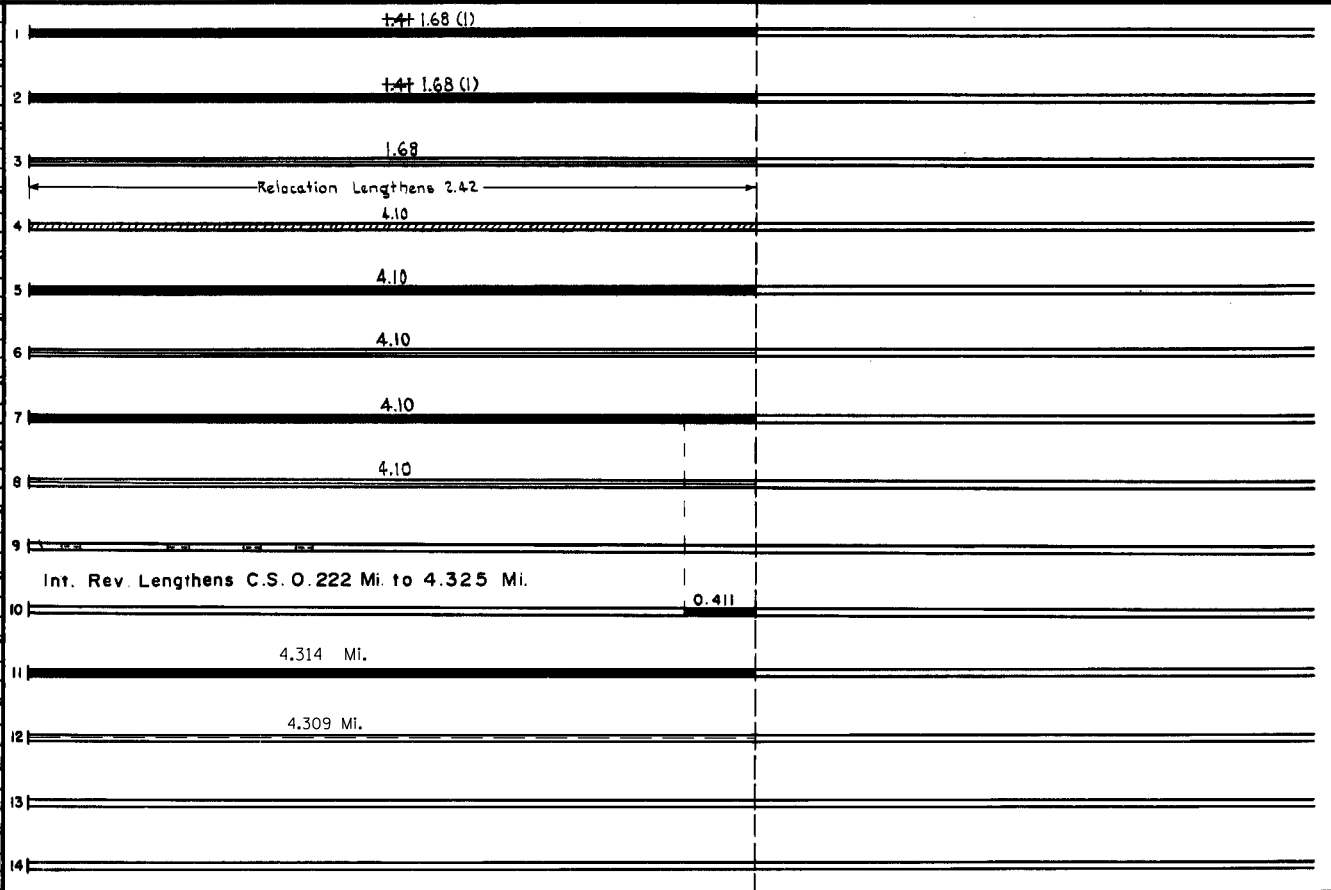

YEARS FROM TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934 1949	1.68	1.68	0.00	0.00	0.00	1.68	0.00	0.00	0.00
1950	4.10	4.10	0.00	0.00	0.00	4.10	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934  
(1) Mileage corrected on basis of letter from David Rose dated 9-17-43  
(2) Contract not final but work substantially complete in 1970.
