

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 314
TRUNK HIGHWAY 71
COUNTY Itasca
DISTRICT 2A

LIMITS: W. Co. Line near Funkley - N. Co. Line

REF. PT. 344-00.548 - 349-00.714

YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o DIST.
		TYPE	WIDTH	THICKNESS	
		Grading	22'		No Record of Constr.
1921		Gravel	22'	2"	Maint. Dept.
1931	71-4-458	Grading Gravel	28' 24'	2"	854 C.Y./Mile.
	(1)				
1932	71-4-458	Oil Tr. Gravel	24'	1"	12489 Gal./Mile. Maint. Dept.
	C	Revert Bit. Surf. to Gravel Surf.			See letter from David Rose dated 4-17-44.
	C	Bit. Surfacing (Blotter)			562,19077 Gal.
1946	A.F.E. 25	Bit. Surf-Treated	24'		
	C	Sand-Gravel Base	28'	10"	
1948	3114-03	Bit. Stab. Base (Mixed Bit.)	28'	2"	147
	C	Plant Mix Bit.	24'	2 1/2"	Stab. Gravel Shoulders 249
1949	3114-04				
	M	Bit. Seal Coat	25'		RC-5, 18400 Gal. Agg. 656 C.Y.
1957	A.F.E. 605				
	C	Plant Mix Bit	24'	1 1/2"	771
1971	3114-07				
	M	Spot Bit. Overlays	24'	1 1/2"	Pt. Mix 2331-537 Tons Total in C.S. 3114, 3610
1983	SF				
	C	GRADING BIT. SURFACING	28'	2" 1"	SPEC. 2331 SPEC. 2341
1990	3114-09				
	M	CRACK REPAIR			
1995	M95278				
	S	Bit. Overlay	28'	2"	Spec. 2360
2004	3114-13				

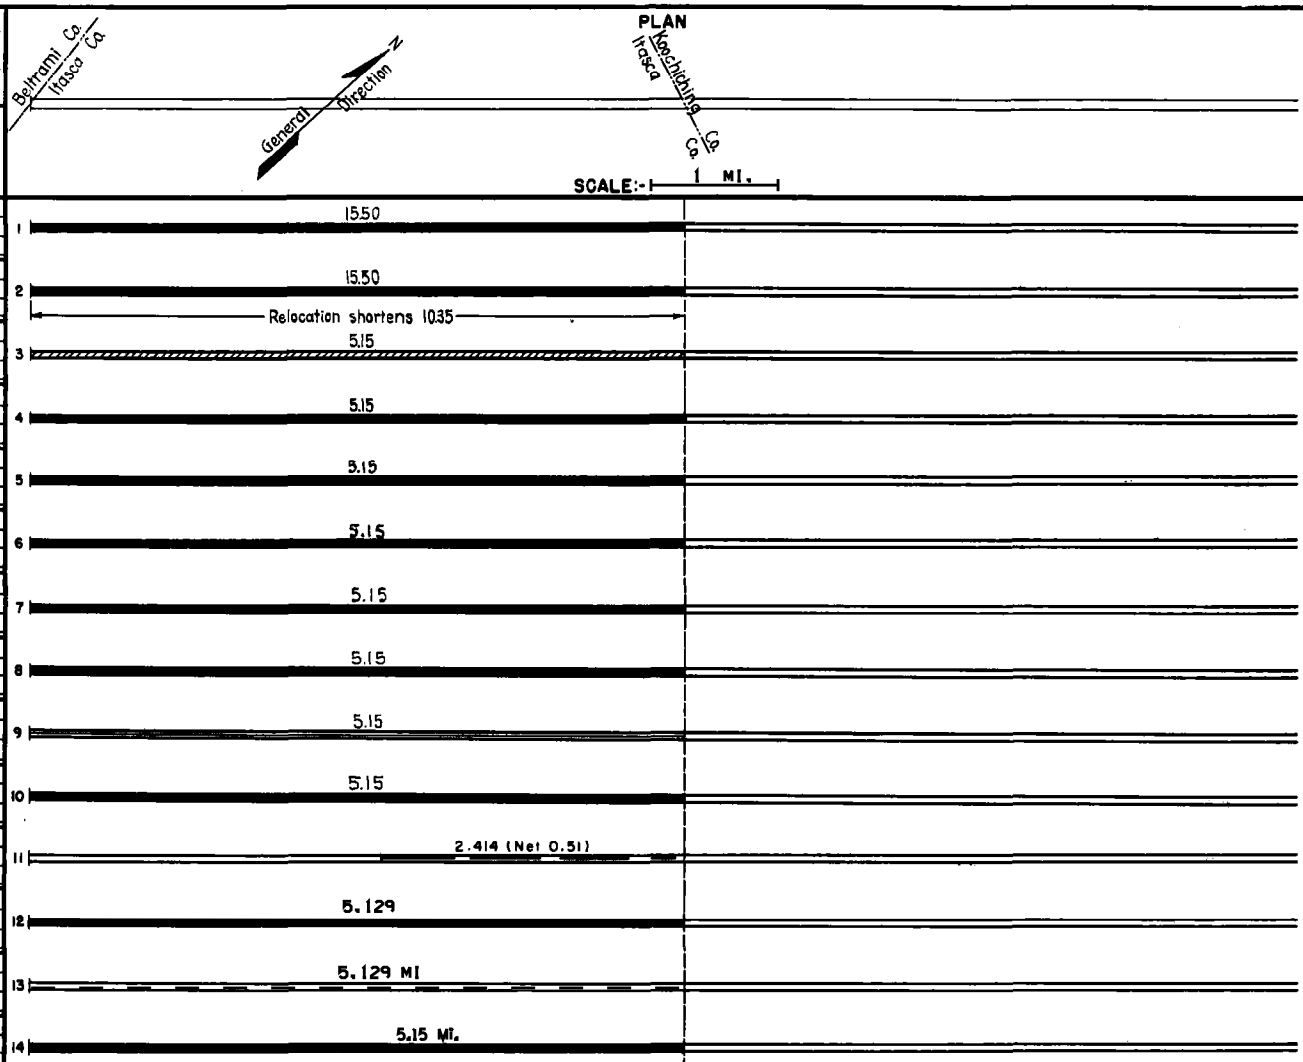

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1930	15.50	0.00	0.00	0.00	15.50	0.00	0.00	0.00	
1931		5.15	5.15	0.00	0.00	5.15	0.00	0.00	0.00	

REMARKS: Layout is to scale as of 1931.

(1) This work not done under this project number but lies within the limits of this project. (2) Actual date not reported. Assumed to be 1943.

