


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3413
TRUNK HIGHWAY 23
COUNTY Kandiyohi
DISTRICT 8A

LIMITS: N. Jct. T.H. 71 - Jct. T.H. 9

YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
		Gravel	22'	2"	No Record of Constr.
1932	71-4-44-2	Grading	40'		
1932	71-4-44-2	Oil Tr. Gravel	24'	1 1/2"	Maint. Dept.
1933	71-4-44-1	Grading Gravel Br. 5261 & 5267	40' 30' 27'	5"	3000 C.Y. / Mile. 143' B.S. O.H. & 99' B.S.
1934	71-4-44-1	CaCl ₂ Stab. Gravel	30'	2 1/2"	With Binder Soil. Method No. 1. Maint. Dept.
1935	71-4-44-1	Oil Tr. Gravel	24'	1 1/2"	Maint. Dept.
M	1941 A.F.E. 55	Frost Boils			Maint. Dept.
M	1941 A.F.E. 37	Spot Treat. Bit. Surf. Repair			Red. Oil 1314 Gal./Mi. Grav. 414 C.Y./Mi. Maint. Dept.
M	1943 A.F.E. 4	Bit. Surf. Repair			Oil 2223 Gal./Mi. Grav. 710 C.Y./Mi. Maint. Dept.
M	1947 A.F.E. 4 A.F.E. 5	Spot Treat. Bit. Surf. Repair & Bit. Seal Coat	24'		SC3 & RC3, 42, 58 Gal. Agg. 1511 C.Y.
M	1948 A.F.E. 4	Spot Treat. Bit. Surf. Repair	30'		MC-3, 4220 Gal. Agg. 236 C.Y.
M	1949 A.F.E. 4	Bit. Surf. Repair	26'		SC-3, 70204 Gal. Agg. 5796 Tons
M	1950 A.F.E. 4	Bit. Fog Seal	24'		RC-1, 12774 Gal. Agg. 310 C.Y.
C	1950 7412-08	Concrete	22'	9-7-9	

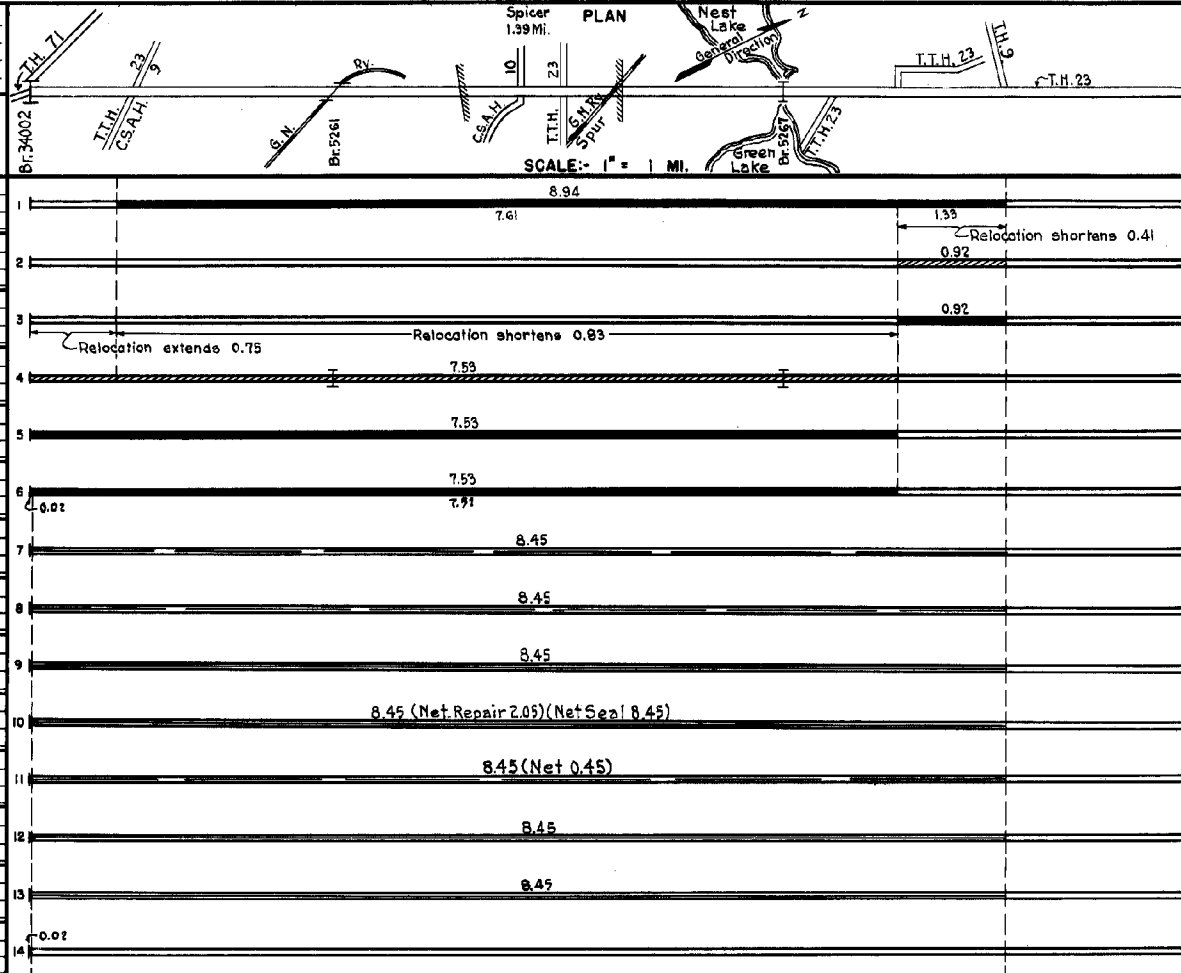

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1931	8.54	7.53	0.00	1.41	0.00	8.94	0.00	0.00	0.00
1932	1932	8.53	7.12	0.00	1.41	0.00	8.53	0.00	0.00	0.00
1933	1962	8.45	7.01	0.05	1.39	0.00	8.40	0.05	0.00	0.00
1963	1970	8.64	7.18	0.07	1.39	0.00	8.57	0.07	0.00	0.00
1971		8.62	7.16	0.07	1.39	0.00	8.55	0.07	0.00	0.00

REMARKS: Layout is to scale as of 1933.

(1) This work not done under these project numbers but lies within the limits of these projects.

