


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3603
TRUNK HIGHWAY 6
COUNTY Koochiching
DISTRICT JB

LIMITS: S. Co. Line - Jct. T.H. 71 in Big Falls



YEAR BUILT	PROJECT N ^o	DESCRIPTION			REMARKS	CODE N ^o
		TYPE	WIDTH	THICKNESS		
1931	6-61-23 B	Grading Gravel Br. 5030, 5029, 5044 (1)	28' 24'	2"	900 C.Y./Mile.	1
1934	6-61-23 B	Gravel	27'	3 1/4"	900 T/Mile.	2
	C					
1942	A.F.E. 35	Culvert			36" C.M. Maint. Dept.	3
	M					
1946	A.F.E. 6	Grav. Resurfacing	24'		4852 C.Y.	4
	M					
1947	A.F.E. 6	Grav. Resurfacing	24'		1224 C.Y.	5
	C					
1948	A.F.E. 19	Bit. Surfacing Mixed Bit (Mixed Prime)	24'	1 1/4"	SC-3, 17132 Gal. Agg. 692 C.Y. new # 358 C.Y. from Base	6
	M					
1949	A.F.E. 6	Grav. Resurfacing (Spots)	24'		2000 C.Y.	7
	M					
1951	A.F.E. 6	Grav. Resurfacing (Spots)	24'		3011 C.Y.	8
	C					
1953	3603-02	Sand-Grav Subbase Bit. Stab. Base Plant Mix Bit	28' 28' 24'	6" 3-6" 1 1/2"		9
	M					
1956	A.F.E. 605	Light Bit. Seal	24'		RC-2, 40370 Gal. Agg. 1512 C.Y.	10
	C					
1964	Br. Crew	(Raise Portals) Br. 5029 Br. 5030			Increase Vertical Clearance to 16'	11
	M					
1970	SF	Bit. Surf. Repair	24'	1"	MC-250 tack, 125 Gal Agg. 233 Tons	12
	C					
1974	3603-04	Bit. Overlay Gravel Shoulders	24'	1 1/2"		13
	C					
1977	3603-07	Temp. By Pass Br. Br. # 99012	24'		Per Repl. of Br. 5030 24' SBS	14

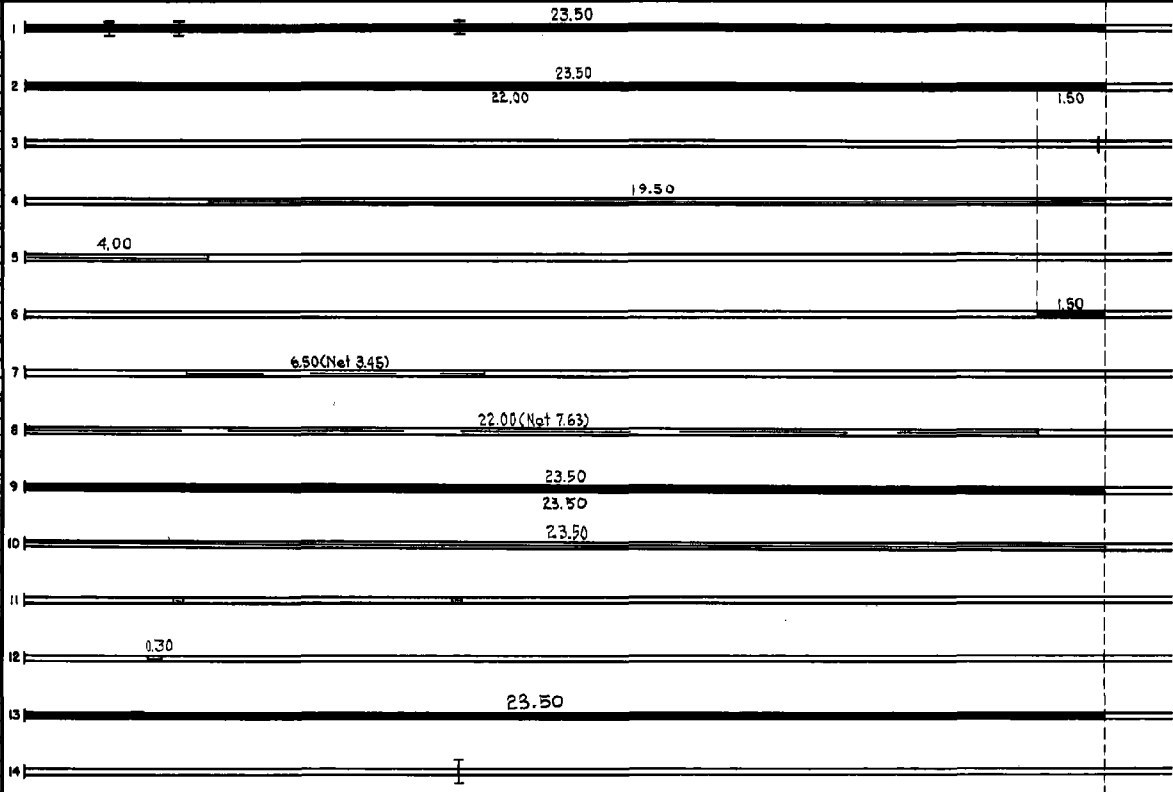

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1931		23.50	22.12	0.09	1.29	0.00	23.41	0.09	0.00	0.00

REMARKS: Layout is to scale as of 1931
(1) Br. # 5030, 210' x 17' (150' H.T., 2-30' B.S.) - Br. # 5029, 210' x 17' (150' H.T., 2-30' B.S.) - Br. # 5044, 30' x 23' B.S.

10-74

