


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4908
TRUNK HIGHWAY 115
COUNTY Morrison
DISTRICT 3A

LIMITS: Jct. T.H. 10 in Randall - Jct. T.H. 371



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
		Earth	16'		No Record of Constr. Added in 1934.
		Br. 1987	23'		45' C.D.G.
1934	115-131-21-1	Grading	32'		
		Gravel	24'	2"	900 C.Y./Mile
1934		Oil Tr. Gravel	24'	1"	Maint. Dept. Equip. & Army Labor. & Material.
1934		Tar Tr. Gravel	30'	1"	(1)
		Br. 4969	24'		410' D.P.G.
1936	A.F.E. 17	Roadside Development			By W.P.A. Supervision by Maint. Dist. 17
1937	A.F.E. 33	Grade Lift			
		Mixed Bit. Surface	30'	1"	Maint. Dept.
1937	1937 A.F.E. 12	(2)			
		Grading	32'		
		Gravel Surface	32'	1 1/2"	Maint. Dept.
1939	Dist 17 A.F.E. 7	Roadside Development			By W.P.A. Supervision by Dist. 17 & 4.
1940	A.F.E. 47	Mixed Bit Surface	18 1/2'	1 1/2"	Traveling Plant.
	1941 A.F.E. 45				Maint. Dept.
1940	A.F.E. 39	Bit. Retreat	24 1/2'		RF-6, 7815 Gal./Mi. Grav. 560 C.Y./Mi. Maint. Dept.
1941	A.F.E. 25	Spot Treat.			SC-3, 89 Gal./Mi.
		Bit. Surf. Repair	28 1/2'		Maint. Dept.
1941	A.F.E. 36	Bit. Seal Coat	25'		RC-3, 3917 Gal./Mi. Agg. 128 C.Y./Mi. Maint. Dept.
1947	A.F.E. 4	Bit. Fog Seal			RC-3, 9463 Gal.
1948	A.F.E. 21	Bit. Resurfacing			AE-3, 5638.478045 Gal.
		Mixed Bit.	24 1/2'	1"	Agg. 6345 tons

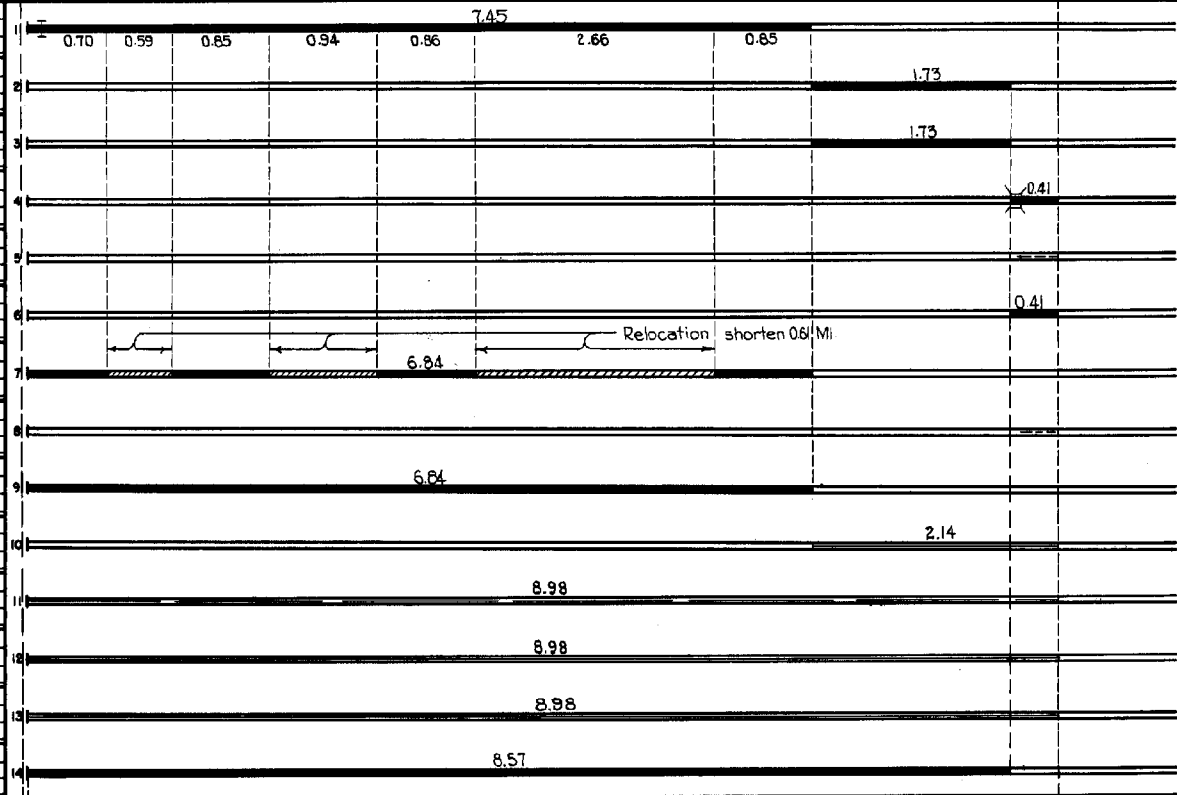

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1936	9.59	8.64	0.08	0.86	0.01	9.51	0.08	0.00	0.00
1937	1958	8.98	8.04	0.08	0.85	0.01	8.89	0.09	0.00	0.00
1959		9.16	8.04	0.68	1.03	0.01	9.07	0.09	0.00	0.00

REMARKS: Layout is to scale as of 1937.

(1) Maint. Dept. equipment & Army labor & material.

(2) Exception to grading from Jct. T.H. 10 to 0.45 Mi. east. Grade and surface width on the 0.45 Mi. is 18' wide.

