


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 5611  
TRUNK HIGHWAY 24  
COUNTY Otter Tail  
DISTRICT 4A

LIMITS: W. Co. Line - Jct T.H. 59  
Ref. Pt. 011+00.758 - 018+00.862



YEAR BUILT	PROJECT N°	DESCRIPTION				CODE N°
		TYPE	WIDTH	THICKNESS	REMARKS	
		Gravel	24'	1"	No Record of Constr.	
1924		Grading	24'		Co. Job 2401	
		Gravel	24'	2 1/2"	1200 C.Y./Mile Added in 1934.	
M 1940	A.F.E. 32	Regraveling			Grav. & Clay 332 C.Y./Mi. Maint. Dept.	7.32
M 1942	A.F.E. 6	Regraveling & Consolidation			Grav. & Binder Soil 255 C.Y./Mi. Maint. Dept.	7.32
M 1947	A.F.E. 6	Grav. Resurfacing (Spots)			1835 Tons	7.32 (Net 6.82)
C 1951	5611-04	Grading	32'			Alignment changes & relocation shorten 0.19
		Gravel	28'	1 1/2"	1200 C.Y./Mi.	7.13
		Ext. 2' H&B Culvs.				
C 1952	5611-05	Gravel Base	28'	3-9"		7.13
		Mixed Bit	26'	1"		
M 1955	A.F.E. 605	Light Bit. Seal	26'		AE RS-2, 16490 Gal. Agg. 540 C.Y.	7.13
C 1957	5611-06	Plant Mix Bit.	24'	2 3/4" added		7.13
M 1959	A.F.E. 605	Light Bit. Seal	25'		RC-2, 12287 Gal. Agg. 441 C.Y.	7.13
M 1963		Spot Treat Bit. Surf. Repair	24'	1"	Bit. 2290 Gal. Agg. 219 Tons To Ex 300 Gal.	0.63 (Net 0.30)
C 1977	5611-09	Mix Bit. Surf.	24'	3"		7.096
		GRAY SHOULDERS	6'			
		TURN LANES				
M 1990	SF	Spot Overlay		1 1/2"	Spec. 2341	0.090
C 1997	5611-09	Milling Bit. Overlay	28'	2"		7.104 MI
			28'	Var.	Spec. 2341	

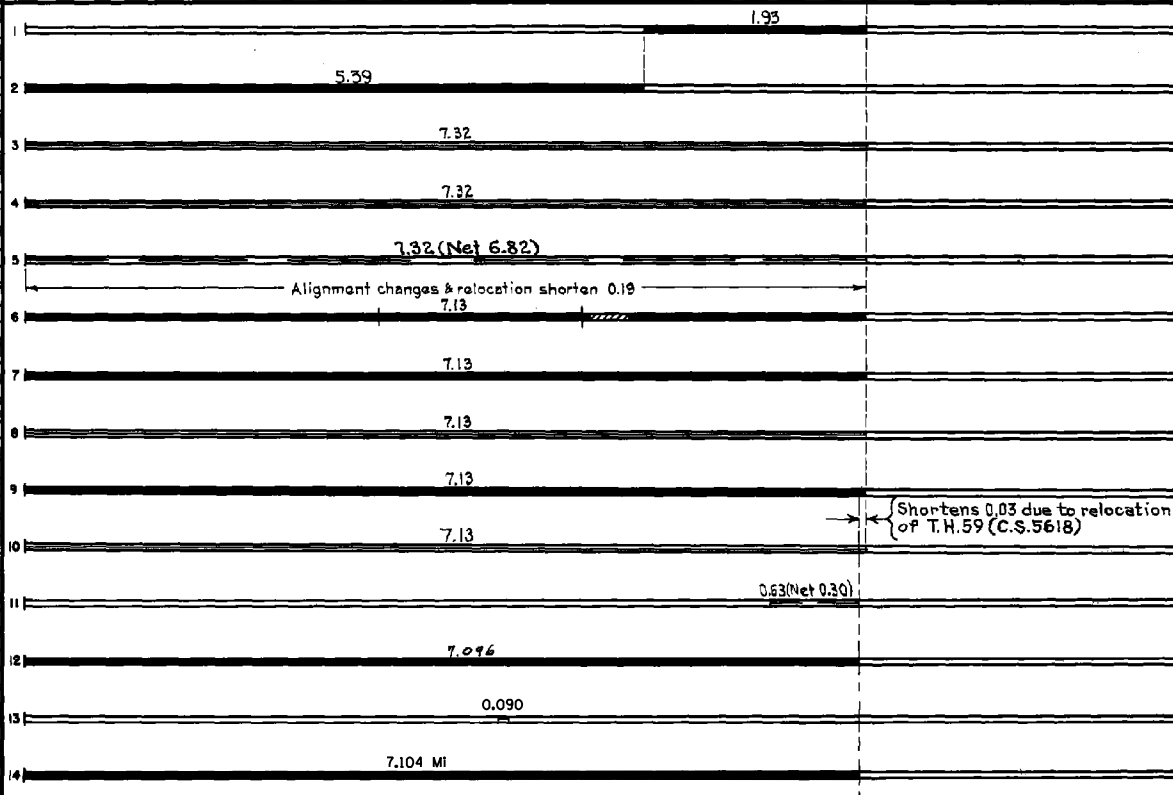

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED			INCORPORATED			RURAL		URBAN	
			RDWY. MI.	BR. MI.	BR. MI.	RDWY. MI.	BR. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1950	7.32	7.32	0.00	0.00	0.00	7.32	0.00	0.00	0.00		
1951	1966	7.13	0.00	0.00	0.00	0.00	7.13	0.00	0.00	0.00		
1967		7.10	7.10	0.00	0.00	0.00	7.10	0.00	0.00	0.00		

REMARKS: Layout is to scale as of 1934.

