

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 5619  
TRUNK HIGHWAY 18  
COUNTY Otter Tail  
DISTRICT 4A

LIMITS: S. Co. Line ~ Jct. T.H. 210



YEAR BUILT	PROJECT N°	DESCRIPTION				CODE N°
		TYPE	WIDTH	THICKNESS	REMARKS	
		Gravel	21'	1 1/2"	No Record of Constr. Added in 1934.	
M 1940	A.F.E. 25	Regravelling			236 C.Y./Mile. Maint. Dept.	
M 1940	A.F.E. 38	Grade Lifts.			957 C.Y./Mile. Maint. Dept.	
M 1942	A.F.E. 6	Regravelling			300 C.Y./Mile. Maint. Dept.	
C 1942	5619-02	Grading Stab. Gravel	34' 3/8"		1300 C.Y./M.	
C 1942	A.F.E. 7	Seeding			Seeds supplied by R.S.D.(S.P. 5619-03) Maint. Dept.	
C 1947	A.F.E. 23 A.F.E. 21	Gravel Lift (Spot) Bit. Surfacing Mixed Bit.	28' 24'	1"	MC3, 48225 Gal. Agg. 2164 Tons	
M 1951	A.F.E. 4	Light Bit. Seal	24'		RC3, 4268 Gal. Agg. 113 C.Y.	
C 1952	5619-06	Grading Gravel	32' 5/8" 26'	1"	0.69 Mi. Divided Highway 700 C.Y./M.	
M 1953	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		MC3, 5800 Gal. Agg. 334 C.Y.	
C 1954	5619-07	Grading Gravel	32' 26'	1 1/4"	700 C.Y./M.	
C 1955	5619-04	Stab. Sand-gr. Sub-base Stab. Gravel Base Plant Mix Bit	23' 3/8" 23' 5/8" 24' 3/8"	0-9" 3" 1 1/2"		
M 1956	A.F.E. 605	Light Bit. Seal			RS-2, 19994 Gal. Agg. 753 C.Y.	
M 1964	SF	Spot Base Repair Restore Bit. Surf.	30' 24'		Base 13770 Tons Road Mix 930 Tons	

Otter Tail Co.  
Douglas Co.

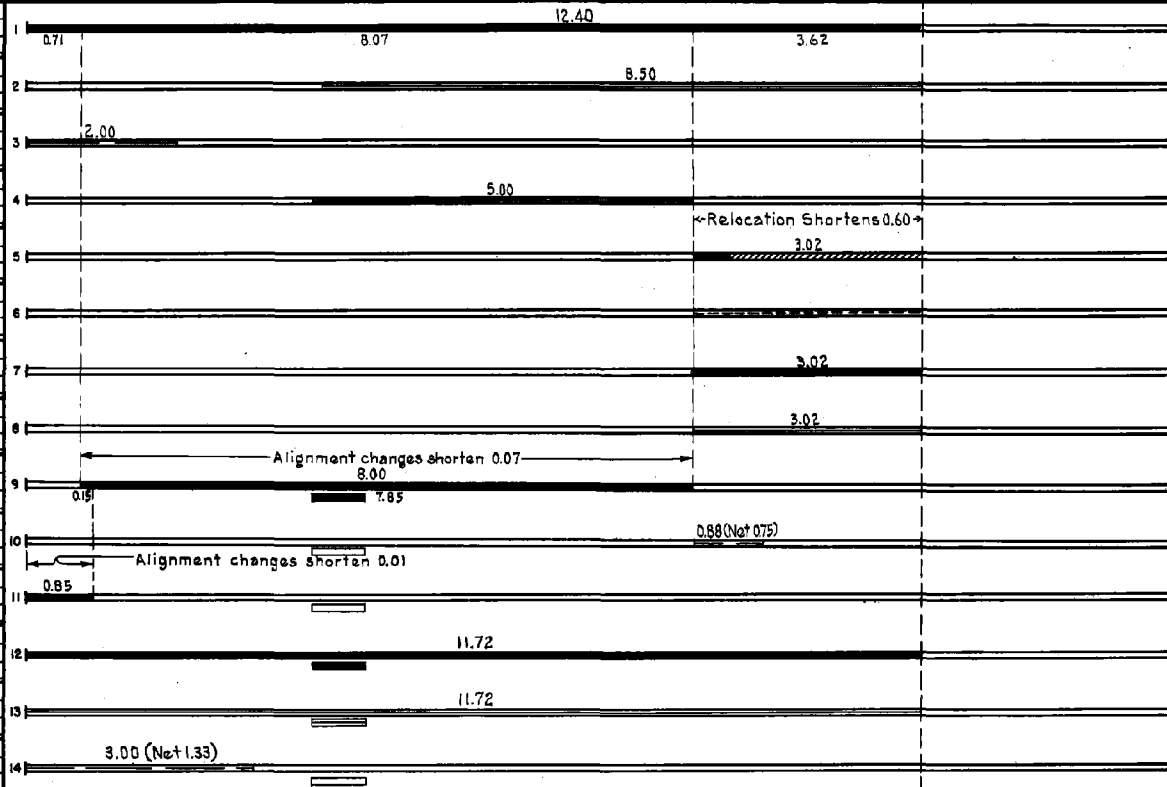

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1942	1941	12.40	12.40	0.00	0.00	0.00	12.40	0.00	0.00	0.00
1942	1941	11.80	11.80	0.00	0.00	0.00	11.80	0.00	0.00	0.00
1952	1951	11.73	11.73	0.00	0.00	0.00	11.73	0.00	0.00	0.00
1954		11.72	11.72	0.00	0.00	0.00	11.72	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1942.

