


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 5812
TRUNK HIGHWAY 107
COUNTY Pine
DISTRICT 1A

LIMITS M. Co. Line - Jct. T.H. 23



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	1 1/2"	No Record of Const. Added in 1934.
1919	Br. 7193 Br. 3025		17'	17'	Added in 1934. 30' C.T.G. 40' Concrete Slab.
M 1940	A.F.E. 58	Spot Graveling			Maint. Dept.
C 1944	A.F.E. 17	Install Culvert			36' x 36' S.C. Maint. Div.
M 1948	A.F.E. 6	Grav. Resurfacing			13,380 C.Y.
C 1952	5812-02	Grading Stab. Sand Mat. Gravel	34' 34' 24'	12" 1 1/2"	C86 & C108 + 30°
C 1953	5812-04	Bit. Stab. Base (Mixed Bit)	26'	2"	
M 1953	A.F.E. 640	Spot Treat. Bit. Surf. Repair Spot Light Bit. Seal	24' 24' 24'		RT-4, 13550 Gal. Agg. 990 Tons
M 1954	A.F.E. 827 A.F.E. 605	Spot Base Repair Spot Surf. Repair Light Bit. Seal (6.00MI)	30' 24' 24'		SC-4 & MC-3, 49477 Gal. Agg. 2128 Tons & 342 C.Y.
M 1955	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24' 24'		SC-4, 4681 Gal. Agg. 392 Tons
M 1956	A.F.E. 604	Spot Treat. Bit. Surf. Repair Lift (0.02MI)	24' 24'		SC-4, 33640 Gal. Agg. 2755 Tons
M 1957	A.F.E. 605	Light Bit. Seal	25'		RC-2, 18769 Gal. Agg. 714 C.Y.
M 1958	A.F.E. 821 A.F.E. 604	Spot Grade Lifts Spot Treat. Bit. Surf. Repair	24' 24'		SC-4, 8205 Gal. Agg. 714 Tons
M 1959	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		5305 Gal. Bit. Agg. 455 Tons

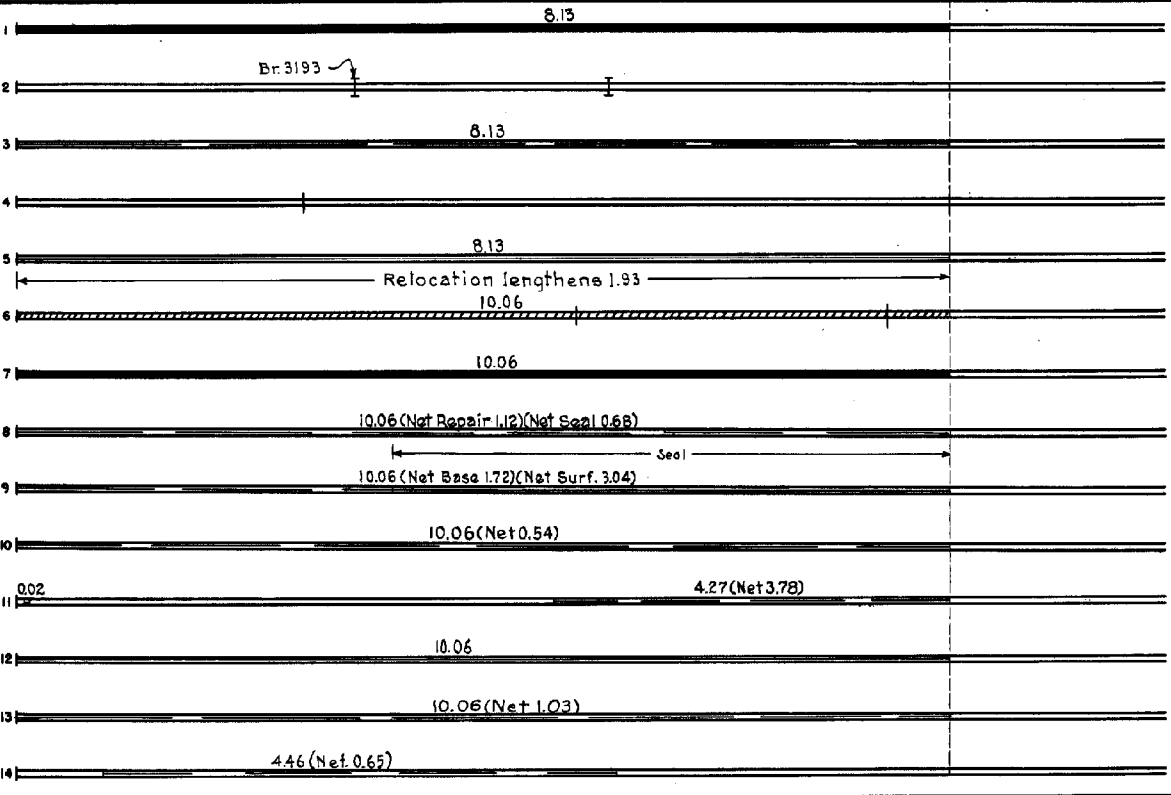

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1951	8.13	8.12	0.01	0.00	0.00	8.12	0.01	0.00	0.00
1952		10.06	10.06	0.00	0.00	0.00	10.06	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934. Plan revised for 1952 relocation.

