


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 5903
TRUNK HIGHWAY 30
COUNTY Pipestone
DISTRICT 8B

LIMITS: W. State Line - W. Jct. T.H. 75 in Pipestone



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	2"	No Record of Constr.
					Added in 1934
1934	47-89-21-1	Grading	32'		10" Sand Lift.
		Gravel	29'	2"	1700 Tons/Mile.
		Br. 5386 & 6112	27'		60 B.S. & W106 D.
1934	47-89-21-1	Tar Tr. Gravel	24'	2"	Road Mix.
					1" Base Course & 1" Wearing Course
1935	47-89-21-2	Grading	32'		
		Gravel	28'	2"	2000 C.Y./Mile.
		Sand Lift	5'-10"		
	(1)				
1935	47-89-21-2	Tar Tr. Gravel	22'	2"	9000 Gal./Mile.
					Maint. Dept.
1937	47-89-21-3A	Grading	W/W		8" Sand Lift.
		Gravel	W/W	2"	2600 C.Y./Mile.
		Br. 5449	40'		Underpass.
1937	47-89-21-2B & 3A	Concrete	40'		
	(2)				
1937	47-89-21-3A	Concrete	40'		Divided Highway
M	1943 A.F.E. 4	Bit. Fog Seal			RC3, 1387 Gal./Mi.
		(3 spots)			Grav. 43 C.Y./Mi.
					Maint. Dept.
M	1945 A.F.E. 5	Patching & Bit. Seal Coat			5G3 & RC3, 2887 G./Mi.
					Grav. 86 C.Y./Mi.
					Maint. Div.
M	1947 A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		MC-3, 7225 Gal.
					Agg. 469 Tons
C	1948 A.F.E. 19	Spot Grav. Lifts Bit. Resurfacing Mixed Bit.	30' 6" 12" 24' 1" added		MC-3, 80715 Gal.
					Agg. 4834 Tons
M	1949 A.F.E. 4	Bit Fog Seal	24'		MC2, 8532 Gal.
					Agg. 200 C.Y.
M	1952 A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		MC-2, 5935 Gal.
					Agg. 276 C.Y.

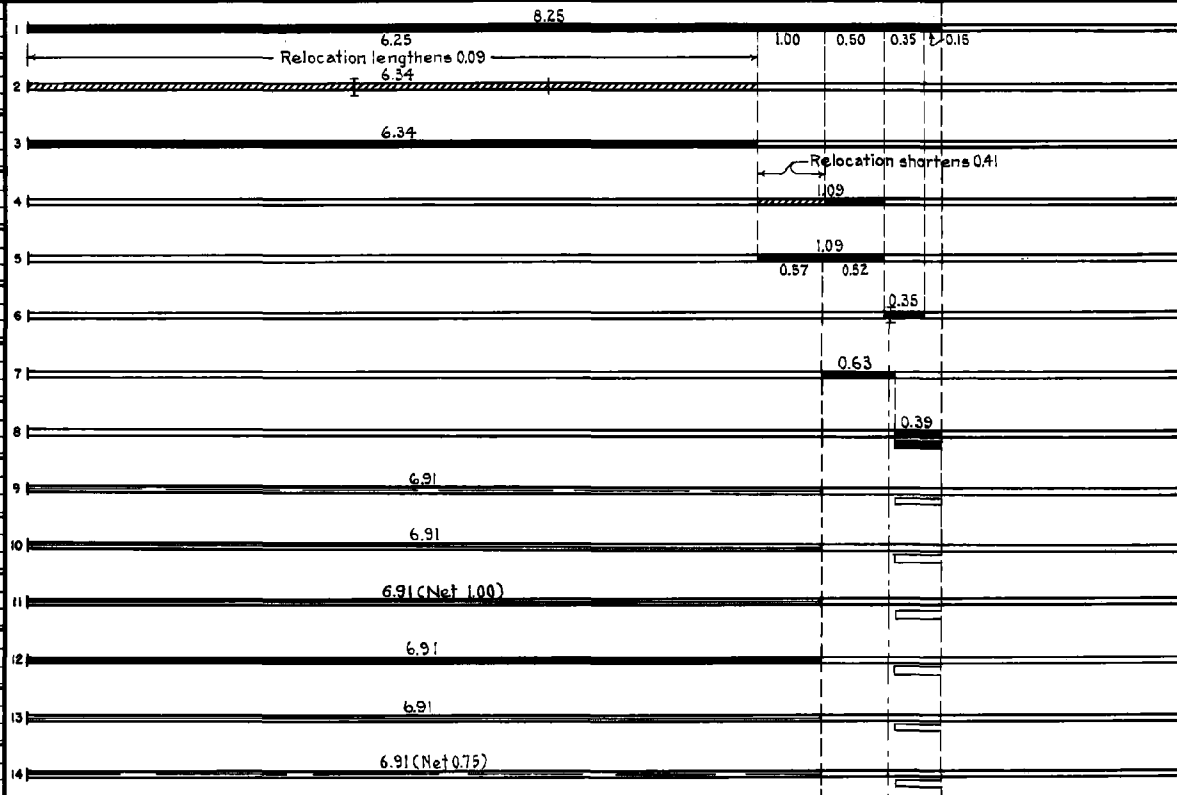

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1934	8.25	6.25	0.00	2.00	0.00	5.25	0.00	2.00	0.00
1934	1934	8.34	6.33	0.01	2.00	0.00	5.33	0.01	2.00	0.00
1935	1938	7.93	7.28	0.01	0.64	0.00	7.28	0.01	0.64	0.00
1939	1960	7.93	7.22	0.01	0.70	0.00	7.22	0.01	0.70	0.00
1961	1962	7.93	6.71	0.01	1.21	0.00	6.71	0.01	1.21	0.00
1963	1973	7.93	6.89	0.01	1.03	0.00	6.89	0.01	1.03	0.00
1974	1974	7.93	6.83	0.01	1.09	0.00	6.83	0.01	1.09	0.00

REMARKS: Layout is to scale 2" = 100'

(1) This work not done under this project number but lies within the limits of this project (2) Each Roadway has a 20' concrete strip.

