

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 6109
TRUNK HIGHWAY 104
COUNTY Pope
DISTRICT 4B

LIMITS: S.Co. Line-Jct.C.S.A.H.21 (N. End of Curve)

Ref. Pt. 018+00.435 - 025+00.059

Swift Co.

Pope
Kandiyohi Co.



PLAN

CSA.H.
0

0


CSA.H.
0

0



SCALE: 1" = 1 MI.

YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	1 1/2"	No Record of Const. Added in 1934.
C 1941	A.F.E. 43 A.F.E. 59	Grading & Culv. Seeding			Seed supplied by R.S.D.(S.P. 6109-03) Maint. Dept.
C 1941	A.F.E. 58	Gravel			640 C.Y./Mile. Maint. Dept.
M 1941	A.F.E. 58	Spot Graveling			260 C.Y./Mile. Maint. Dept.
M 1945	A.F.E. 6	Grav. Resurfacing			342 C.Y./Mi. Maint. Dept.
M 1946	A.F.E. 50	Grade Lift	24' 3.0"		3010 C.Y.
M 1951	A.F.E. 6	Grav. Resurfacing (Spot)			822 C.Y.
M 1952	A.F.E. 6	Grav. Resurfacing			816 C.Y. & 294 Tons
C 1954	6109-07	Grading Gravel	26'	1 1/2"	700 C.Y./Mi.
C 1955	6109-08	Stab. Sand-Gr. Sub-base Stab. Gravel Base Plant Mix Bit.	30' 30' 24'	0'-6" 3" 1 1/2"	
M 1956	A.F.E. 605	Bit. Seal Coat	24'		RC-5, 25455 Gal. Agg. 714 C.Y.
M 1963		Light Bit. Seal	25'		RS-2K, 12140 Gal. Agg. 412 C.Y.
M 1990	4381	Bit. Overlay Bit. Shouldering	24' 2'	1 1/2" 1 1/2"	Spec 2341

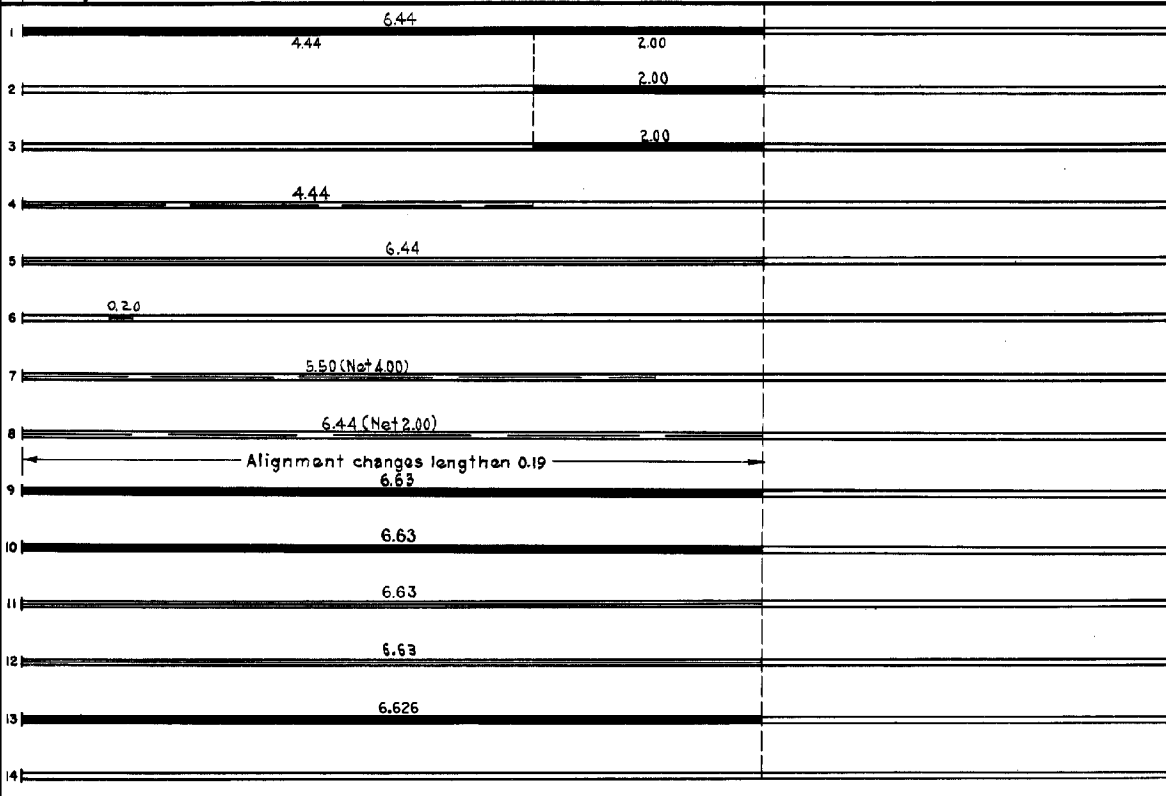

YEARS FROM TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.
1934 1952	6.44	6.44	0.00	0.00	0.00	6.44	0.00	0.00	0.00
1954	6.63	6.63	0.00	0.00	0.00	6.63	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934

