


PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6410
TRUNK HIGHWAY 68
COUNTY Redwood
DISTRICT 7B

LIMITS: Jct. T.H. 67 in Morgan to E. Co. Line
Ref. Pt. 086+00.924 - 091+00.198



YEAR BUILT	PROJECT NO	DESCRIPTION			
		TYPE	WIDTH	THICKNESS	REMARKS
C	6406-07	Sand-Grav Sub-base Gravel Base Plant-Mix Bit	30'-6"	6" 3" 1 1/2"	Except where base is in place (See foot-note (1))
C	6406-11	Sand-Grav Sub-base Bit-Grav Base Plant Mix Bit	32' 32' 24'	5" 4" 2"	
M	1953	Light Bit. Seal	25'		RS-2K, 7767 Gal. Agg. 319 C.Y.
C	6410-02 (2)	Grading Plant mix Bit. Gravel Shoulders	24-56'	3'-4"	Rt. & Lt. of rdwy. Imp. 2 1/2' Rt. & Lt.
M	1967	C Light Bit. Seal	24'		CRS-1, 9907 Gal. FA-1, Agg. 272 C.Y.
M	1978	SF Bit. Spot Overlay		1 1/2"	Pl. Mix AC
M	1983	SF Bit. Overlay		1 1/2"	Pl. Mix 2331
M	1984	SF Chip Seal Coat	50'		CRS-2 B Quartzite
M	1986	SF Bit. Sealing			
M	1988	SF Bit. Overlay	24'	1 1/2"	Spec. 2341
M	1989	4335 Bit. Overlay	24'	1 1/2"	Spec. 2331
M	1989	SF Crack Repair			
M	1991	4495 Bit. Overlay	24'	1 1/2"	Spec. 2331
M	1998	6410-04 Milling Bit. Overlay	Var. 24'	1 1/2"	Spec. 2350

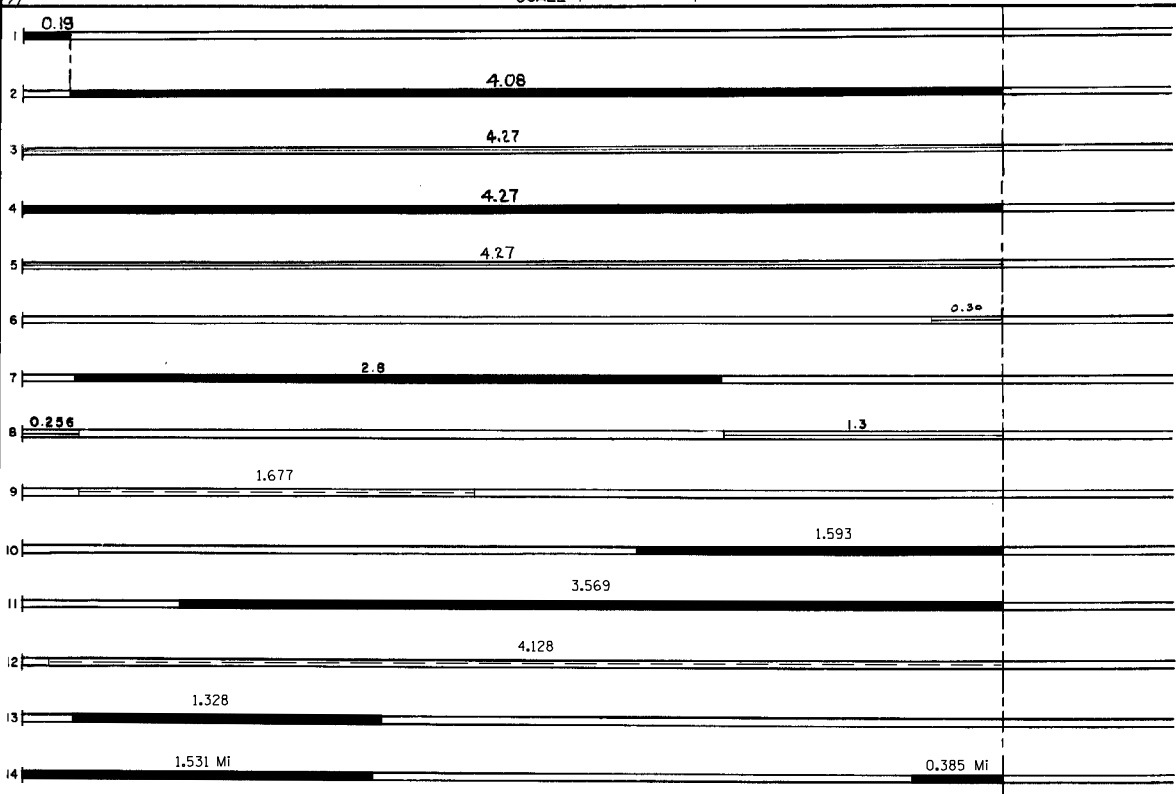

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1961		4.27	3.45	0.00	0.82	0.00	4.27	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1/8"
(1) The Gravel is 9" Thick in Morgan
(2) Portion of project in Morgan from Jct. T.H. 67 to 0.19 mi. S.E. graded for full width of rdwy. & sub-base & base construction.
