




PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6917  
TRUNK HIGHWAY 53  
COUNTY St. Louis  
DISTRICT 1A-18

LIMITS: Jct. T.H.33-N.Jct.T.H.37 E. of Eveleth



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
M	1940 & 1941	Special Maint. Should. & Drainage)			
1941	A.F.E. 28				Maint. Dept.
C	1944	Bit. Resurfacing Mixed Bit. on old concrete	22'	2"	MC2,12267 Gal./M. Agg. 844 C.Y./Mi. Maint. Div.
C	1945	6917-13	Bit. Concrete Plant Mix (1)	21'	1 1/2 2 1/2"
C	1946	6917-15	Br. 3249	29'	30' C.D.G.
	A.F.E. 21		Br. 3245	29'	30' C.D.G. Widening
C	1945 & 46	A.F.E. 18	Ch. Change & Culv. Reshaping & Grav. Shoulders & Seeding		Remove Br. 3246 & 3248 Spots
C	1947	6917-14	Gravel Base (2)	30'	5"
	6917-20	Plant Mixed Bit. Widen 3 Bridges	22'	1 1/2"	Br. 3241 " " 40' Br. 3244 " " 36'
M	1949	A.F.E. 4	Bit. Fog Seal	21/22'	Agg. 1035 C.Y.
M	1951	A.F.E. 17	Spot Treat. Bit. Surf. Repair	24'	MC44564, 4180 Gal. Agg. 264 C.Y.
C	1952	6917-23	Plant Mix Bit.	22'	2" added
C	1953	6917-17	Br. 6603	30'	40' C.D.G.
M	A.F.E. 604	Spot Treat.			Bit. 144 65 Gal. Agg. 1106
1953	A.F.E. 605	Bit. Surf. Repair	6'		Tons. Pl. Mix 2642 Tons
	A.F.E. 823	Spot Bit. Seal Coat	3/20'		A.F.E. 821 (3)
C	1954	6917-27	Grading Bit. Stab. Base Plant Mix. Bit.	30'	Approaches to Br. 6604 On 18" min. Grav. Sub-base
C	1954	6917-16	Br. 6604	30'	134 B.S.
	6917-18	Br. 6602	30'	182 B.S.	
C	1954	6917-30	Plant Mix Bit.	22'	3 3/4" On old conc. - old iron blocks removed

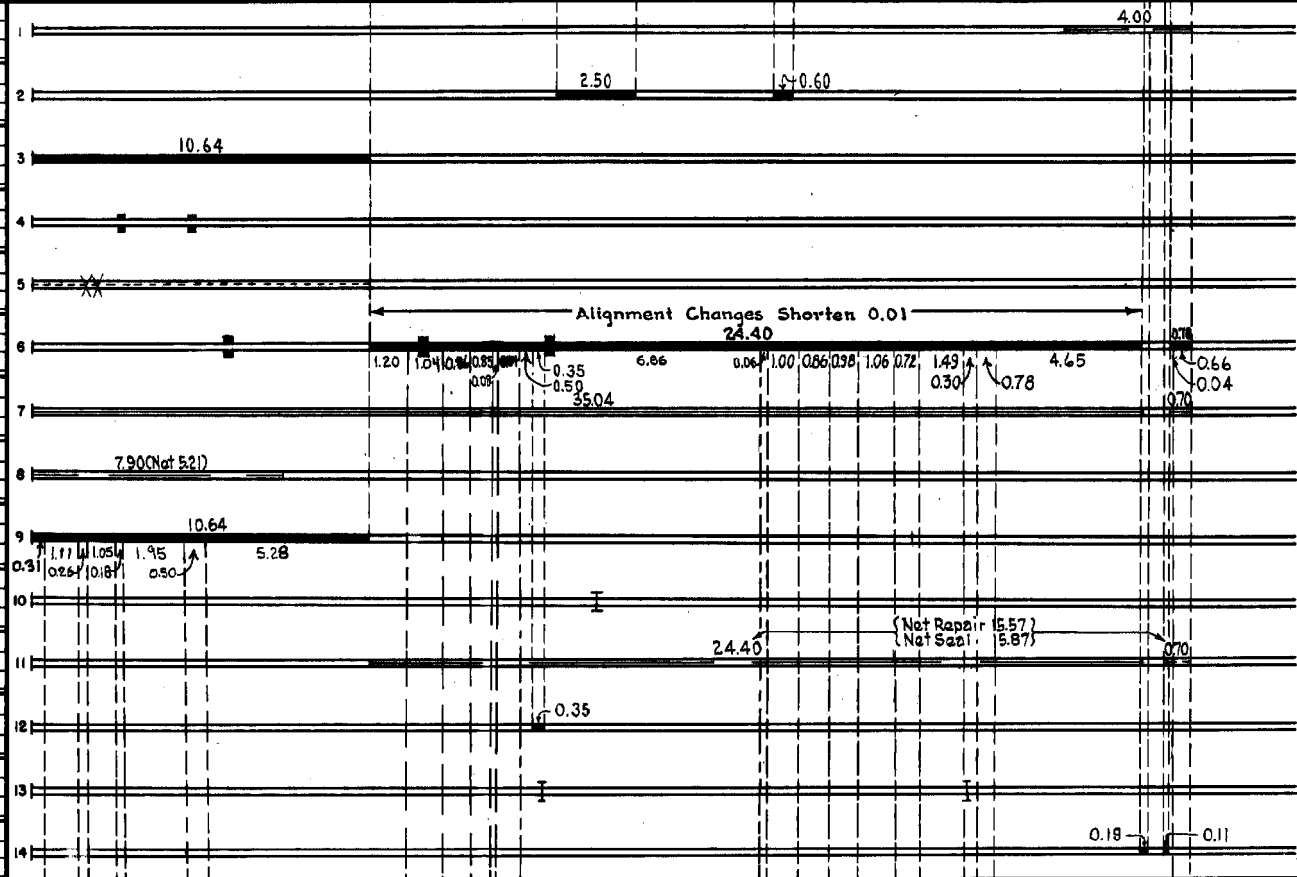

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.


REMARKS: See Sheet No. 1  
 (1) Approx. 43% of this 10.64 mi. is Plant Mixed Bit. on a variable gravel lift, the balance being Plant Mixed Bit. on the old P.C. Concrete. (2) 5" Gravel Base over old 1 1/2" P.C. Concrete  
 (3) A.F.E. 821 covers 0.35 mi. egg repairs. (4) Contract not final but work substantially complete

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6917  
TRUNK HIGHWAY 53  
COUNTY St. Louis  
DISTRICT 1A-1B

LIMITS: Jct. T.H.33-N.Wet.T.H.37 E. of Eveleth



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
C	1955 6917-29	Bit. Stab. Base	40'	6"	On 12" Sand-Gr. Sub-base
	6917-19	Plant Mix Bit.	24'	3"	250' D.T. & B.S.
M	1956 A.F.E. 605	Light Bit. Seal (0.31 Mi)	24'		MC-2 & RC-2, 550 Gal.
	A.F.E. 617	Sag Repair (0.20 Mi)	24'		Agg. 35 C.Y. Bit. Mix 105 Tons
M	A.F.E. 605	Light Bit. Seal (7.9 Mi)	23'		RC-2 & MC-2, 12433 Gal.
	1958 A.F.E. 604	Spot Treat			Agg. 52.5 C.Y.
		Bit. Surf. Repair			Plant Mix 1438 Tons
M	1959 A.F.E. 604	Bit. Surf. Repair			Plant Mix 397 tons
C	6917-32	Grading Base	294'		Divided Highway
	1960 6917-38	Grading Road Mix Bit.	274'		
	6917-37	Br. 9530			214' C.G.S.-U.P.
C	6917-35	Br. 9481			220' P.C.S.-U.P.
	1960 6917-36	Br. 9482			170' B.S.-U.P.
C	1961 6917-44	Road Mix Bit. Base	226'	1 1/2"	
C	1961 6917-41	Grading Gravel Base			Divided Highway
		Road Mix Bit. Base	226'	1 1/2"	
		Br. 9493 & 9494	230'		Both 146' P.C.S.-O.H.
M	1961	Bit. Surf. Repair	5-7'	1/2"-3"	on edges of Surf. 172 Tons Pl. Mix Bit.
C	6917-45	Grading			Divided Highway
	1963 6917-51 (1)	Sub-base, Base			New S.B. rdwy. & portions of N.D. rdwy.
		Bit & Concrete	428'		
C	6917-69021	Br. 69021	2-29'		187' B.S.-O.H.
	1963 6917-69020	Br. 69020	30'		178' B.S.-O.H.
C&M	1963 6917-49	Asphaltic Conc.	2-24'	4"	
		Spot Bit. Surf. Repair	6'	1 1/2"	Edges of Surf. imp.
C&M	1964 6917-50	Lighting System			at N. Jct. T.H.37
	S.P.	Bit. Surf. Repair			Pl. Mix 442 C.Y.
	C	Light Bit. Seal	23'		Bit. 26607 Gal. Agg. 1169 C.Y.
C	1965 6917-54	Plant Mix Bit. Surfacing	4852'	4"	2824'-4.18 mi., 2826'-0.73 mi.
		Bit. Shoulders			

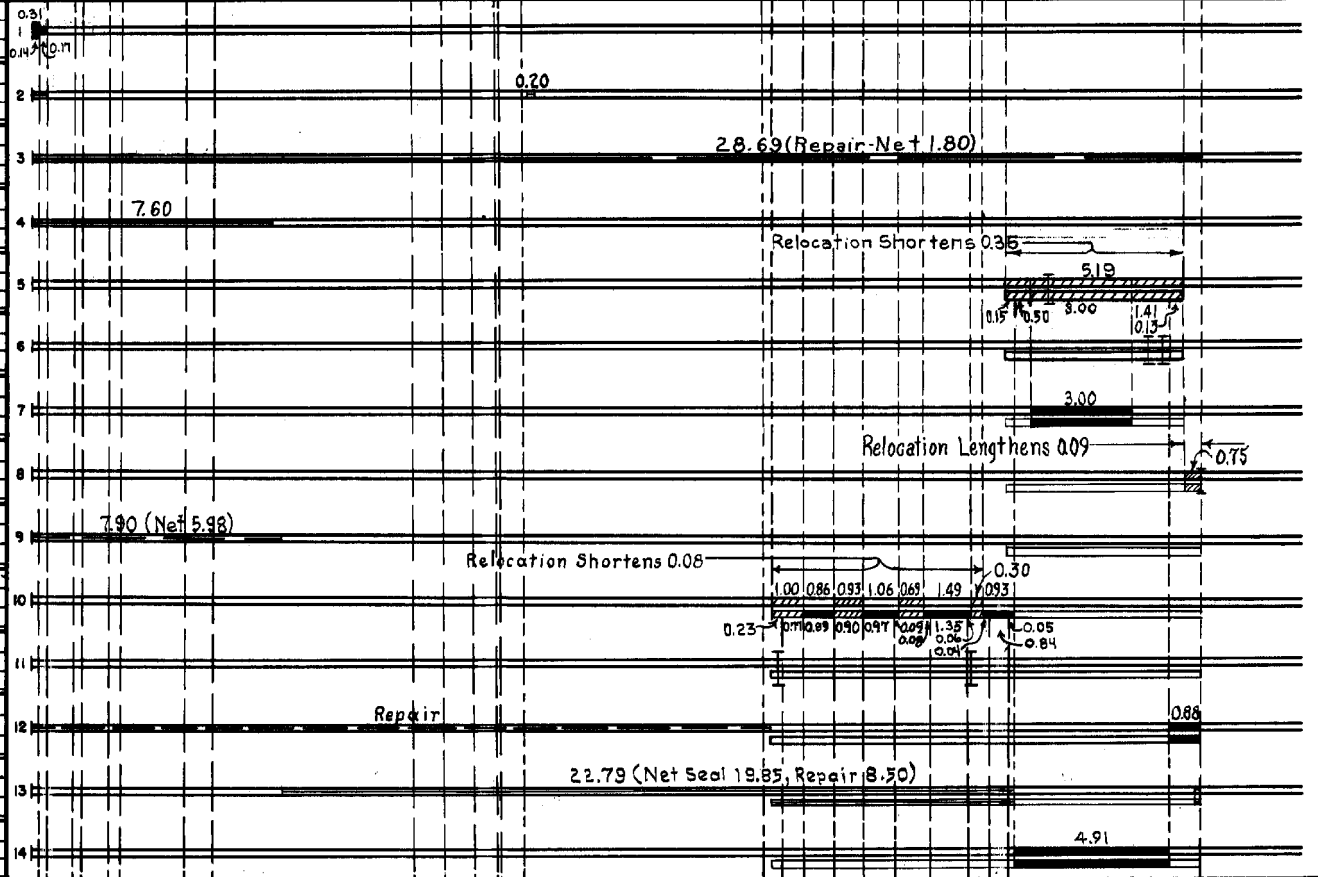

YEARS FROM	TOTAL TO	MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet No. 1 (1) 6" sand gravel sub-base, 5" gravel & 3" bit. base under bit. surf. 3/4" gravel base Under P.C. Concrete







