


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6947
TRUNK HIGHWAY 37
COUNTY St. Louis
DISTRICT 16

LIMITS: W. Jct. T.H. 169 (Jct. T.H. 73) at W. Limits of Hibbing - Jct. T.H. 53
(E. End Br.)
(See sheet 2 for data subsequent to 1975)



YEAR BUILT	PROJECT N ^o	DESCRIPTION		CODE N ^o
		TYPE	WIDTH THICKNESS	
		P.C. Concrete 6 Bridges (1)	20'	No Record of Const. Added in 1949
1940	6934-08	Widening P.C. Concrete	10'	9-6-9
C		Bit. Resurfacing		On old concrete
1950	A.F.E. 17	Mixed Bit.	21' 1 1/2"	RT-6, 71987 Gal. Agg. 4588 Tons
C		Base (3)		Const. C128D (Br. 8811)
1953	6947-02	Plant Mix Bit. Grav. Shoulders	22' 3'-4" 10'	C1010D (Br. 8812) 5' Rt. & Lt.
C		Install C.M. Culv.		
1954	A.F.E. 824			
C				Top Widened to 40'
1955	6947-06	Shoulder Grading		
C		Grading	44'	1.25 Mi. Divided Highway
1956	6947-04	Grav. Base & Sub-base Mixed Bit. (Base)	15' 26 1/2" 1 1/2"	(Const. temp. U.P. to be replaced in 1957)
C		Br. 6836		178' B.S. - U.P.
1957	6947-05			
(4)				
C		Concrete	48' 8"	
1958	6947-08			
C		Plant Mix Bit.	48' 4"	
1958	6947-09			
C		Br. 9530	30'	214' C.G.S. - O.H.
1959	6947-10	Traffic Signals		*Mi. Pt. 0.00-0.87
A.F.E. 605		Bit. Seal Coat (Shoulders)		3573 Gal. M62, Agg. 4000
C		Grading		
1960	6917-32	Gravel Base Road Mix Bit. (Base)	26' 1 1/2"	
C		Lighting Systems		In Hibbing
1961	6947-11	Grade, Base & Rd. Mix Bit. on Frontage Rds.	24' 1 1/2"	By Maint.
M				
1970	SF	Shoulder Resurface	6' 13' Var.	MC 250 tack 270 Gal. Agg. 309 Tons

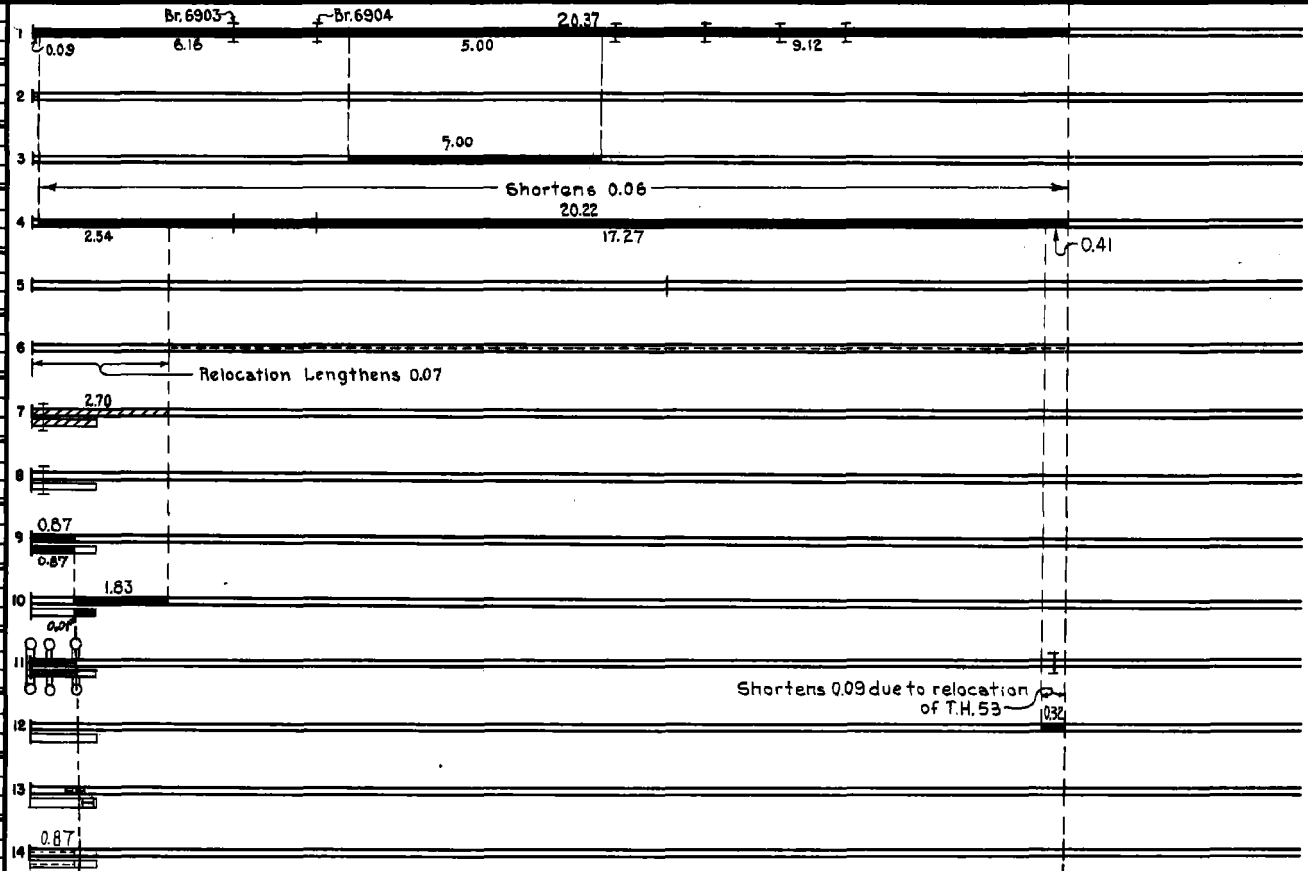

YEARS FROM TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949 1952	20.37	18.32	0.12	1.93	0.00	18.32	0.12	1.93	0.00
1953 1955	20.31	18.31	0.10	1.90	0.00	18.31	0.10	1.90	0.00
1956 1958	20.36	18.32	0.10	1.96	0.00	18.32	0.10	1.96	0.00
1959 1959	20.38	18.28	0.14	1.96	0.00	18.28	0.14	1.96	0.00
1960 1971	20.29	18.19	0.14	1.96	0.00	18.19	0.14	1.96	0.00
1972 1975	20.32	18.22	0.14	1.96	0.00	18.22	0.14	1.96	0.00
1976	19.40	18.18	0.14	1.08	0.00	18.18	0.14	1.08	0.00

REMARKS: Layout is to scale as of 1949
(1) 29' C.D.G. (Br. 6903), 26' C.D.G. (Br. 6904), 51' T.P.G. (Br. 6905), 38' B.S. (Br. 6906), 250' O.H. (Br. 6907) & 714' O.H. (Br. 6909).
(2) Apparently the portion westerly of S.A.R. 5 by St. Louis Co. Dates unknown.
(3) 79% of base is 32' x 6' min. Bit. Stab. Grav. on old conc. or Sand-Grav. sub-base, balance is old 20' concr. which was widened with 6" Bit. Base on 6" Sand-Grav. Sub-base. (4) Contract not final but work substantially complete.

