


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 7323
TRUNK HIGHWAY 238
COUNTY Stearns
DISTRICT 3B

LIMITS: Jct. T.H. 52 - N. Co. Line



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Gravel	24'		No Record of Const. Added in 1949
M 1951	A.F.E. 6	Grav. Resurfacing	24'		3599 C.Y.
M 1952	A.F.E. 6 A.F.E. 28	Grav. Resurfacing Spot Sand-Grav Lifts	27'		11284 Tons Lifts from M.P. 0.55-0.86
C 1950	City	Grading Stab. Gravel Base Hot Plant Mix	44' 44' 44'		
C 1954	A.F.E. 833	Bit. Surfacing Mixed Bit. Relay Port. Culv's	24' 1 1/2"		SC-4, 126320 Gal. Agg. 9487 Tons Spot Grav. Lifts
M 1955	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		SC-4, 31179 Gal. Agg. 2891 Tons
C 1956	A.F.E. 817	Gravel Base Bit. Surfacing Mixed Bit. (Mixed Pr.)	28' 0"-9" 24' 1"		MC-01 SC-4, 109168 Gal. Agg. 8192 Tons
C 1956	A.F.E. 828 A.F.E. 829	Grading Gravel Base Br307 (in place)	36' 36' 25'	8 1/2"	Grav. 2814 Tons B.S.-U.P.
	1926 52-3-45-3	Concrete	24' 8-7 1/2"		Transferred from C.S. 7311 (T.H. 52) in 1956
C 1957	A.F.E. 829	Bit. Stab. Base Mixed Bit.	36' 2 1/2" 24' 1"		Added thickness Bit. 6212 Gal. Surf. Agg. 217 tons
M 1958	A.F.E. 605	Bit. Seal Coat	25'		RG2, 23072 Gal. Agg. 901 C.Y.
M 1963		Light Bit. Seal	24'		RS-2K, 21061 Gal. Agg. 828 C.Y.
C 1970	7323-00	Bit. Seal Coat	24' 3/4"		
D 1977	2323-DC	Bit. Resurfacing Agg. Shoulder	24' 2 1/2" Var. Var.		

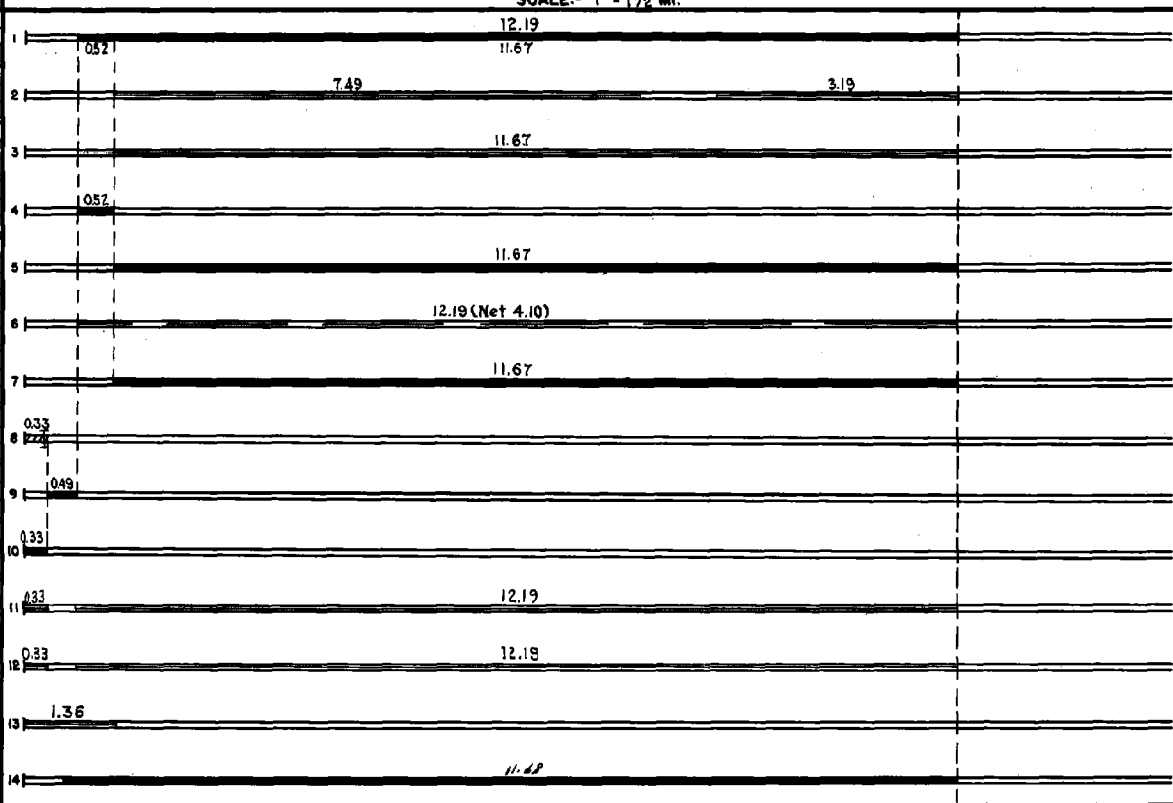

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949	1950	12.19	11.52	0.00	0.67	0.00	12.19	0.00	0.00	0.00
1951	1955	12.19	11.31	0.00	0.88	0.00	11.65	0.00	0.54	0.00
1956	1965	13.01	11.41	0.00	1.60	0.00	11.75	0.00	1.24	0.00
1966		13.01	11.33	0.00	1.68	0.00	11.67	0.00	1.34	0.00

REMARKS: Layout is to scale as of 1949

