


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 7702  
TRUNK HIGHWAY 10  
COUNTY Todd  
DISTRICT 3A

LIMITS: N. Co. Line - E. Co. Line  
Ref. Pt. 102+00.385 - 114+00.471



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
1925	10-2-32-2A&B	Grading	30'		
1925	10-2-32-2B	Gravel	24'	3"	1400 C.Y./Mile
1926	10-2-32-2A	Gravel	24'	3"	1400 C.Y./Mile
	(1)				
1927	10-2-32-2A&B	Tar Tr. Gravel	24'	1 1/2"	10780 Gal./Mile State Maint.
1929	10-2-32-2	Grading	24'		Swamp Fill.
	(1)				
1930	10-2-32-2	Gravel	24'	1"	500 C.Y./Mile State Maint.
	(1)				
1930	10-2-32-2	Oil Tr. Gravel	24'	1 1/2"	23565 Gal./Mile State Maint.
C					
1941	7702-08	Ext. Mono Culverts			
C					
1942	7702-06	Grading Gravel	42'	1 3/4"	
C					
1942	A.F.E. 7	Seeding			Seeds supplied by R.S.D. S.P. 7702-10&11 Maint. Dept.
C					
1942	7702-02	Concrete	22'	9-79	Salvaged Bit. Matl. used in shoulders.
C					
1942	7702-12	Mixed Bit.	74'	1"	48' wide for .16 Mi. in Staples.
M					
1942	A.F.E. 5	Bit Seal Coat	24'		AE-1, 3663 Gal./Mi. Agg. 107 C.Y./Mi. Maint. Dept.
C					
1944	7702-18	Offtake Ditch			

1	12.07									
	3.41								8.66	
2	8.66									
3	3.41									
4	12.07									
	1.61		3.33		0.74	0.78	0.84	1.04		3.73
5	0.84									
6	0.84									
7	0.84									
8										
9	3.33									
									2.66	
10										
11	1.61									
12	3.33									
					0.01				2.66	
13	3.73									
14										

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1925	12.07	11.07	0.00	1.00	0.00	11.07	0.00	1.00	0.00

REMARKS: Layout is to scale as of 1925.


(1) This work not done under these project numbers but lies within the limits of these projects.

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 7702  
TRUNK HIGHWAY 10  
COUNTY Todd  
DISTRICT 3A

LIMITS: N. Co. Line - E. Co. Line  
Ref. Pt. 102+00.385 - 114+00.471

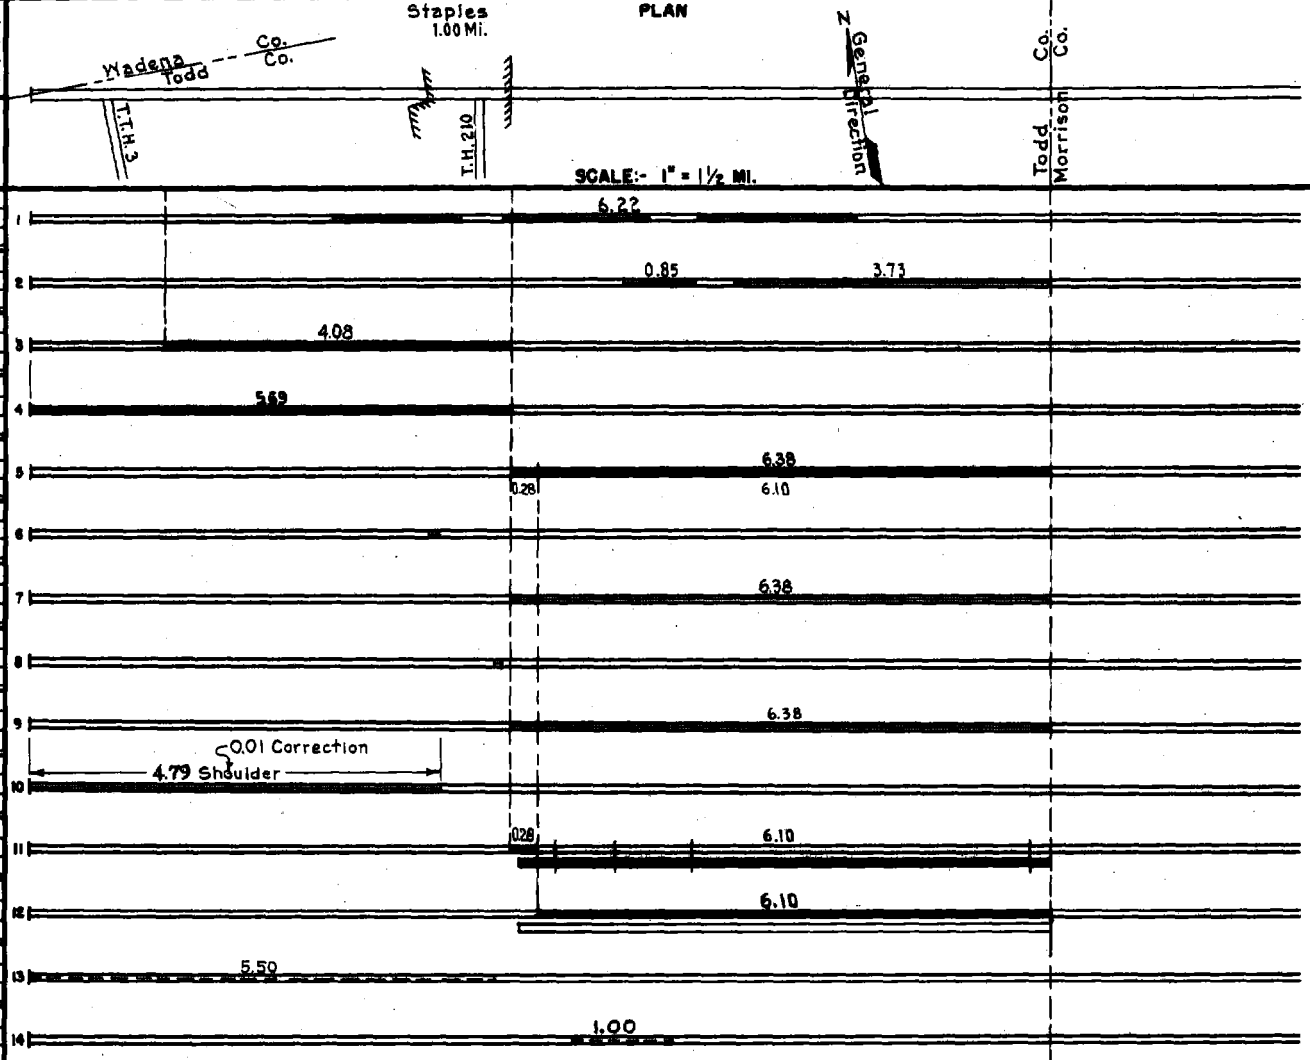

YEAR BUILT	PROJECT NO.	DESCRIPTION		CODE NO.
		TYPE	WIDTH THICKNESS	
M 1944	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'	RT-6 MC2, 1353 Gal./Mi. Sand & Gravel, 35 C.Y./Mi. Maint. Div.
M 1945	A.F.E. 4	Bit. Surf. Repair	24'	RT-6 MC2, 7211 G./Mi. Gravel, 300 C.Y./Mi. Maint. Div.
C 1948	7702-14	Concrete	24' 9'-9"	
M 1949	A.F.E. 21	Repair Shoulders		
C 1949	7702-22	Spot Gravel Base Plant Mix Bit.	24' 1 1/2' added	
C 1949	A.F.E. 17	Judicial Ditch		
M 1953	A.F.E. 605	Light Bit. Seal	24'	RS-2, 10108 Gal. Agg. 649 tons
C 1955	A.F.E. 828	Extend Storm Sewer		18" x 500' Conc. Pipe
M 1959	A.F.E. 605	Bit. Seal Coat	25'	RS-2, 14540 Gal. Agg. 511 C.Y.
M 1960 1961		Subgrade Correction & Bit. Surf. Stabilize Shoulders	25'	Mi. Pts. 235 to 236
C 1965	7702-25	Grading	45'	on W.B. rdwy.
C 1965	7702-26	Gravel Base P.C. Concrete	3 1/4' 8'	Extend Mono Culv. 3.28 mi. Divided Highway
C 1966	7702-27	Grading Rt. & Lt. Gravel Base P.C. Concrete	28' Var. 24' 6'	On E.B. rdwy.
M 1971	SF	Joint Seal		
M 1973	SF	Joint Seal		400 lbs Sealant

YEARS FROM TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		ROWY. M.	BR. M.	ROWY. M.	BR. M.	ROWY. M.	BR. M.	ROWY. M.	BR. M.

REMARKS: See Sheet No. 1



