


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8301
TRUNK HIGHWAY 4
COUNTY Watonwan
DISTRICT 7B

LIMITS: So. Co. Line - W. Jct. T.H. 60



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
C	1941 8301-04	Br. 5965	30'		
C	1941 8301-02	Gravel	36'		
C	8301-03	5-Culverts (1)			
C	1942 A.F.E. 7	Seeding			Seed supplied by R.S.D. (S.P. 8301-05) Maint. Dept.
M	1943 A.F.E. 6	Grav. Resurface (Spots)			158 C.Y. / Mi. Maint. Dept.
M	1946 A.F.E. 6	Grav. Resurfacing	24'		4038 C.Y.
C	1947 8301-07 (2)	Bit. Stab. Grav. Base	30'	9"	
C	1949 8301-08	Plant Mix Bit.	24'	1 1/2"	
M	1951 A.F.E. 4	Bit. Fog Seal	24'		RS-1, 11512 Gal. Agg. 286 C.Y.
M	1955 A.F.E. 605	Light Bit. Seal	24'		RS-2, 13508 Gal. Agg. 535 C.Y.
C	1957 8301-12	Salv. Bit. & Grav. Base Concrete	24' x 9' x 9"		Extend C108 & C48 Culverts
M	1972 SF	Joint Seal			17900 lbs.
C	1978 8302-19 FFO16-1(48)	GRADING BR 83023	90'		352' Pavet. B.S.
C	1978 8309-24 F016-1(60)	CONCRETE SURF Bit. Shoulders	10' x 8" x 1 1/2"		
M	1984 8301	Saw B. Reseal Core Joints			44,446 Lin. Ft.

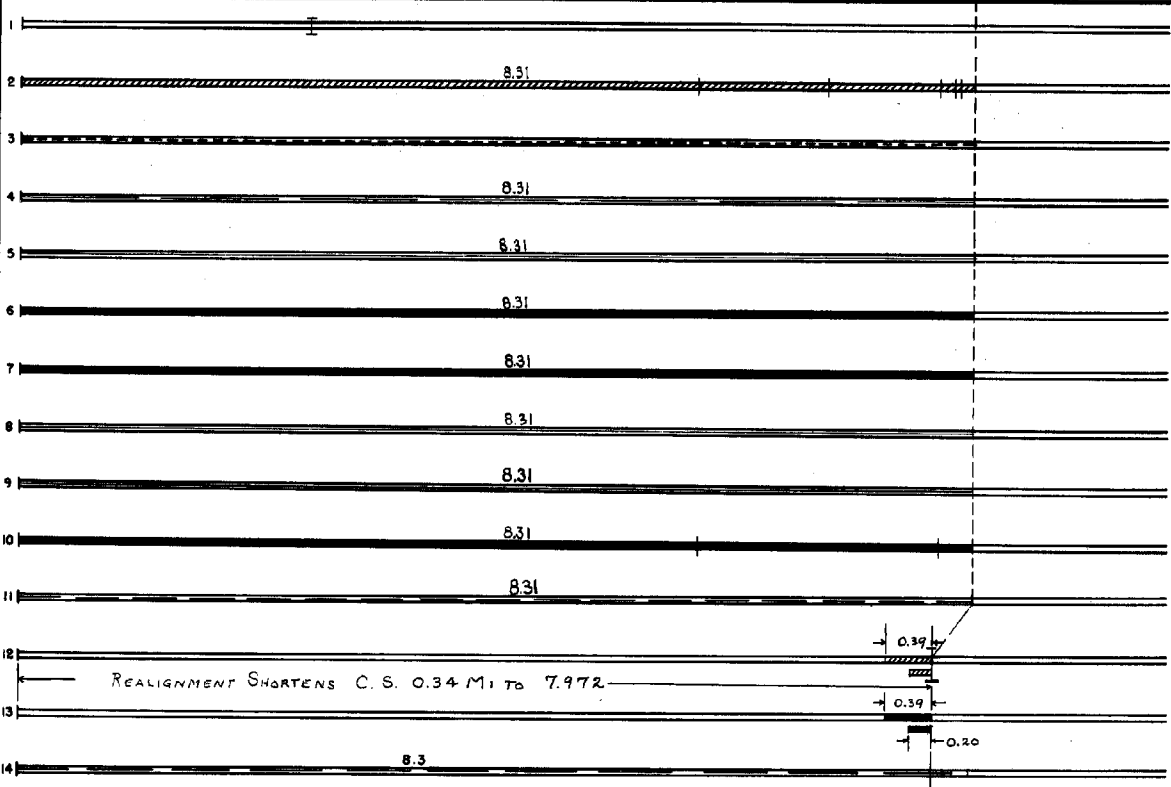

YEARS FROM TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1941	8.31	7.94	0.02	0.35	0.00	8.29	0.02	0.00	0.00

REMARKS: Layout is to scale as of 1941. See sheet N81 for data prior to 1941.
(1) Br. 8539, C108x34, Br. 8540, W106x54, Culv. C46x38; Culv. C86x34; Br. 8541, W106x38.
(2) Contract not final but work substantially complete in 1947.

