




PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8302  
TRUNK HIGHWAY 4  
COUNTY Matonwan  
DISTRICT 7B

LIMITS: E. Jct. T.H. 60 in St. James - No. Co. Line



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION		REMARKS	CODE N <sup>o</sup>
		TYPE	WIDTH THICKNESS		
M	1952 A.F.E. 5	Bit. Fog Seal Coat	24'	RS-1, 6907 Gal. Agg. 101 C.Y.	1
M	1952 A.F.E. 6	Grav. Resurfacing	24'	4312 Tons	2
C	1953 8302-10	Sand-Grav. Subbase	32' 4"		3
C	8302-11	Bit. Stab. Base	32' 4"		3
C	1954 A.F.E. 817	Plant Mix Bit.	24' 2"	Br. 8832 (C106T)	4
C	1954 A.F.E. 817	Rip Rap		At Br. 5076	4
M	1956 A.F.E. 605	Bit. Seal Coat	24'	RS-2, 9635 Gal. Agg. 300 C.Y.	5
C	1958 A.F.E. 818	Bit. Resurfacing Mixed Bit.	25' 1" added	MC3, 42063 Gal. Agg. 2810 Tons	6
M	1959 A.F.E. 605	Light Bit. Seal	26'	RS-2, 7682 Gal. Agg. 280 C.Y.	7
M	1962	Spot Treat Bit. Surf. Repair Light Bit. Seal	24' 25'	Rd. Mix. 14195 tons MC3, RS-2, 35620 Gal. Agg. 488 C.Y.	8
C	1965 8302-13	Shoulder Grading Bit. Base Plant Mix Bit. Surf.	24' 3"	Rt. & Lt. of rdwy imp. Grading & Base not on entire project	9
M	1966 SF	Bit. Surf. Repair	24' 1"	MC 250, 57175 Gal. Agg. 4351 Tons	10
M	1967 C	Bit. Surf. Repair Light Bit. Seal	24' 1" 24'	MC 800-21, 373 Gal. CRS-1 10,080 Gal.	11
C	1978 8302-19	GRADING, Bit. SURFACING RS 6101 (18)	2' 24' 16'	TEMP. TH 4 E Jct TH 60 - IN PLACE TH 60 IN ST. JAMES 0.40 MI. TRANSFERRED FROM CS 8309 IN PL. TH 60 - CSAH 14	12
C	1978 8302-21	Bit. SURFACING	24' 2"		13

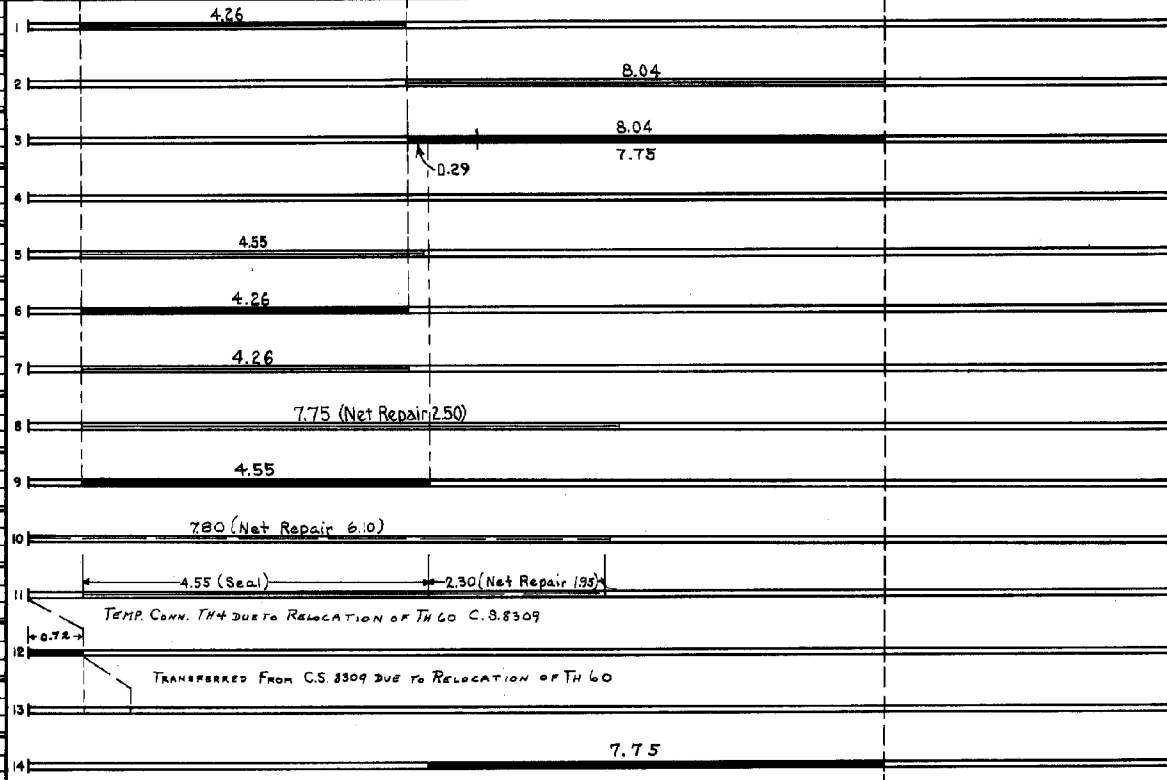

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet No. 1



