


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8306
TRUNK HIGHWAY 30
COUNTY Watonwan
DISTRICT 7A

LIMITS: Jct. T.H. 15 - E. Co. Line



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
1923		Gravel	20'	3 3/4"	1
M		Regravelling			2
1941	A.F.E. 37				
M		Grade Lifts	24'	12"	3
1943	A.F.E. 17				
M		Grav. Resurfacing (Spots)			4
1944	A.F.E. 6				
M		Grav. Resurfacing (Spots)			5
1946	A.F.E. 6				
M		Grav. Resurfacing			6
1947	A.F.E. 6				
M		Grav. Resurfacing (Spots)			7
1949	A.F.E. 6				
M		Gravel Resurfacing	24'		8
1950	A.F.E. 6				
M		Grav. Resurfacing			9
1951	A.F.E. 6				
C		Grading	38'		10
1952	8306-02	Gravel	34'	1"	
C		Soil Cement Base	24'	6"	11
1955	8306-03	Plant Mix Bit.	24'	1 1/2"	
M		Spot Treat			12
1963	SP	Bit. Surf. Repair	24'		
M		Light Bit. Seal	25'		13
1964	C				
M		Bit. Surf. Repair	24'	1"	14
1967	SF				

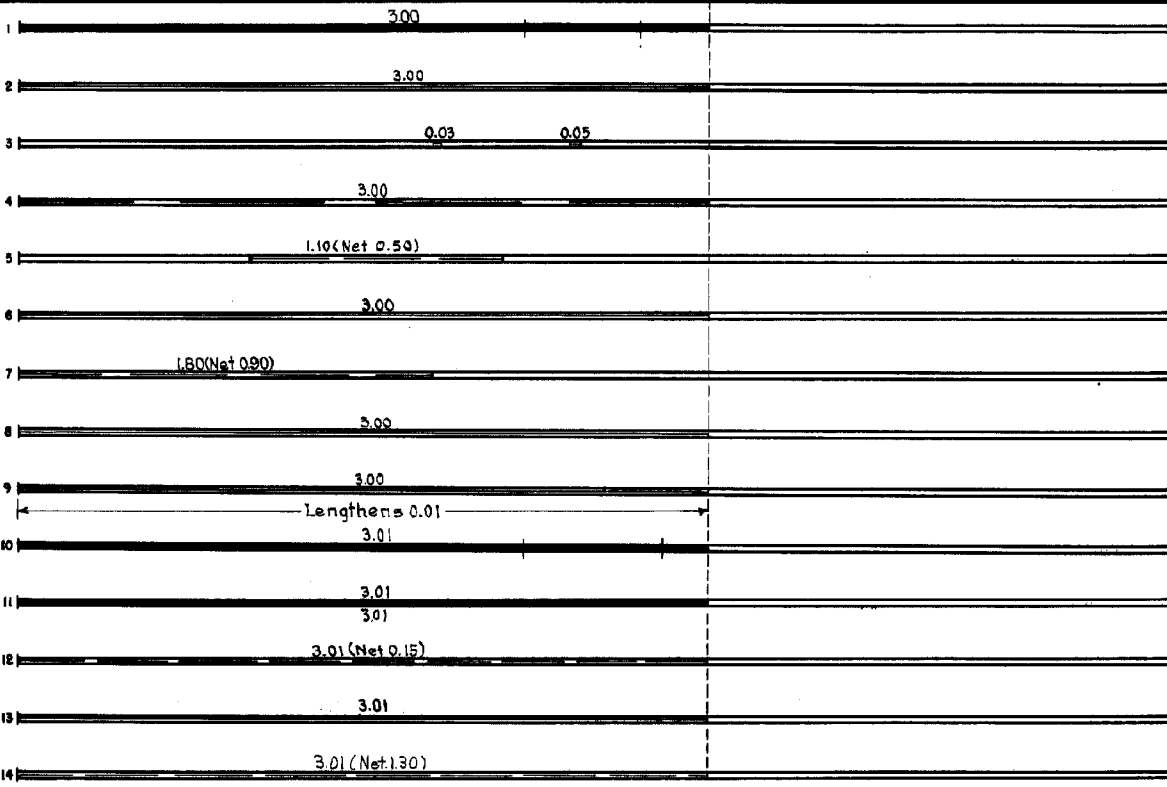

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1951	3.00	3.00	0.00	0.00	0.00	3.00	0.00	0.00	0.00
1952		3.01	3.01	0.00	0.00	0.00	3.01	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1954.
(1) Contract not final but work substantially complete.

7-74

