


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8307
TRUNK HIGHWAY 30
COUNTY Watonwan
DISTRICT 7B

LIMITS: W. Co. Line - Jct. T.H.4



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	2"	No Record of Constr. Added in 1934.
		Br. X-576	15'		22 B.S.
					Co. Job 2203 & 2204.
1922		Gravel (1)	20'	3 1/2"	1500 C.Y./Mile.
		Br. 3498 & 3487	26'9"		19' B.S. & 30' B.S.
1936		Br. 6111	16'		45 C.D.G.
		Gravel	20'	2"	No Record of Constr. Added in 1939.
C	1940 A.F.E. 14	Reshaping Gravel	24'	1 1/2"	Maint. Dept.
M	1940 A.F.E. 15	Regravelling			299 C.Y./Mile. Maint. Dept.
M	1947 A.F.E. 6	Grav. Resurfacing			3031 C.Y.
M	1950 A.F.E. 6	Grav. Resurfacing	24'		4239 Tons
		Mixed Bit.	20'		No Record of Const. 1948 Road Inv. Shows Bit. Surf.
C	1952 8307-02	Grading & C86 Culv. Salvaged Gravel	34'	2"	10'-15' select Mat'l. 1000 C.Y./Mile. C105D & C1010T
C	1955 8307-05	Sand-Grav. Sub-base Gravel base Plant Mix Bit.	34' 4 1/2" 34' 3" 24' 1/2" 3"		
M	1956 A.F.E. 605	Bit. Seal Coat	24'		RS-2, 33648 Gal. Agg. 1465 C.Y.
C	1965 8307-07	Plant Mix Bit. Gravel Shoulders	24' 1/2" 3"		
M	1967 C	Light Bit. Seal	24'		CRS-1, 23310 Gal. FA-1, Agg. 666 C.Y.

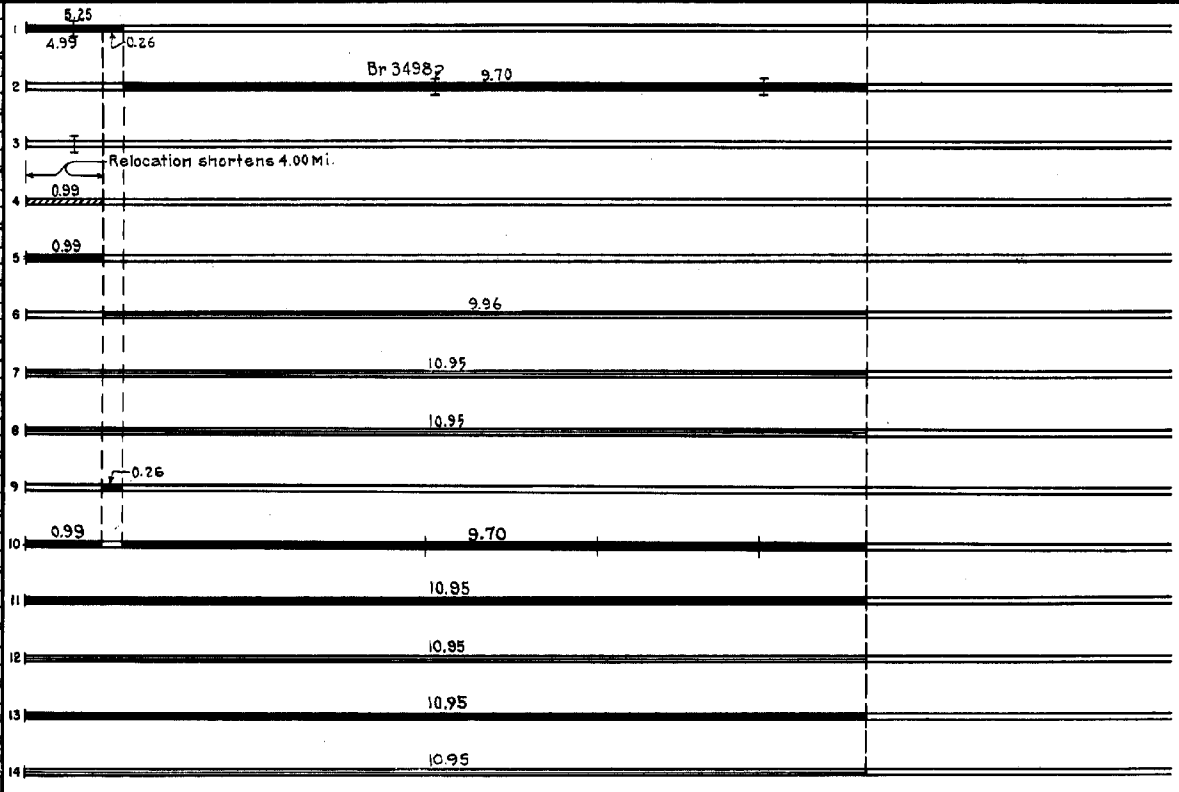

YEARS FROM	TOTAL TO	MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1938	4.95	3.93	0.02	1.00	0.00	14.93	0.02	0.00	0.00
1939		10.95	10.44	0.01	0.50	0.00	10.94	0.01	0.00	0.00

REMARKS: Layout is to scale as of 1939
(1) Added in 1934.

