


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8308
TRUNK HIGHWAY 60
COUNTY Watonwan
DISTRICT 18

LIMITS: W. Co. Line - E. Jct. T.H. 4 in St. James.



YEAR BUILT	PROJECT N ^o	DESCRIPTION		REMARKS	CODE N ^o
		TYPE	WIDTH THICKNESS		
		Gravel	20' 2"	No Record of Constr.	
1919	60-16-5	Concrete	V.W.	No Record of Constr. City Paving	
1922		Gravel	20' 2"	800 C.Y./Mile. Maint. Dept.	
1932	60-16-27	Grading Br. 5159	40' 27"	168 D.H.	
1932	60-16-27	Gravel	30' 1 1/2"	700-800 C.Y./Mile.	
1933	60-16-27	Gravel	30' 2'-3"	400-1000 C.Y./Mile.	
	(3)	Asph. Tr. Gravel	36' 1 1/2"	1920 Gal./Mile. Maint. Dept.	
1934	60-16-27	Asph. Tr. Gravel	30' 1 1/2"	1920 Gal./Mile. Maint. Dept.	
	(3)	Asphalt Tr. Gravel	24' 1 1/2"	1920 Gal./Mile. Maint. Dept.	
1934	60-16-27&A Ext.	Concrete	20' 9'-7.9		
1936	60-16-27D	Concrete	20' 9'-7.9	0.09 Mi. Widened by City to 53' Date Unknown	
1937	60-16-27C & E	Concrete	20' 9'-7.9		
1938	60-16-27C & E	Seeding			
C		Conc. Widening (0.28 Mi.)	24' 8"	12 Rt. & Lt.	
1951	8308-04	Concrete	44' 8"	Old conc. removed	
(4)	8308-05	Traffic Signals		(0.29 Mi. Granular Base)	

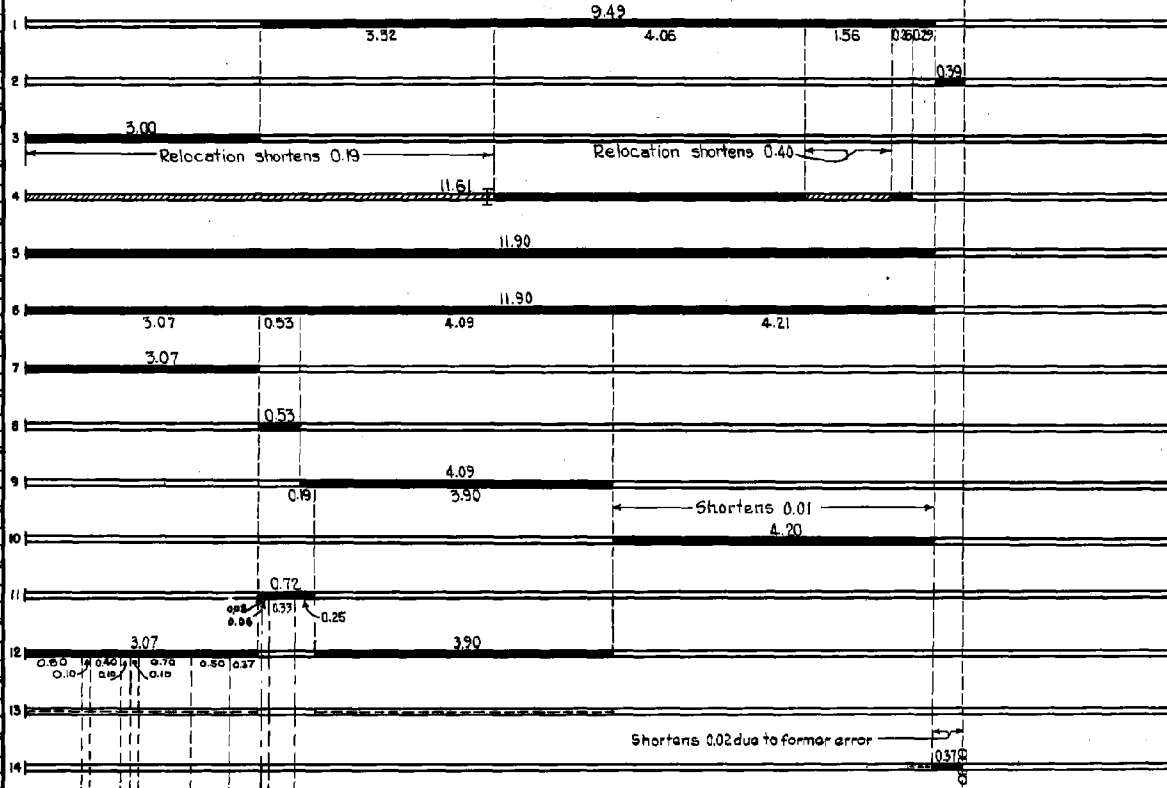

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1931	12.88	11.70	0.00	1.18	0.00	12.20	0.00	0.68	0.00
1932	1933	2.29	11.05	0.03	1.21	0.00	11.58	0.03	0.65	0.00
1934	1950	2.28	11.05	0.03	1.20	0.00	11.58	0.03	0.67	0.00
1951	1970	12.26	11.05	0.03	1.18	0.00	11.58	0.03	0.65	0.00
1971	1972	(2.26)	10.61	0.03	1.62	0.00	11.14	0.03	1.09	0.00
1973		12.26	10.40	0.03	1.83	0.00	10.93	0.03	1.30	0.00

REMARKS: Layout is to scale as of 1937.

(1) Br. 5159 built in 1934.
 (2) Accumulated thickness.
 (3) This work not done under this project number but lies within the limits of this project.
 (4) Contract on S.P. 8308-04 not final but work substantially complete.

