


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8310
TRUNK HIGHWAY 60
COUNTY Watonwan
DISTRICT 7B

LIMITS: N. Jct. T.H. 15 in Madelia - E. Co. Line
Ref. Pt. 084+00.096 - 086+00.060



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
1922	60-16-4	Concrete			
1923		Gravel	20'	3 1/2"	(600 C.Y./Mile. Maint. Dept.)
1930	60-16-25A	Grading	40'		
	(1)				
1930	60-16-25A	Gravel	32'	1 1/2"	800 C.Y./Mile. Maint. Dept.
1931	60-16-25A	Concrete	20'	9-19"	
C	8310-05	Grade Base, P.C. Conc. on E.B. Rdwy	24'	8"	
		Asph. Conc. W.B. Rd.	24'	4 1/2"	
C	8310-08	Pt. Mix Bit. Overlay	20'		
		Curb & Gutter	40'	1 1/2"	
		Gravel Shoulders	10'		
C	8310-07	Grading	40'		
C	8310-09	Grading Base	24'		
		Concrete	24'	9"	
		Bit. Shoulders			
M	1982	SF	Seal Coat	10'	CRS-2 B FA-2 Mod. SB. Shldr.
M	1983	SF	Clean. Saw. & Baseal Concrete Joints		Contract No. 4012
M	1985	SF	Clean. Saw and Baseal Conc. Joints		Cont. No. 4127
M	1988	4276	Joint Repair		
M	1990	4373	Joint Repair		

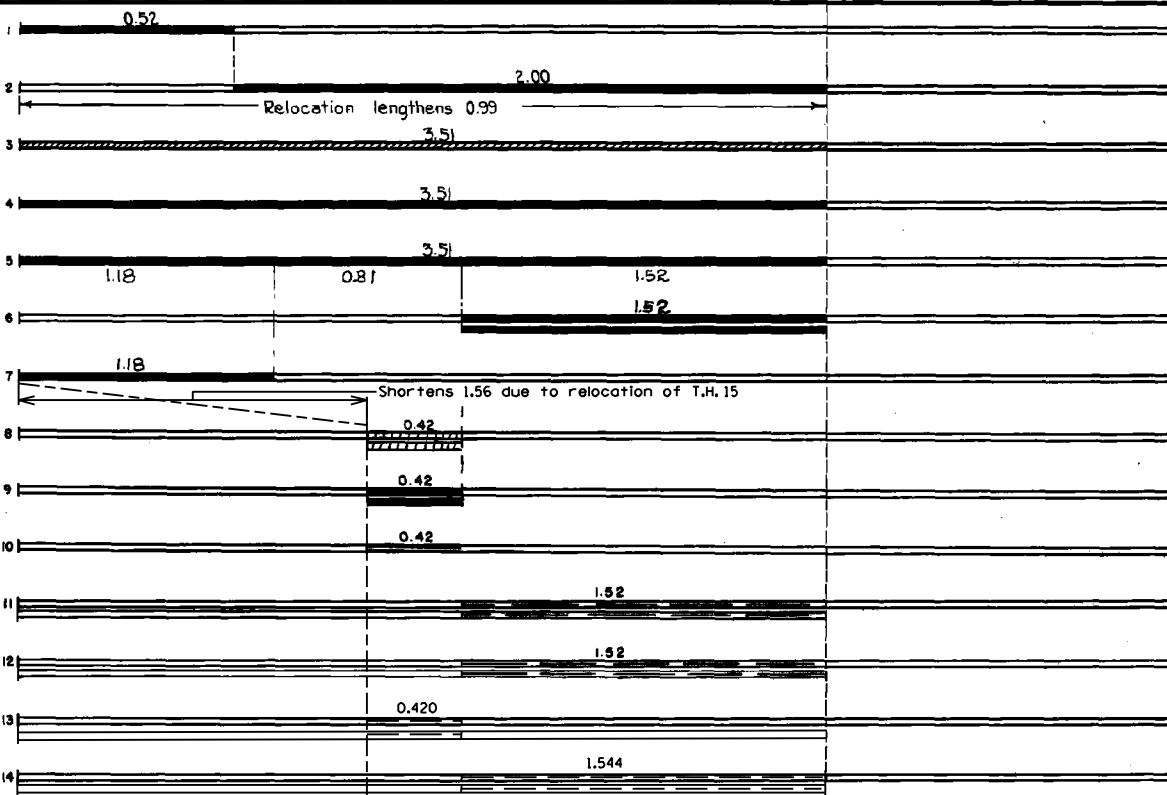

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1923	1929	2.52	0.00	0.52	0.00	2.00	0.00	0.52	0.00
1930		3.51	0.00	0.91	0.00	2.60	0.00	0.91	0.00

REMARKS: Layout is to scale as of 1930.
(1) This work not done under this project number but lies within the limits of this project.

