


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8507
TRUNK HIGHWAY 74
COUNTY Winona
DISTRICT 6A

LIMITS: W. Co. Line to Jct. T.H. 14 in St. Charles



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Gravel	43'	1"	No Record of Constr. Added in 1934.
		Br. X796, 1008 & X794	617'		27' B.S., 24' B.S. & 17' B.S.
		Oil Tr. Gravel	44'		No Record of Constr. Added in 1934.
1935		Br. 3520	23'		23' B.S. Maint. Dept.
1937		Br. 5733	27'		35' B.S. Maint. Dept.
1938	A.F.E. 36	Crushed Rock	20'	1 1/4"	Maint. Dept.
1939	8507-02	Concrete	52'	7"	
1942	A.F.E. 6	Crushed Rock			501 C.Y./Mi. Maint. Dept.
1946	A.F.E. 6	Gr. Rock Resurfacing	24'		6920 C.Y.
1948	A.F.E. 31	Bit. Surfacing	24'	1"	MC3, 7360 Gal. Agg. 340 C.Y.
1949	A.F.E. 4	Bit. Surf. Repair	24'		MC3, 285 Gal. Agg. 15 C.Y.
1950	A.F.E. 4	Light Bit. Seal	24'		RCS-1, 114 Gal. Agg. 19 C.Y.
1950	8507-04	Grading	204'	2'-9"	2.0' Select Material
1950	A.F.E. 6	Crushed Rock			Culverts (2)
1950	A.F.E. 6	Gr. Rock Resurfacing	24'		752 C.Y.
1951	8507-05	Grading	26'	2"	2.0' Select Material
		Crushed Rock			1000 C.Y./Mi.
		C86 Culvert			

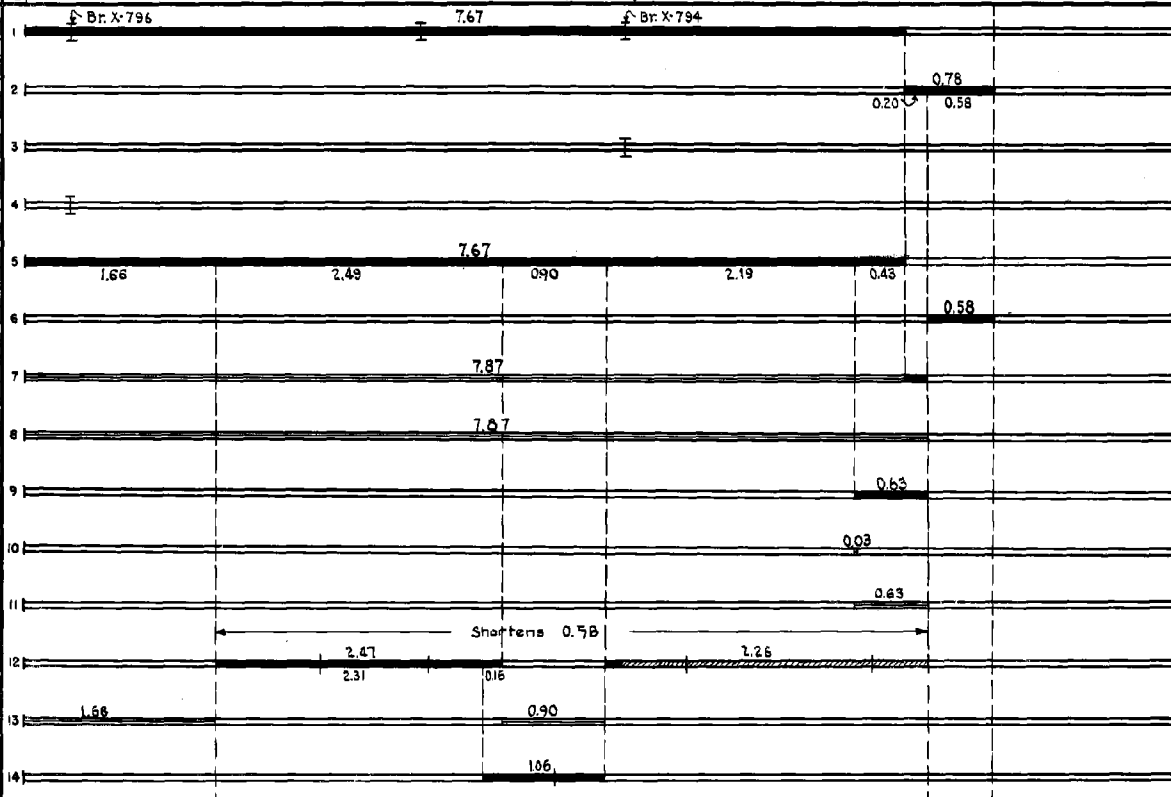

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1936	6.45	6.89	0.01	1.55	0.00	6.89	0.01	1.55	0.00
1937	1949	6.45	6.85	0.02	1.55	0.00	6.88	0.02	1.55	0.00
1950	1956	7.87	6.71	0.01	1.17	0.00	6.71	0.01	1.17	0.00
1957		7.77	6.62	0.00	1.15	0.00	6.62	0.00	1.15	0.00

REMARKS: Layout to scale as of 1934
 (1) Contract not final but work substantially complete in 1950.
 (2) C66, C1010 (Br. 8744), C1212 (Br. 8745), & C66.

