

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0104
TRUNK HIGHWAY 27
COUNTY Aitkin
DISTRICT 1A

LIMITS: Jct. T.H. 65 - E. Co. Line

R. P. 221 + 00.259 - 231 + 00.365

YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICK-NESS	
		Gravel Br. N ^o 485	23' 16'	3"	No Record of Constr. Added in 1934. 15' B.S.
M	1940 A.F.E. 47	Regraveling			197 C.Y./Mi. Maint. Dept.
M	1941 A.F.E. 26 A.F.E. 52	Spot Graveling & Frost Boil Lifts	20'		909 C.Y./Mi. Maint. Dept.
C	1942 A.F.E. 23	2-Culverts			Replaces Br. 485 2-48" Maint. Dept.
C	1943 A.F.E. 23	Remove Br. 485			Maint. Dept.
M	1944 A.F.E. 6	Grav. Resurfacing			447 C.Y./Mi. Maint. Div.
M	1948 A.F.E. 6	Grav. Resurfacing			8019 C.Y.
M	1952 A.F.E. 12	Grav. Resurfacing (Spots)			1227 C.Y.
M	1954 A.F.E. 828 A.F.E. 606	Side Ditch Cleaning Drainage Corr. Grav. Resurfacing			1701 Tons
M	1955 A.F.E. 606	Spot Grav. Lifts (Net 180) Grav. Resurfacing	27' 20'		Grav. Lifts 3623 Tons Grav. Surf. 4669 Tons
M	1956 A.F.E. 606	Grav. Resurfacing (Spots)	24'		3360 Tons
M	1958 A.F.E. 606	Grav. Resurfacing	20'		4088 Tons
M	1965 SF	Grav. Resurfacing	20'		2817 Tons
C	1974 0104-03	Grade Base Bit. Surface	24'	2"	

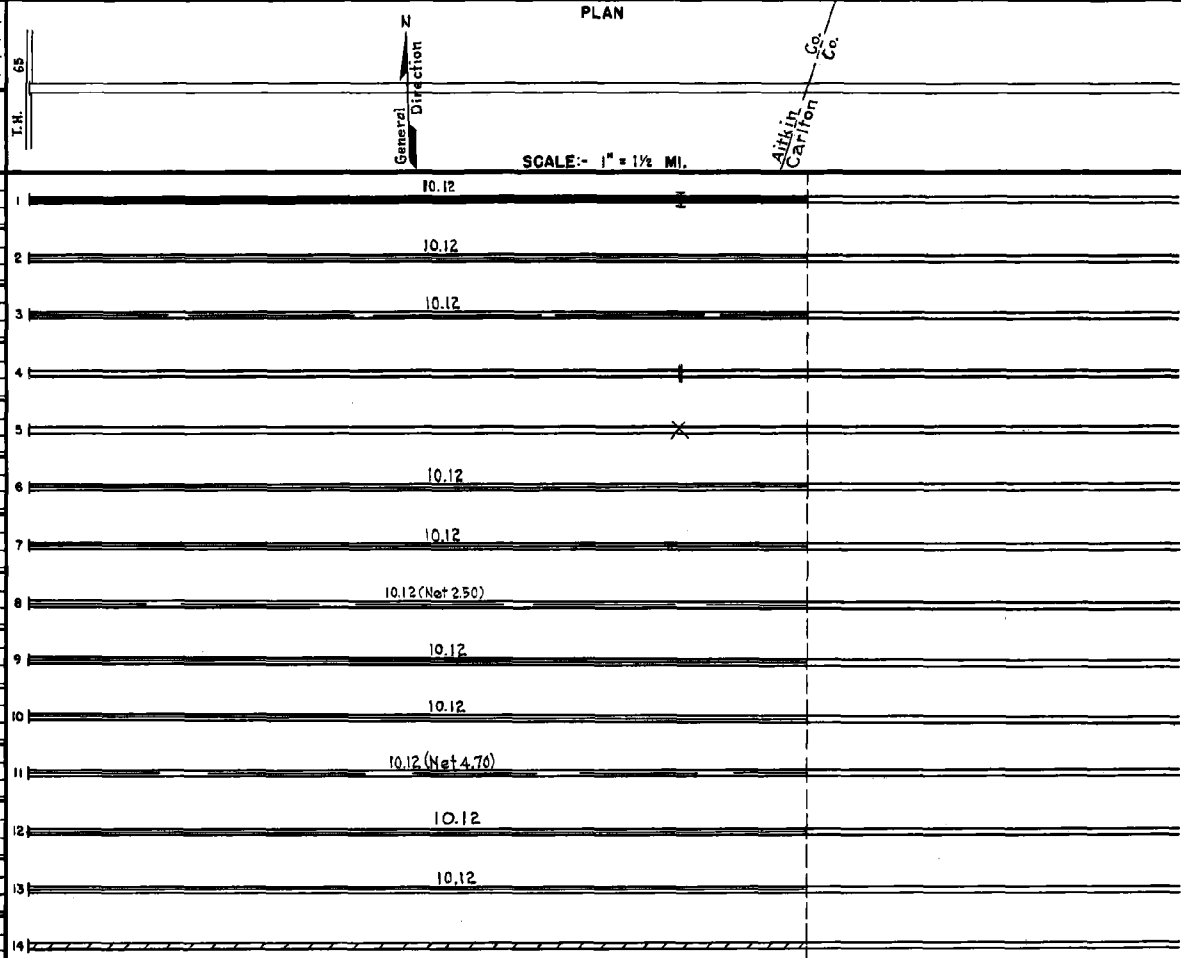

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN		
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	
1934		10.12	10.12	0.00	0.00	0.00	0.00	10.12	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934

