


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0405
TRUNK HIGHWAY 1
COUNTY Beltrami
DISTRICT 2A

LIMITS: W. Jct. T.H. 72 - East Co. Line

YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o DIST
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	2"	No Record of Constr. Added in 1934.
		Br. N ^o 309 & 108	22'	2"	10' W.S. & 27' B.S.
M	1941 A.F.E. 24	Regraveling	20'		391 C.Y./Mi. Maint. Dept.
C	1946 A.F.E. 27	Regrade & Gravel	28'	2"	5743 C.Y.
M	1948 A.F.E. 6	Grav. Resurfacing			4400 Tons
M	1970 A.F.E. 6	Gravel Resurfacing			7470 Tons
C	1951 A.F.E. 28	Install Culverts			1-36"x32' 2-48"x48'
C	A.F.E. 31 (1)	Grading	28'		1.0 Select Material
	0405-03	Gravel	26'	2"	1200 C.Y./Mi.
	0405-04	Br. 6792	28'		20' B.S.
M	1955 A.F.E. 606	Grav. Resurfacing	24'		2855 Tons
M	1956 A.F.E. 606	Grav. Resurfacing	24'		253 Tons
C	1961 0405-05 & 06	Grading Sub-base & Base Plant Mix Bit. (Base)	22' 22' 24'	3" 3" 1 1/2"	
M	1966 C	Light Bit. Seal	25'		RC-250, 10592 Gal. Agg. 385 C.Y.
C	1968 0405-08	Pl. Mix. Bit. Surf. Gravel Shldrs.	24'	3"	Bit. Matl. 802 Ton 4" Rt. & Lt.
C	1972 0405-09	PLATE BEAM GUARD RAIL BR # 6792			515 Lin. Ft.
M	1983 SF	Spot Bit. Overlays	24'	1 1/2"	Pl. Mix 2331 - 853 Tons Total in CS 0405 8360

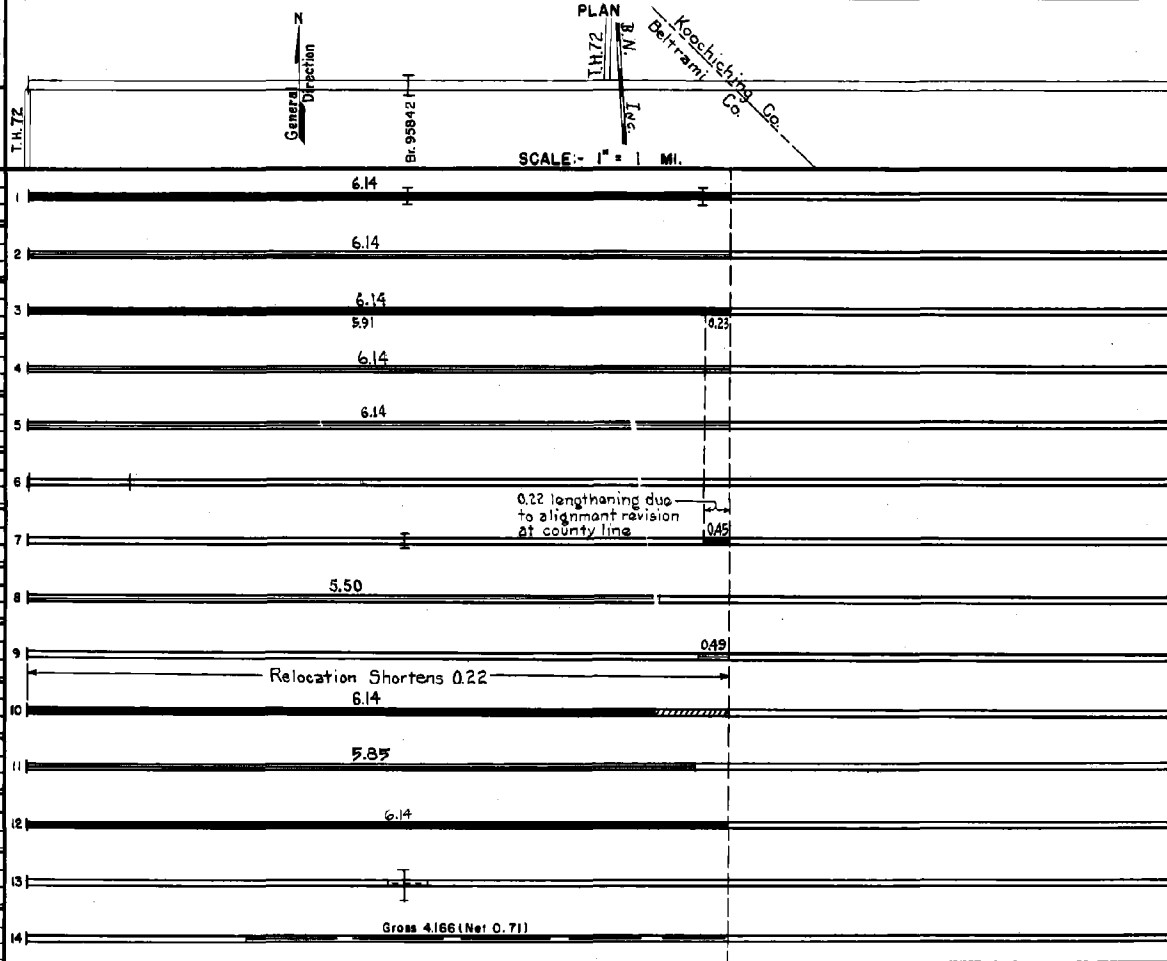

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED			INCORPORATED			RURAL		URBAN	
			RDWY. MI.	BR. MI.	0.01	RDWY. MI.	BR. MI.	0.00	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1951	6.14	6.13	0.01	0.00	0.00	6.13	0.01	0.00	0.00		
1952	1960	6.36	6.35	0.01	0.00	0.00	6.35	0.01	0.00	0.00		
1961		6.14	6.14	0.00	0.00	0.00	6.14	0.00	0.00	0.00		

REMARKS: Layout is to scale as of 1934
(1) For approaches to Br. 6792.

