


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0709  
TRUNK HIGHWAY 60  
COUNTY Blue Earth  
DISTRICT 7A

LIMITS: East Jct. T.H. 14 - East Co. Line



YEAR BUILT	PROJECT NO.	DESCRIPTION			CODE NO.
		TYPE	WIDTH	THICKNESS	
1921	60-60-21	Grading	30'		
1922	60-60-21	Gravel	24	4 1/2"	2400 C.Y./Mile.
1924	60-60-22	Grading Gravel	30' 24'	4"	1800 C.Y./Mile.
1927	60-60-21 60-60-22 (U)	Oil Tr. Gravel	22'	1 1/2"	10347 Gal./Mile. Maint. Dept.
1931	60-7-20	Grading Gravel	32' 26'	1 1/2"	Trans. from T.H. 14 in 1936. 800 C.Y./Mile.
1934	60-7-20	Oil Tr. Gravel	22'	1 1/2"	Trans. from T.H. 14 in 1936. Maint. Dept.
C	0709-01	Grading Gravel	35' 35'	1 1/4"	
M	0709-02	Mono. Culverts			2-W46.
1940	A.F.E. 22	Bit. Retreat			MG-3-964-583 Gal./Mi. Grav. 54 C.Y./Mi. Maint. Dept.
C	A.F.E. 27	Seeding			Seed supplied by R.S.D. S.P. 0709-06 Maint. Dept.
C	0709-05	Mixed Bit. Stab. Grav. Base	26' 32'	1" 6 1/2"	
M	A.F.E. 41	Fog Seal	26'		RC-3-1734 Gal./Mi. Sand 10 C.Y./Mi. Maint. Dept.
M	A.F.E. 12 A.F.E. 4	Spot Treat. Bit. Surf. Repair			SC-4-1323 Gal./Mi. Maint. Dept.
M	A.F.E. 4	Spot Treat. Bit. Surf. Repair			MC-2-1077 Gal./Mi. Grav. 22 C.Y./Mi. Maint. Dept.
M	A.F.E. 4	Bit. Fog Seal			RC-2-2223 Gal./Mi. Sand 52 C.Y./Mi. Maint. Dept.

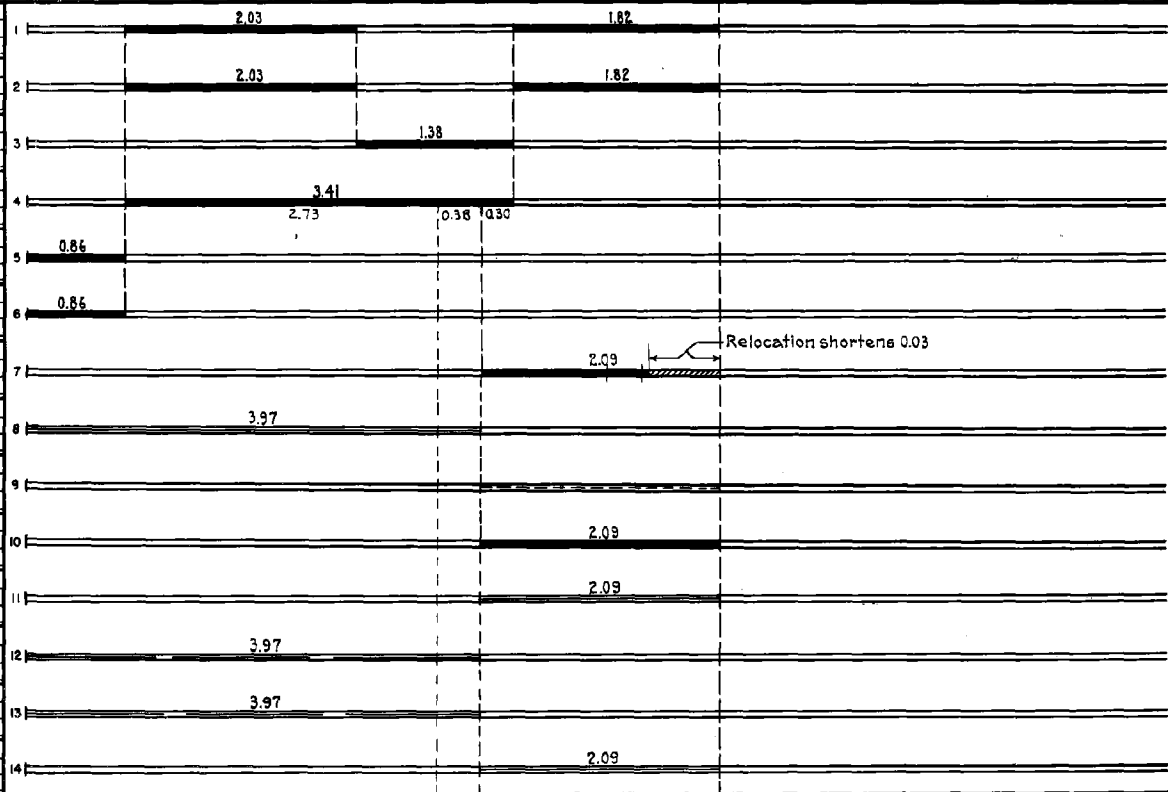

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			ROWY MI.	BR. MI.	ROWY MI.	BR. MI.	ROWY MI.	BR. MI.	ROWY MI.	BR. MI.
1924	1935	5.23	3.96	0.00	1.25	0.00	5.23	0.00	0.00	0.00
1936	1945	6.09	4.84	0.00	1.25	0.00	6.09	0.00	0.00	0.00
1946	1961	6.06	5.43	0.00	0.63	0.00	6.06	0.00	0.00	0.00
1962	1967	6.08	5.58	0.00	0.50	0.00	6.08	0.00	0.00	0.00
1968		6.09	5.46	0.00	0.63	0.00	6.09	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1936

(U) This work not done under these project numbers but lies within the limits of these projects


FORM R.L.-7 REV. 2-40

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0709  
TRUNK HIGHWAY 60  
COUNTY Blue Earth  
DISTRICT 7A

LIMITS: E. Jct. T.H. 14 - E. Co. Line



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
C	1944 0709-10	Base Repair (Spots) Mixed Bit.	26'	1 1/2" Agged	
M	1944 A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		MC3 2194 Gal./Mi. Grav. 41 C.Y./Mi. Maint. Div.
M	1945 A.F.E. 4	Spot Treat. Bit. Surf. Repair			MC2 2406 Gal./Mi. Grav. 70 C.Y./Mi. Maint. Div.
C	1946 0709-08	Grading Stab. Gravel	36'	2"	
(1)		Extend Mono. Curb.	30'		W55 x 77'
M	1947 A.F.E. 5	Bit. Seal Coat	24'		RC-3, 5379 Gal. Agg. 148 C.Y.
C	1948 0709-11	Stab. Grav. Base Mixed Bit.	30' x 26'	9" x 1 1/2"	
M	1948 A.F.E. 5	Bit. Seal Coat	24'		RC-3, 1430 Gal. Agg. 65 C.Y.
M	1950 A.F.E. 4	Bit. Seal Coat	24'		RCS-18 MC3, 6989 Gal. Agg. 152 C.Y.
M	1953 A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		SG-3, 12587 Gal. Agg. 713 C.Y.
M	1954 A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		MC3 & RCS2, 30329 Gal. Agg. 1740 Tons & 280 C.Y.
M	A.F.E. 605	Spot Light Bit Seal	24'		
M	1956 A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		MC-3, 23453 Gal. Agg. 1925 Tons
M	1957 A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		MC-3, 8213 Gal. Agg. 567 Tons
M	1959 A.F.E. 604	Bit. Surf. Repair	24'		MC-3, 2461 Gal. Agg. 229 Tons
M	1960	Bit. Surf. Repair	24'		MC-3 & SC-3, 2100 Gal. Agg. 129 Tons

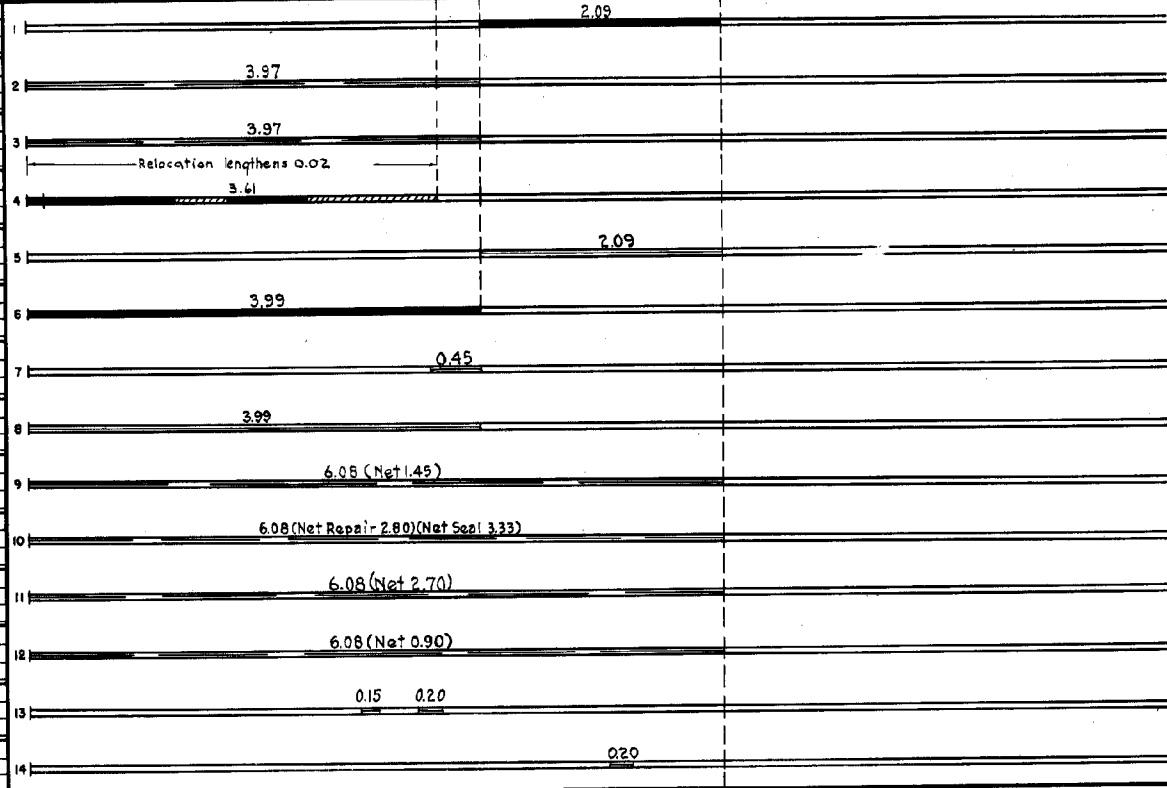

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet N° 1  
(1) Contract not final but work substantially complete in 1946.

