

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1308
TRUNK HIGHWAY 8
COUNTY Chicago
DISTRICT

LIMITS: South Co. Line - Jct. T.H. 98

PLAN


Chicago -
Washington Co.



T.H. 98

YEAR BUILT	PROJECT N ^o	DESCRIPTION				CODE N ^o
		TYPE	WIDTH	THICK-NESS	REMARKS	
		Gravel	24'	4"	No Record of Constr. Added in 1934.	
		Asphalt	24'	1 1/2"	No Record of Constr. Added in 1934.	
1937	A.F.E. 18	Mixed Bit.	20'	1"	Maint. Dept.	
M	1940	Bit. Retreat.			MG 3,5192 Gal./Mi. Grav. 336 C.Y./Mi. Maint. Dept.	
M	1943	Bit. Surf. Repair	20'		RT-6, 2355 Gal./Mi. Maint. Dept.	
C	1944	Bit. Resurfacing Mixed Bit.	20'	1"	RT-6, 6616 Gal./Mi. Agg. 420 C.Y./Mi. Maint. Div.	
M	1948	Bit. Surf. Repair	22'		RT-6, 16341 Gal. Agg. 750 C.Y.	
C&M	1950	Bit. Resurfacing Mixed Bit. Bit. Fog Seal (0.40 Mi.)	21'	1"	RT-6, 11574 Gal. Agg. 608 C.Y.	
C	1951	Grading Gravel	36' 24'	2"	1200 C.Y./Mi.	
C	1954	Concrete	22'	9-79		
C	1970	Pl. Mix Bit. Shldrs. Turn Lanes				
M	1971	Edgelina Seal Joint Seal			59,560 Lin. Ft. 35,734 Lin. Ft.	
C	1978	Bit. Resurfacing				
C	1981	Traffic Noise Recess and Safety Improvements				

SCALE:-

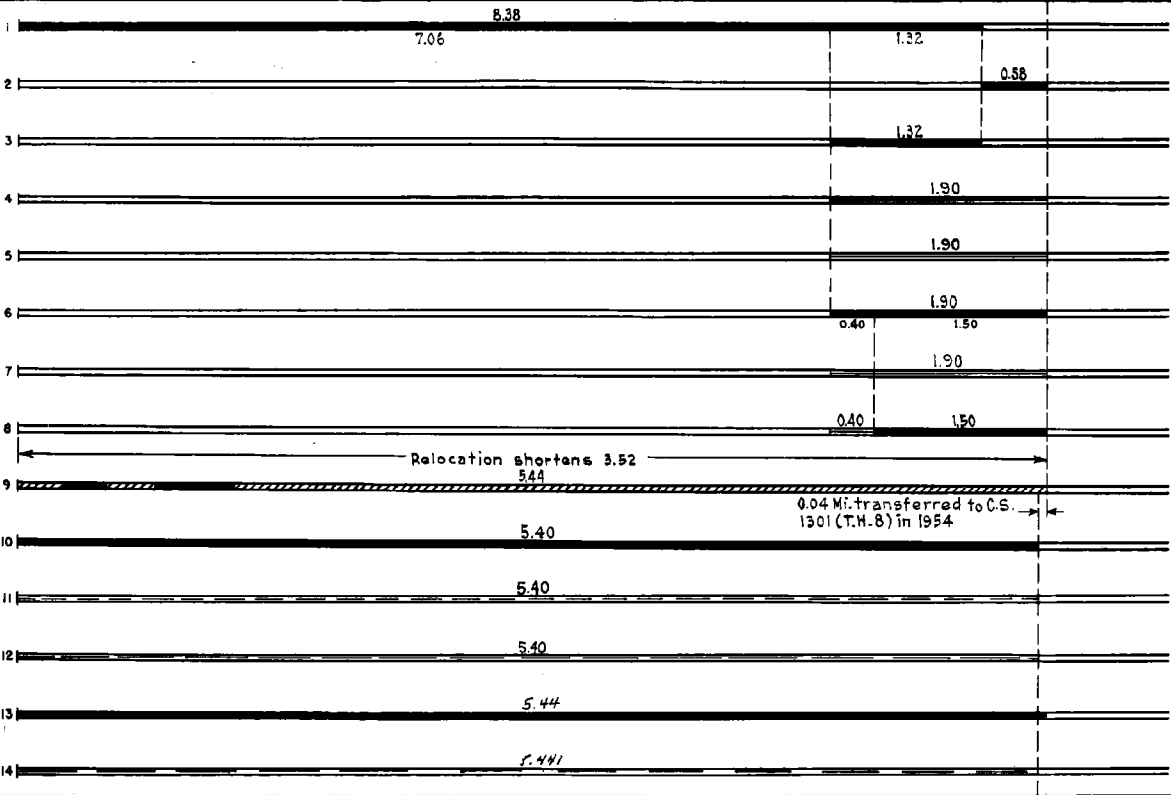

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1950	8.96	7.90	0.00	1.06	0.00	8.96	0.00	0.00	0.00
1951	1953	5.44	5.44	0.00	0.00	0.00	5.44	0.00	0.00	0.00
1954		5.40	5.40	0.00	0.00	0.00	5.40	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934. Plan revised for 1951 relocation.

