


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2806
TRUNK HIGHWAY 76
COUNTY Houston
DISTRICT 6A

LIMITS: S. State Line - S. Jct. T.H. 44



YEAR BUILT	PROJECT N°	DESCRIPTION				CODE N°
		TYPE	WIDTH	THICKNESS	REMARKS	
1928		Grading (1) Crushed Rock Br. 135 & 1309	28' 20' 1917	2 1/2"	Co. Job 2804, Added in 1934, 1180 C.Y. / Mi. 40' L.T. & 30' B.S.	
1928		Grading (1) Crushed Rock	28' 20'		Co. Job 3002, 1056 C.Y. / Mi. Added in 1934.	
M	1940 A.F.E. 32	Resurface Crushed Rock			328 C.Y. / Mi. Maint. Dept.	
C	1940 A.F.E. 25	Mixed Bit.	24'	1"	Maint. Dept.	
M	1942 A.F.E. 4	Bit. Retreat			5035, 7351 Gal. / Mi. Cr. Rk. Sand 414 C.Y. / M. Maint. Dept.	
M	1942 A.F.E. 6	Resurface Crushed Rock			582 C.Y. / Mi. Maint. Dept.	
M	1945 A.F.E. 6	CaCl ₂ Treated Crushed Rock Resurfacing			888 C.Y. / Mi. Maint. Div.	
C	1946 A.F.E. 16	Bit. Resurfacing Mixed Bit.	24'	1" added	5 C. 3, 6550 Gal. Agg. 391 C.Y.	
M	1947 A.F.E. 4	Bit. Fog Seal	24'		MC-3, 1500 Gal. Agg. 40 C.Y.	
C	1948 A.F.E. 32	Bit. Resurfacing Mixed Bit.	24'	3/4" added	MG286C3, 8028 Gal. Agg. 440 C.Y.	
M	1948 A.F.E. 6	Crushed Rock Resurfacing			8987 Tons	
C	1949 A.F.E. 22	Bit. Surfacing Mixed Bit.	24'	1"	MG185C4, 84073 Gal. Agg. 6056 Tons	
M	1949 A.F.E. 4	Spot Treat. Bit. Surf. Repair Bit. Fog Seal	24' 24' 24'		RC185C-3, 2037 Gal. Agg. 69 C.Y.	
M	1970 A.F.E. 4	Spot Treat. Bit. Surface Repair Light Bit. Seal Coat	24' 24' 24'		Bit. 19140 Gal. Agg. 698 C.Y.	

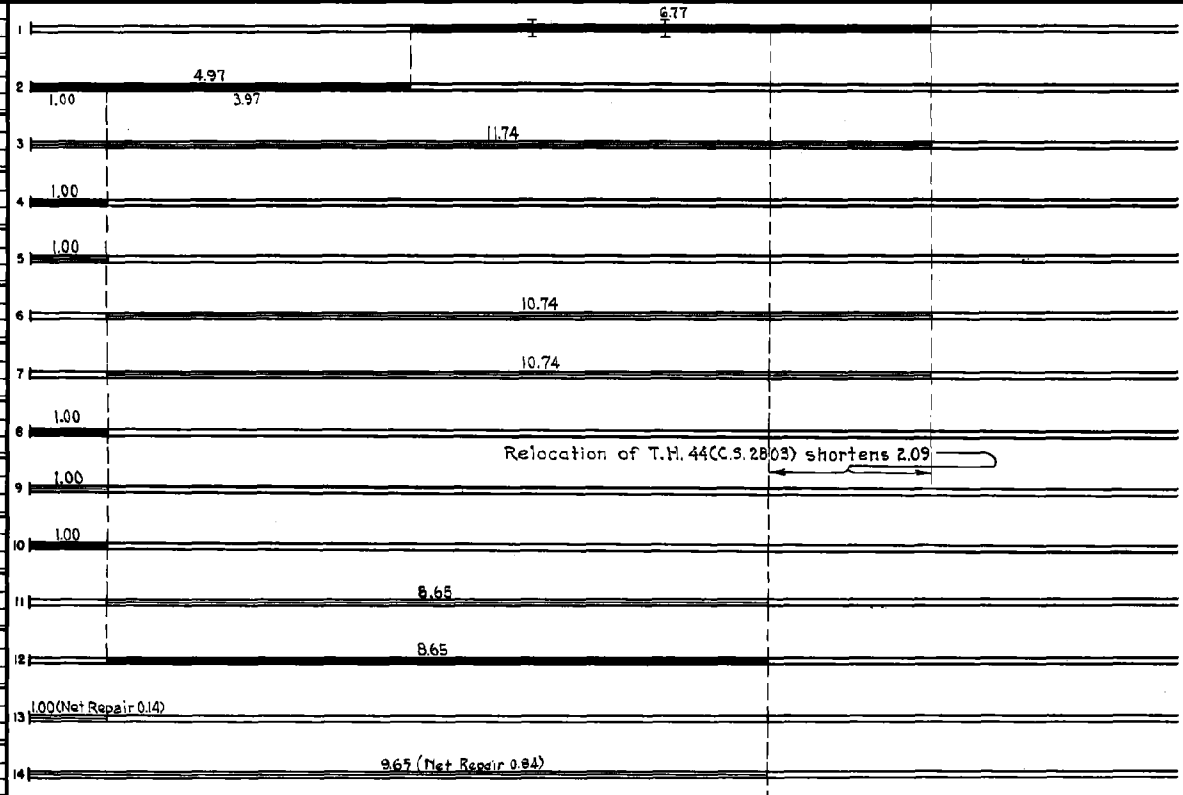

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1946	11.74	11.37	0.01	0.36	0.00	11.37	0.01	0.36	0.00
1947	1948	9.65	9.64	0.01	0.00	0.00	9.64	0.01	0.00	0.00
1949	1953	9.65	8.76	0.01	0.88	0.00	9.64	0.01	0.00	0.00
1954		7.83	7.18	0.00	0.65	0.00	7.83	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934. Plan revised for 1947 shortening due to relocation of T.H. 44 (C.S. 2803)

(1) Graded as Co. Job 2701.

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2806
TRUNK HIGHWAY 76
COUNTY Houston
DISTRICT 6A

LIMITS: S. State Line - S. Jct. T.H. 44

Houston
State of Iowa
0.65 Mi.

General Direction N

Br. 6728

PLAN
Minnesota
Br. 6844

T.H. 44

Caledonia
0.00 Mi.

T.H. 44

SCALE: 1" = 1/2 MI.

YEAR BUILT	PROJECT N ^o	DESCRIPTION				CODE N ^o	
		TYPE	WIDTH	THICKNESS	REMARKS		
M 1951	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		MC-3, 18778 Gal. Agg. 999 C.Y.	1	9.65(Net 2.90)
M 1952	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		MC-3, 26192 Gal. Agg. 1826 C.Y.	2	9.65(Net 4.60)
M 1953	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		SG-3, 26168 Gal. Agg. 1148 C.Y.	3	9.65(Net 3.59)
M 1954	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		SG-3, 20678 Gal. Agg. 1620 Tons.	4	8.00(Net 3.40)
C (2) 1954	2806-04	Grading Crushed Rock	48' 28'		Conc. Arch Culv. (24' Span) Br. 6728, C12 1/2 D.H. (Br. 6844) & C 66 H.	5	Relocation shortens 1.82 7.83
M 1955	A.F.E. 606	Cr. Rock Resurf.	24'		1259 Tons	6	3.00
C 1956	2806-06	Crushed Rock Base Plant Mix Bit.	32' 24'	12" 2"		7	7.83
C 1957	2806-07	Guard Rail (14580')				8	7.83
M 1957	A.F.E. 605	Bit. Seal Coat	25'		RS-2, 28461 Gal. Agg. 915 C.Y.	9	7.83
M 1959	A.F.E. 866	Erosion Control				10	
M 1964	SF	Spot Treat. Bit. Surf. Repair	24'		Bit. Mix 105 Tons MC-2 Tack 100 Gal.	11	7.83(Net 0.09)
M 1966	SF	Bit. Surf. Repair	24'	3/4"	Tack 190 Gal. Bit. Mixture 108 Ton	12	7.83(Net 0.25)
M 1968	SF	Bit. Seal Coat	24'		RC-250, 5970 Gal. Agg. 230 C.Y.	13	7.83(Net 3.25)
M 1970	SF	Spot Bit Repair	24'	3/4"	Tack-16 637 Gal. Agg. 725 C.Y.	14	7.83(Net Repair 150)

YEARS FROM	TOTAL TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet No. 1
(2) Contract not final but work substantially complete

