


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3501
TRUNK HIGHWAY 11
COUNTY Kittson
DISTRICT 28

LIMITS: E. End of Bridge (Red River) - Jct. T.H. 75 in Donaldson



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o DIST
		TYPE	WIDTH	THICKNESS	
		Gravel	26'		No Record of Const. Added in 1934.
		Br. 6019	19'		48' B.E.
1918		Br. 2929	17'		23' B.S. Added in 1934.
M	1941 A.F.E. 43	Regraveling	24'		396 C.Y./Mi. Maint. Dept.
M	1942 A.F.E. 6	Spot Graveling	24'		240 C.Y./Mi. Maint. Dept.
M	1945 A.F.E. 6	Grav. Resurfacing (Spots)			155 C.Y./Mi. Maint. Div.
M	1949 A.F.E. 6	Grav. Resurfacing			9115 Tons
M	1950 A.F.E. 6	Gravel Resurfacing			6044 Tons
C	1951 3501-02	Grading Gravel	34'	30'	2" 1200 C.Y./Mi. 1151
M	1953 A.F.E. 606	Grav. Resurfacing (Spots)			4480 Tons
M	1954 A.F.E. 606	Grav. Resurfacing (Spots)			1636 Tons
C	1955 3501-04	Grading (10.64 Mi) Bit. Stab. Base * (2)	32'	32'	2" Const. C.1010 D (Br. 8905) & C.1214 D (Br. 8906) 855
C&M	1956 A.F.E. 817	Guard Rail (468 L)			*On 10' Sand-Gr. Sub-base
C&M	1956 A.F.E. 819	Reshape Roadway & Ditches			
M	1957 A.F.E. 605	Light Bit Seal	27'		RC-2, 21695 Gal. Agg. 760 C.Y.
C	1963	Plant Mix Bit	24'	1 1/2"	Bit Mix 17792 Tons 1263
		Grav. Shoulders	7'		3 1/2' Rt & Lt. 1143

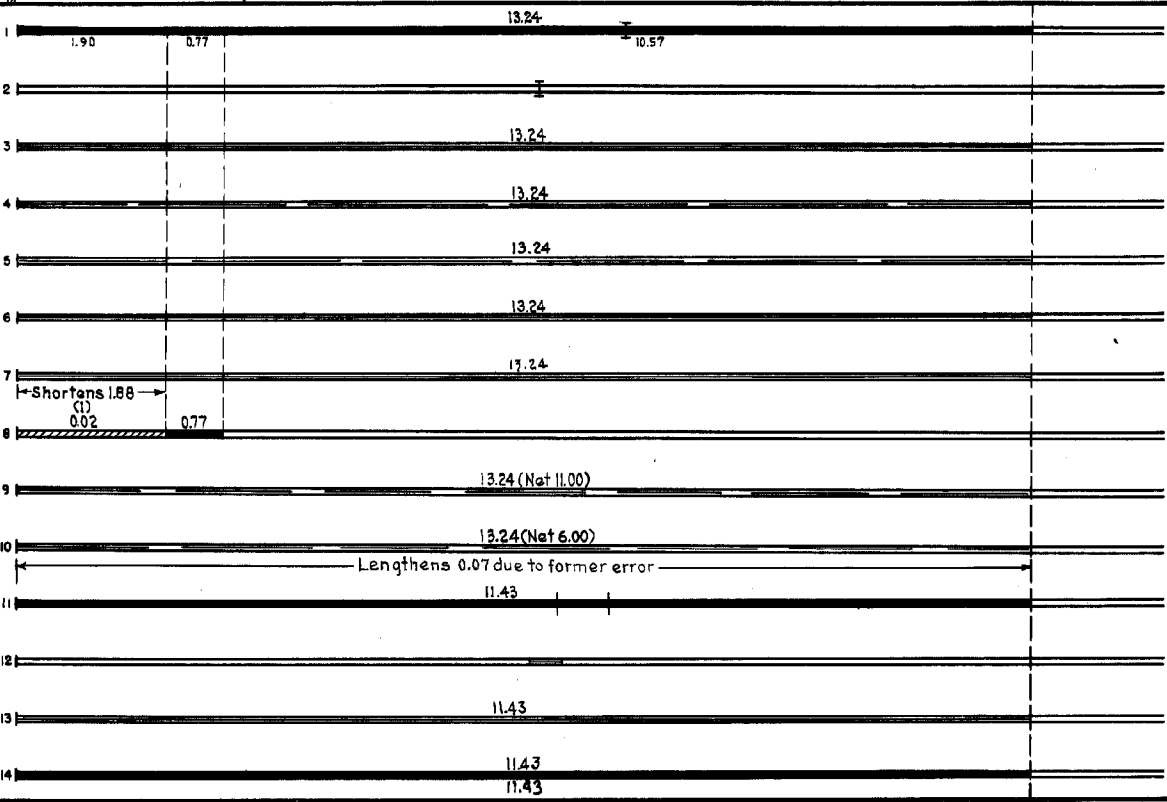

10-75

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1935	13.24	12.78	0.01	0.45	0.00	13.23	0.01	0.00	0.00
1934	1954	11.36	10.90	0.01	0.45	0.00	11.35	0.01	0.00	0.00
1954	1955	11.43	11.01	0.00	0.42	0.00	11.43	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934
(1) 0.02 Mi. not in use until Br. 6690 over Red River is built (1954) (2) Contract not final but work substantially complete

