


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3603
TRUNK HIGHWAY 6
COUNTY Koochiching
DISTRICT 1B

LIMITS: S. Co. Line - Jct. T. H. 71 in Big Falls



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
1931	6-61-23 B	Grading Gravel Br. 5030, 5029, 5044(1)	28' 24'	2"	900 C.Y./Mile.
1934	6-61-23 B	Gravel	27'	3 3/4"	900 T/Mile.
C	1942 A.F.E. 35	Culvert			36" C.M. Maint. Dept.
M	1946 A.F.E. 6	Grav. Resurfacing	24'		4852 C.Y.
M	1947 A.F.E. 6	Grav. Resurfacing	24'		1224 C.Y.
C	1948 A.F.E. 19	Bit. Surfacing Mixed Bit. (Mixed Prime)	24'	1.4"	5C-3, 17132 Gal. Agg. 692 C.Y. new 958 C.Y. from Base
M	1949 A.F.E. 6	Grav. Resurfacing (Spots)	24'		2000 C.Y.
M	1951 A.F.E. 6	Grav. Resurfacing (Spots)	24'		3011 C.Y.
C	1953 3603-02	Sand-Grav. Subbase Bit. Stab. Base Plant Mix Bit.	28' 28' 24'	6" 3'-6" 1 1/2"	
M	1956 A.F.E. 605	Light Bit. Seal	24'		RC-2, 40370 Gal. Agg. 1512 C.Y.
C	1964 Br. Crew	(Raise Portals) Br. 5029 Br. 5030			Increase Vertical Clearance to 16'
M	1970 SF	Bit. Surf. Repair	24'	1"	MC-250 tack, 125 Gal. Agg. 233 Tons
C	1974 3603-04	Bit. Overlay Gravel Shoulders	24'	1 1/2"	
C	1977 3603-07	Br. #99012	24'		TEMP. BY PASS BR FOR REPL. OF BR. 5030 30' SBS

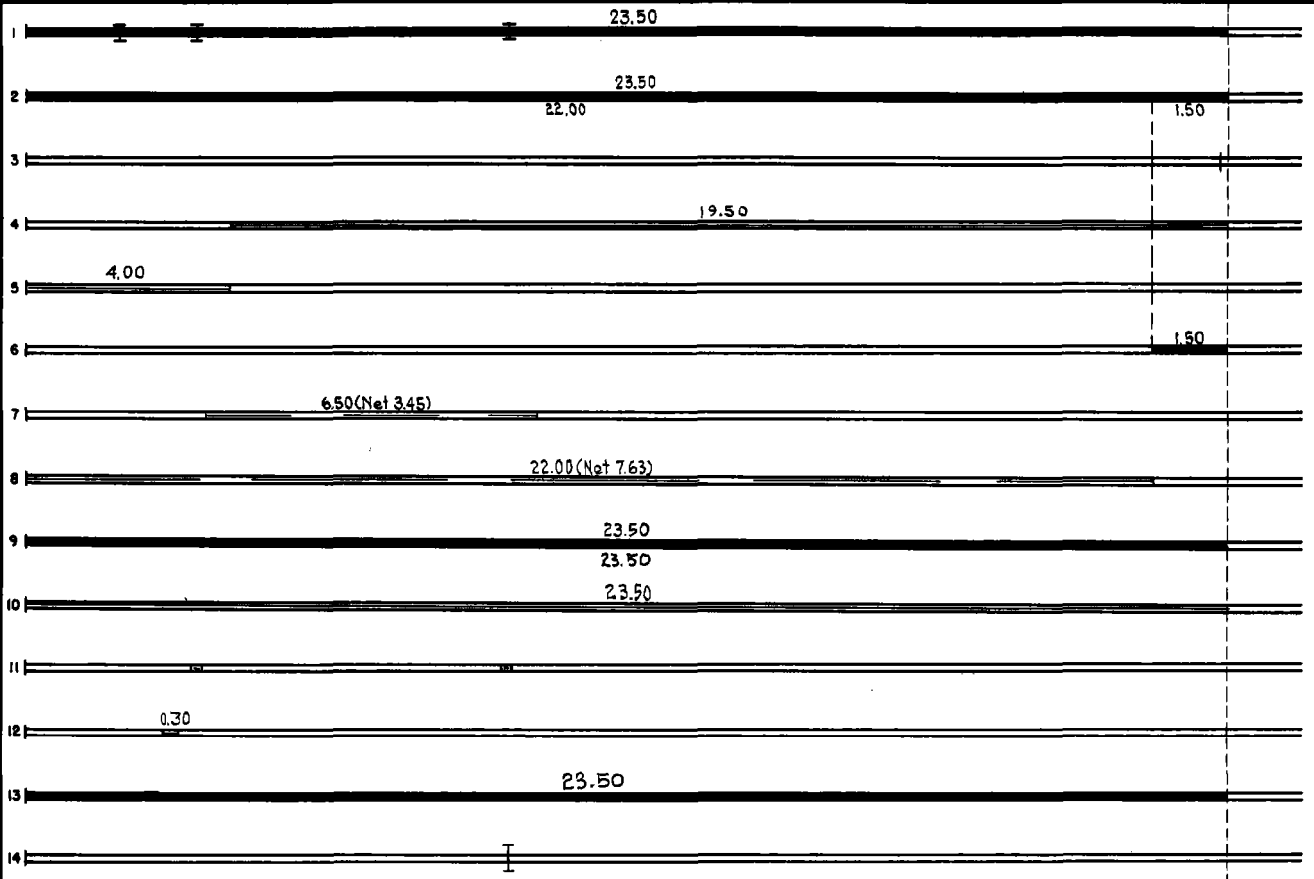

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.
1931		23.50	22.12	0.09	1.29	0.00	23.41	0.09	0.00	0.00

REMARKS: Layout is to scale as of 1931

(1) Br. # 5030, 210' x 17' (150' H.T., 2-30' B.S.) - Br. # 5029, 210' x 17' (150' H.T., 2-30' B.S.) - Br. # 5044, 30' x 23' B.S.

