


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4010  
TRUNK HIGHWAY 99  
COUNTY LeSueur  
DISTRICT 7A

LIMITS: Jct. T.H. 13 - E. Co. Line.



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
					No Record of Constr.
		Gravel	24'	4"	Added in 1934.
M 1941	A.F.E. 39	Regravelling			425 C.Y./Mile Maint. Dept.
M 1944	A.F.E. 6	Grav. Resurfacing			417 C.Y./Mile Maint. Div.
M 1947	A.F.E. 6	Grav. Resurfacing (Spots)			513 C.Y.
M 1948	A.F.E. 6	Grav. Resurfacing	28'		1416 Tons
C 1951	4010-01	Grading Gravel	32' 28'		1.0' Select Material 1200 C.Y./Mile
C 1952	4010-03	Sand-Grav Subbase Gravel Base Mixed Bit.	28' 28' 24'	6" 3" 1 1/2"	
M 1954	A.F.E. 605	Light Bit. Seal	24'		RS-2, 8521 Gal. Agg. 285 C.Y.
M 1956	A.F.E. 604	Bit. Surf. Repair	24'		MC-3, 1100 Gal. Agg. 88 Tons
M 1961		Light Bit. Seal Spot Treat Bit. Surf. Repair	25' 24'		RS-2, 6791 Gal. MC-3, 100 Gal. Agg. 225 C.Y. & 75 tons
M 1964	SF	Bit. Surf. Repair	24'		MC-3, 300 Gal. Agg. 168 Tons
M 1968	SF	Bit. Surf. Repair	24'	1/4"	Bit. Mix 144 Tons
M 1969	SF	Spot Bit. Repair	24'	3/4"	MC-250 Tack 335 Gal. Mix 192 Tons
M 1971	SF	Spot Bit. Repair	24'	1/2"	MC-250-Tack 400 Gal. Agg. 372 Ton

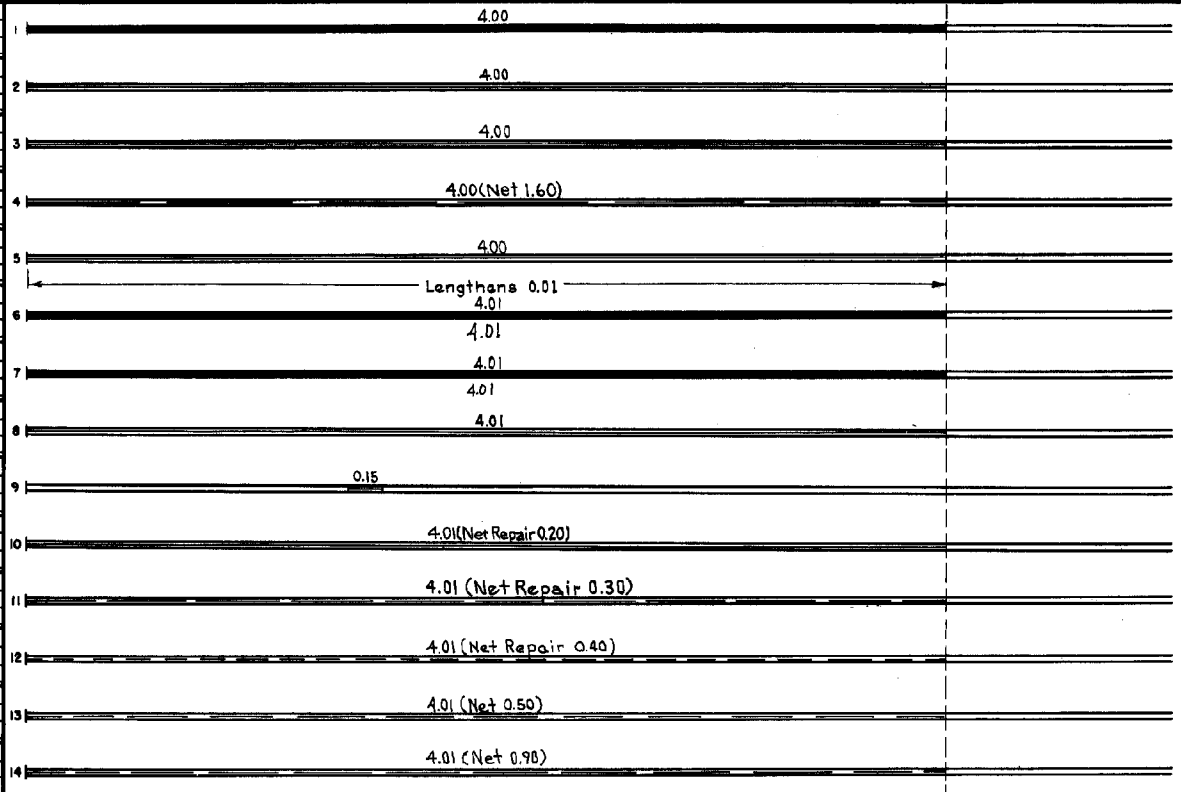

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN		
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	
1934	1950	4.00	4.00	0.00	0.00	0.00	0.00	4.00	0.00	0.00	0.00
1951		4.01	4.01	0.00	0.00	0.00	0.00	4.01	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934.

