


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 4608
TRUNK HIGHWAY 222
COUNTY Martin
DISTRICT 7B

LIMITS: Jct. T.H. 16-Meagher St. in Granada

Ref. Pt. 001+00.158 - 003+00.211



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Gravel Bridge #1925	21' 19"		No Record of Const. Added in 1949 47 Conc. Arch.
M 1950	A.F.E. 6	Grav. Resurfacing			1567 Tons
C 1950	A.F.E. 6	Bit. Surfacing			603,6229 Gal.
A.F.E. 19		Bit. Surf.-Treated	22'	3/4"	Agg. 316 C.Y.
C 1952	4608-01	Grading	36'		
		Gravel	34'	1 1/2"	1200 C.Y./Mi.
C 1954	4608-03	Bit. Stab. Base	2'50"	4"	On 8" Sand-Grav. Sub-base
(I) 4608-06		Plant Mix Bit.	2'50"	2"	
		Widen Br. 1925	30'		47 Conc. Arch
C 1956	A.F.E. B17	Bit Surfacing Approaches to Br. 1925			Bit. Mix. 246 Tons
M 1953		Light Bit. Seal	25'		RS-2K, 6481 Gal. Agg. 240 C.Y.
C -07	1973	Grading			
S4157 (I)		Bit. Surf.	24'	4 1/2"	
C 4680-22		Grade Base	26'	1 1/2"	
I 090-2 (40)		Plant Mix Bit. Surf.	24'	3"	
104		Plant Mix Bit. Shld.	10'		
M 1976	SF	Seal Coat			FA-2 Mod. AC 800
M 1985	SF	Seal Bit Overlay	44'	1 1/2"	Sp. 2331 557 Tons (A)
			30'	1 1/2"	Sp. 2331 20 Tons (B)
M 1988	SF	Bit. Sealing			
M 1990	SF	Bit. Overlay	24'	1 1/2"	Spec. 2331
M 1991	SF	Bit. Overlay	24'	1 1/2"	

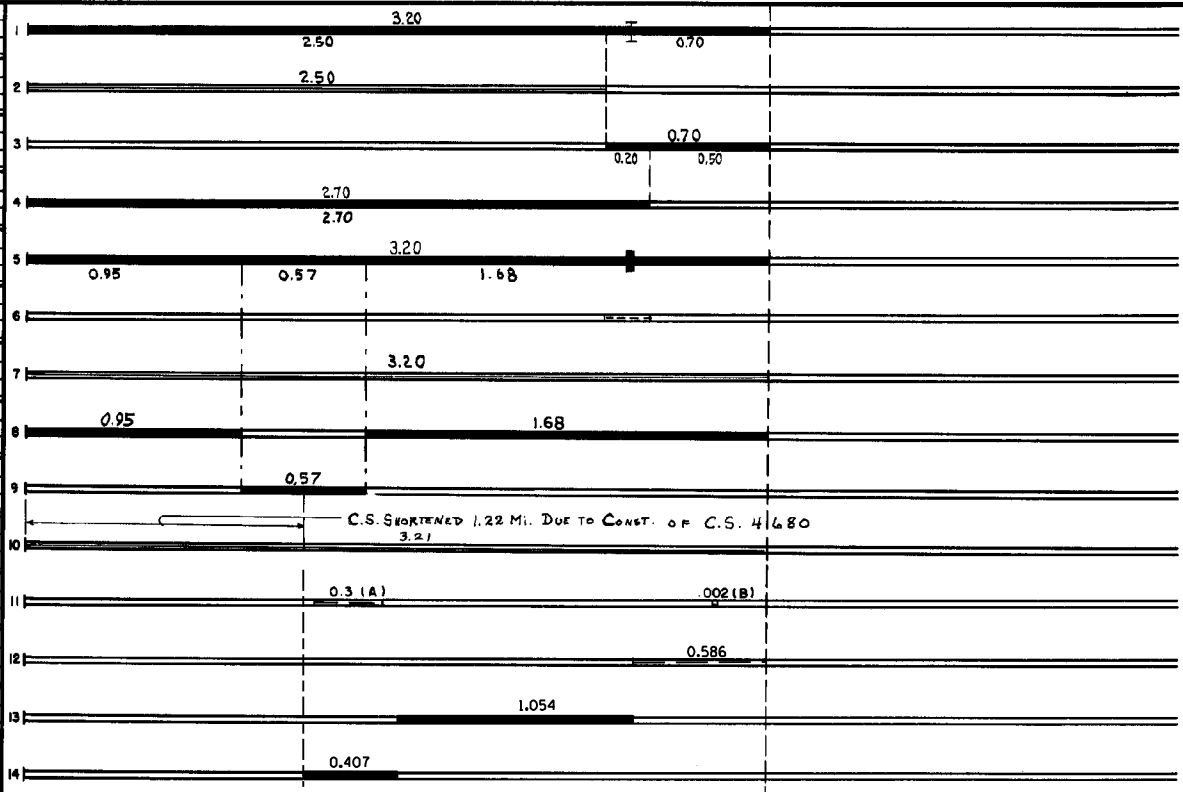

YEARS FROM TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949	3.20	2.45	0.00	0.74	0.01	3.19	0.01	0.00	0.00

REMARKS: Layout is to scale as of 1949
(1) Contract not final but work substantially complete.
(2) For Bridge Detail See C.S. 4680

