


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4815
TRUNK HIGHWAY 47
COUNTY Mille Lacs
DISTRICT 38

LIMITS: E. Co. Line - Jct. T.H. 27 in Isle



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o	REMARKS
		TYPE	WIDTH	THICKNESS		
1942	4815-01	Grading Gravel	36'			1000 C.Y./Mi.
1942	A.F.E. 7	Seeding				Seed supplied by R.S.D. (S.P. 4815-04) Maint. Dept.
1942	A.F.E. 27	Culv. Inst.				Maint. Dept.
1947	1946 & A.F.E. 27 1946 & A.F.E. 6	Spot Grav. Lifts Grav. Resurfacing (Spots)	32'			559 C.Y.
1948	A.F.E. 29	Bit Surfacing Mixed Bit (Mixed Prime)	26'	1 1/2"		SG-3, 22254 Gal. Agg. 420 C.Y.
1949	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'			SC-4, 2588 Gal. Agg. 132 C.Y.
1950	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'			SC-3, 12783 Gal. Agg. 820 C.Y.
1951	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'			SG-4, 6242 Gal. Agg. 392 C.Y.
1952	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'			SC-4, 2822 Gal. Agg. 259 Tons
1953	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'			SC-4, 4086 Gal. Agg. 330 Tons
1954	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'			SC-4, 9811 Gal. Agg. 896 Tons
1955	4815-06	Gravel Base Mixed Bit.	34' 26'	6" 2"		
1957	A.F.E. 605	Light Bit. Seal	25'			RC-2, 4768 Gal. Agg. 180 C.Y.
1958	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'			SC-4, 1575 Gal. Agg. 126 Tons

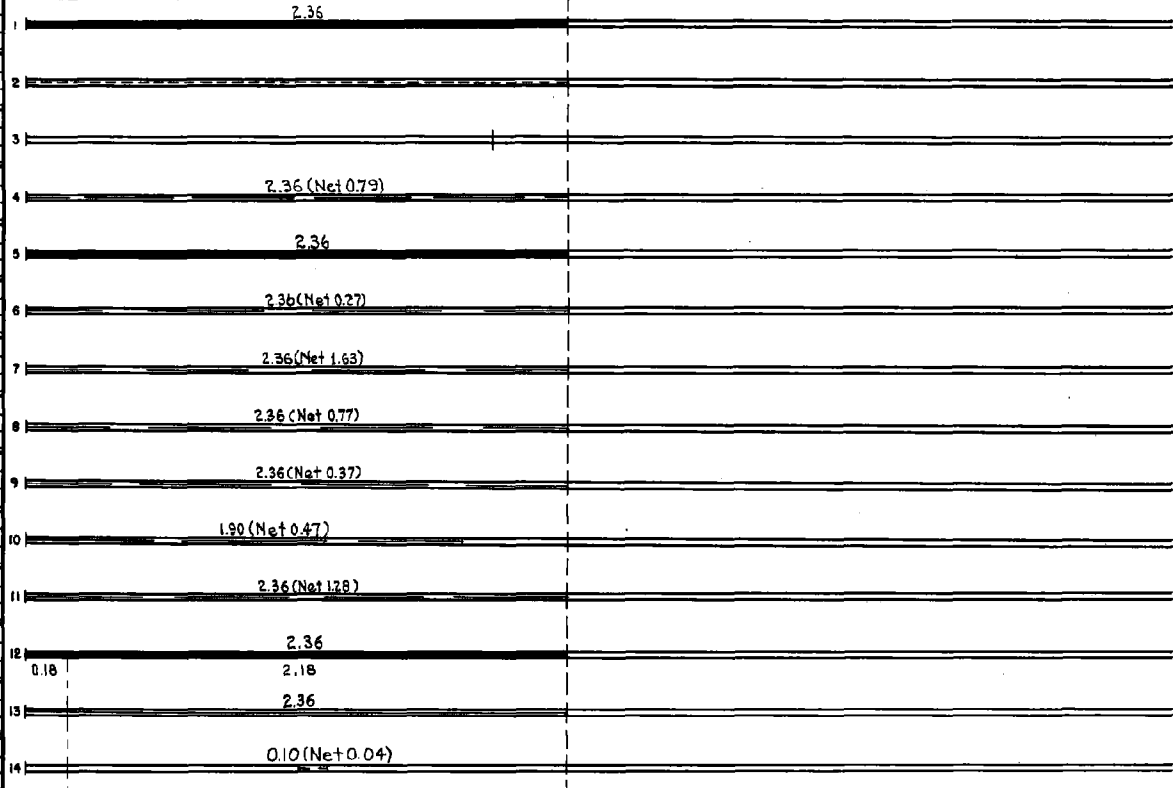

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.
1942	2.36	1.83	0.00	0.53	0.00	2.36	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1942

