


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6608
TRUNK HIGHWAY 3
COUNTY Rice
DISTRICT 6B

LIMITS: S.Co.Line-S.Jct.T.H.60 in Faribault



| YEAR BUILT | PROJECT N° | DESCRIPTION | | | CODE N° |
|------------|---|---|-------------------|-----------|--|
| | | TYPE | WIDTH | THICKNESS | |
| 1924 | 65-1-40 | Grading Br. 4006 Br. ? (1) | 32' 21' | | |
| 1925 | 65-1-40 | Concrete | 18' | 8-7-8 | |
| 1925 | 65-1-46 | Grading Concrete | 20' 18' | | |
| 1930 | 65-1-46 | Concrete | V.M. | | Widening & Curb. at Jct. T. H. 60. |
| 1935 | 65-1-40 | Br. 5336 | 28' | | B.S.-V.P. |
| C 1956 | A.F.E. 617 | Bit. Surfacing Plant Mix Bit. | 18' | 8" | MC2&RC2 3226 Gal. Plant Mix 6443 Tons |
| C 1958 | Built in connection with work on C.S. 6680, S. 6660-02 & 04 | Grading Bit. Surf. Base Plant Mix Bit. | 30' 30' 24' | | Br. 8912 (C1212 D) on 6" Sand-Grav. Subbase |
| M 1960 | | Light Bit Seal | 25' | | RS-1, 8615 Gal. Agg. 304 Tons |
| C 1964 | 6608-06 | Grading Sub-base Gravel & Bit Base Plant Mix Bit. | | | Rt & Lt of Concrete in place |

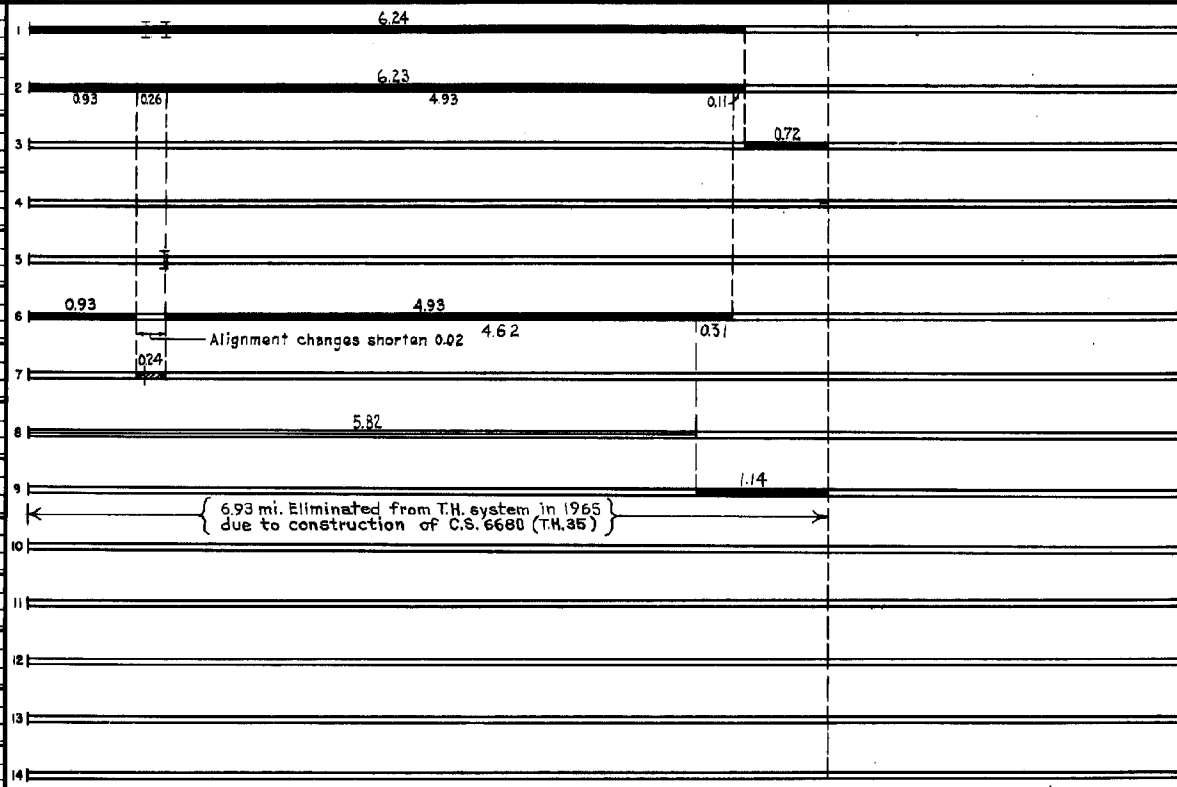

| YEARS | | TOTAL MILES | UNINCORPORATED | | INCORPORATED | | RURAL | | URBAN | |
|-------|------|-------------|----------------|---------|--------------|---------|-----------|---------|-----------|---------|
| FROM | TO | | RDWY. MI. | BR. MI. | RDWY. MI. | BR. MI. | RDWY. MI. | BR. MI. | RDWY. MI. | BR. MI. |
| 1924 | 1924 | 6.96 | 5.84 | 0.01 | 1.11 | 0.00 | 5.84 | 0.01 | 1.11 | 0.00 |
| 1925 | 1957 | 6.95 | 5.83 | 0.01 | 1.11 | 0.00 | 5.83 | 0.01 | 1.11 | 0.00 |
| 1958 | 1964 | 6.93 | 5.82 | 0.00 | 1.11 | 0.00 | 5.82 | 0.00 | 1.11 | 0.00 |
| 1965 | | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 |

REMARKS: Layout to scale as of 1925
(1) No record of constr. of underpass.
