


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6807
TRUNK HIGHWAY 88
COUNTY Roseau
DISTRICT 28

LIMITS: W. Jct. T.H. 11 at Fox - International Boundary



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N° DIST.
		TYPE	WIDTH	THICKNESS	
		Gravel	26'		No Record of Const. Added in 1949
		Bridge 1281	18'		146 L.F.
M	1950 A.F.E. 6	Gravel Resurfacing			6600 Tons
M	1953 A.F.E. 606	Grav. Resurfacing			3332 Tons
C	1953 6807-03	Grading	28'		
		Gravel Base	28' 9"		2053
		Mixed Bit.	24' 1/2"		
C	1954 6807-02	Br. 6781	24'		50'-60'-50' L.T. (Cold spans used)
M	1955 A.F.E. 606	Grav. Resurfacing			2493 Tons
C	1955 6807-05	Grading	30'		
		Gravel Base	30' 3"		On 9" Sand-Gr. Sub-base
		Mixed Bit.	24' 1/2"		2354
C	1956 A.F.E. 817	Guard Rail			168 L.F.
M	1957 A.F.E. 605	Light Bit. Seal			RC-2, 1367 1/2 Gal. Agg. 455 C.Y.
C	6807-07	Grading	32'		457
	1958 6808-08	Stab. Grav. Base	32' 9"-12"		1058
		Mixed Bit.	26' 1/2"		
M	1962	Bit. Surf. Repair	24'		MC 2,50,004 Gal. for Repair & 85,04 for Tack
C	1972 -11	Bit. Resurfacing	24' 11/2"		572
		Agg. Shldrs.			
		Turf Lanes			
C	1975 6800-01	PLATE BEAM GUARD RAIL AT BR. 6781			206 LIN. FT. 1175
C	1984 6807-13	Grading, Base	44' 6"		
		Bit. Surface	24' 3/2"		
		Br. 68005			Repl. Br. 6781

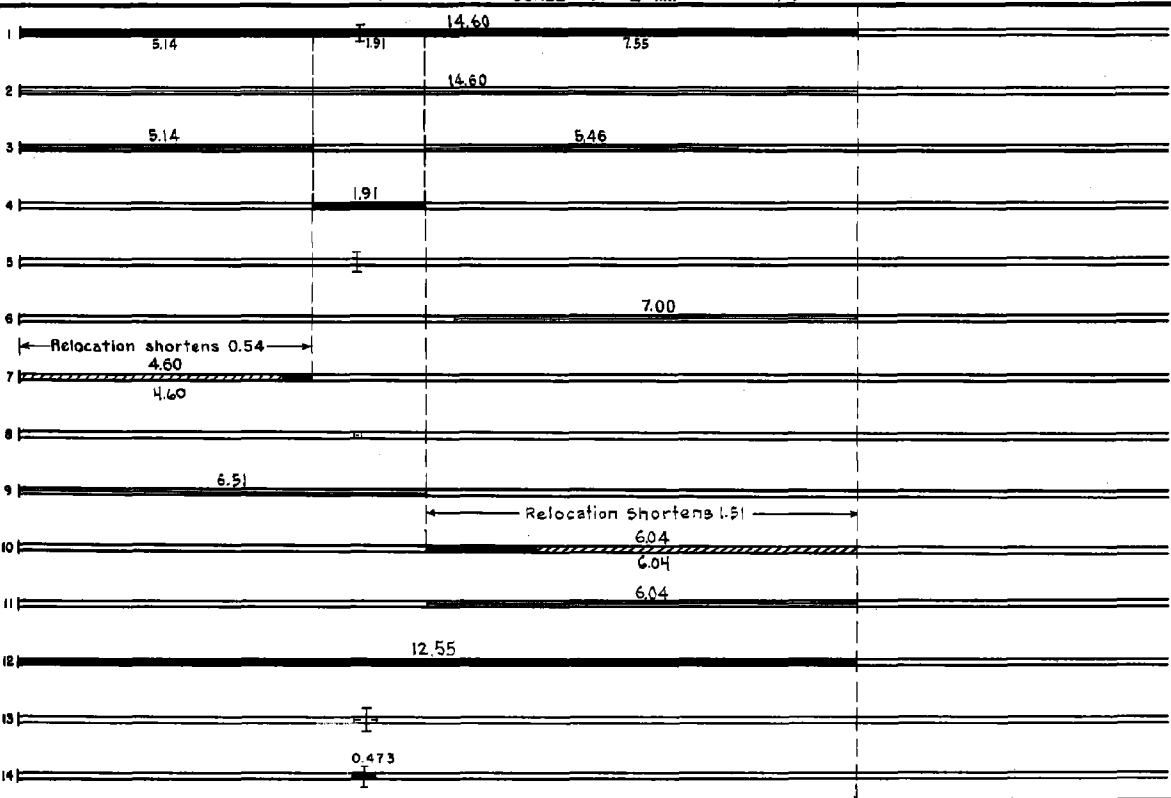

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949	1954	4.60	4.57	0.03	0.00	0.00	4.57	0.03	0.00	0.00
1955	1957	4.06	4.03	0.03	0.00	0.00	4.03	0.03	0.00	0.00
1958		12.55	12.52	0.03	0.00	0.00	12.52	0.03	0.00	0.00

REMARKS: Layout is to scale as of 1949
(1) Contract not final but work substantially complete.

475

